



JAN - FEB - MAR
Q1/2011

Legend

- Gymnasium & Pool Phase II Construction Begins (not shown)
- Solar Energy Project and Parking Lot D Construction Begins
- Parking Lot A Improvements, Student Services Canopy Construction Begins
- Library & Academic Resource Center Construction Ongoing
- Family Resource Center Construction Ongoing

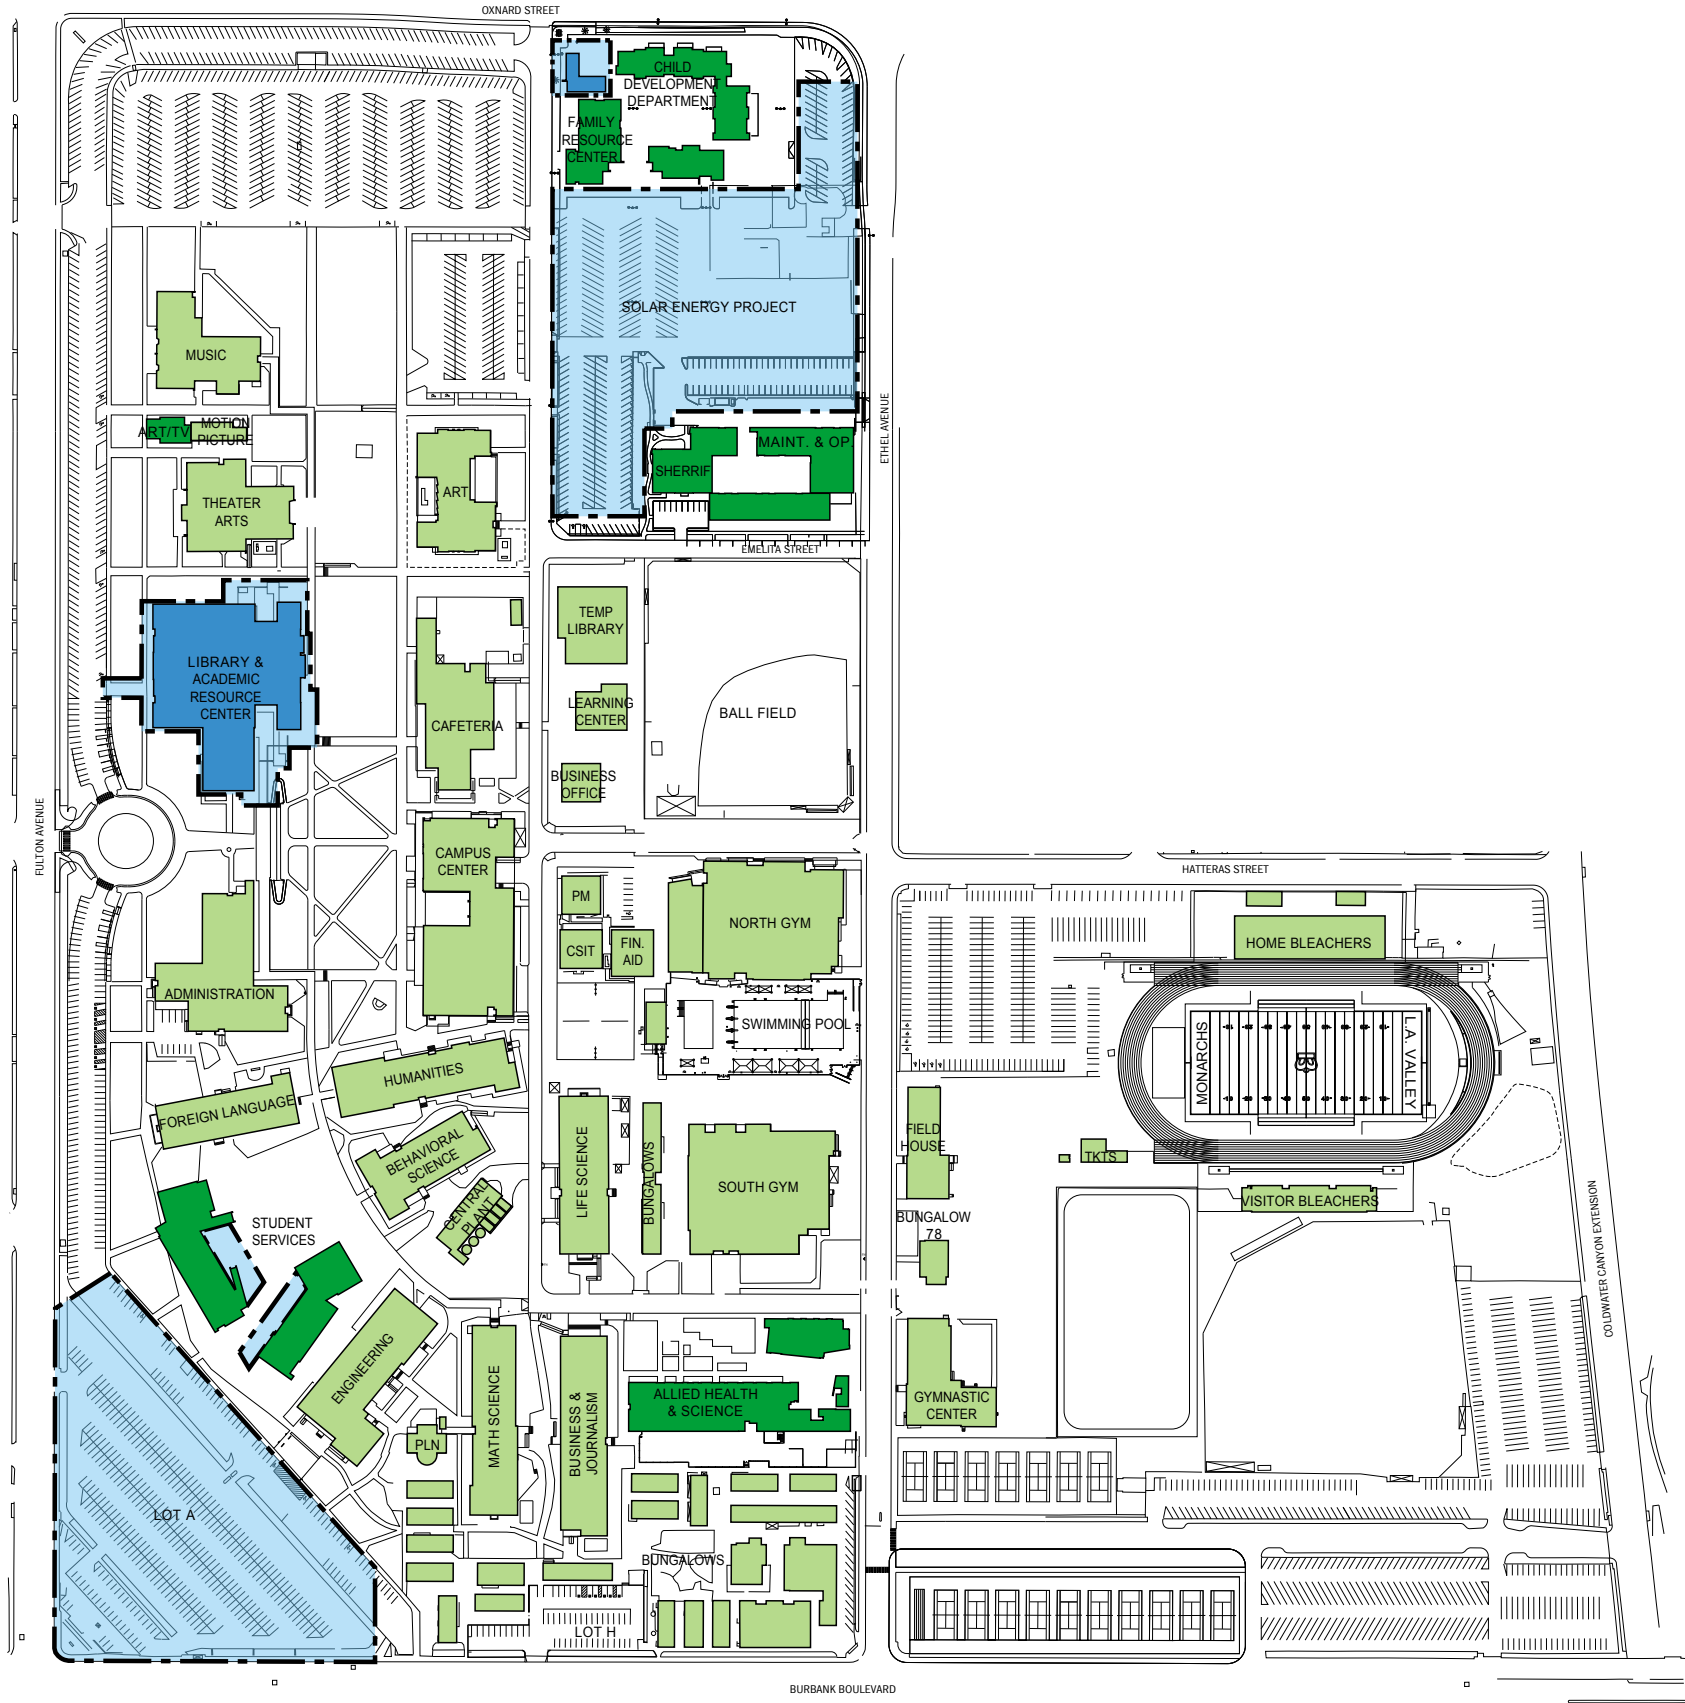


- Existing Building
- New Building
- Area Under Construction
- Building To Be Demolished Or Relocated




APR - MAY - JUN
Q2/2011

Legend

- Building Retrofit Begins
- Library & Academic Resource Center Construction Ongoing
- Gymnasium & Pool Phase II Construction Ongoing (not shown)
- Solar Energy Project and Parking Lot D Construction Ongoing
- Parking Lot A Improvements, Student Services Canopy Construction Ongoing
- Family Resource Center Construction Completed

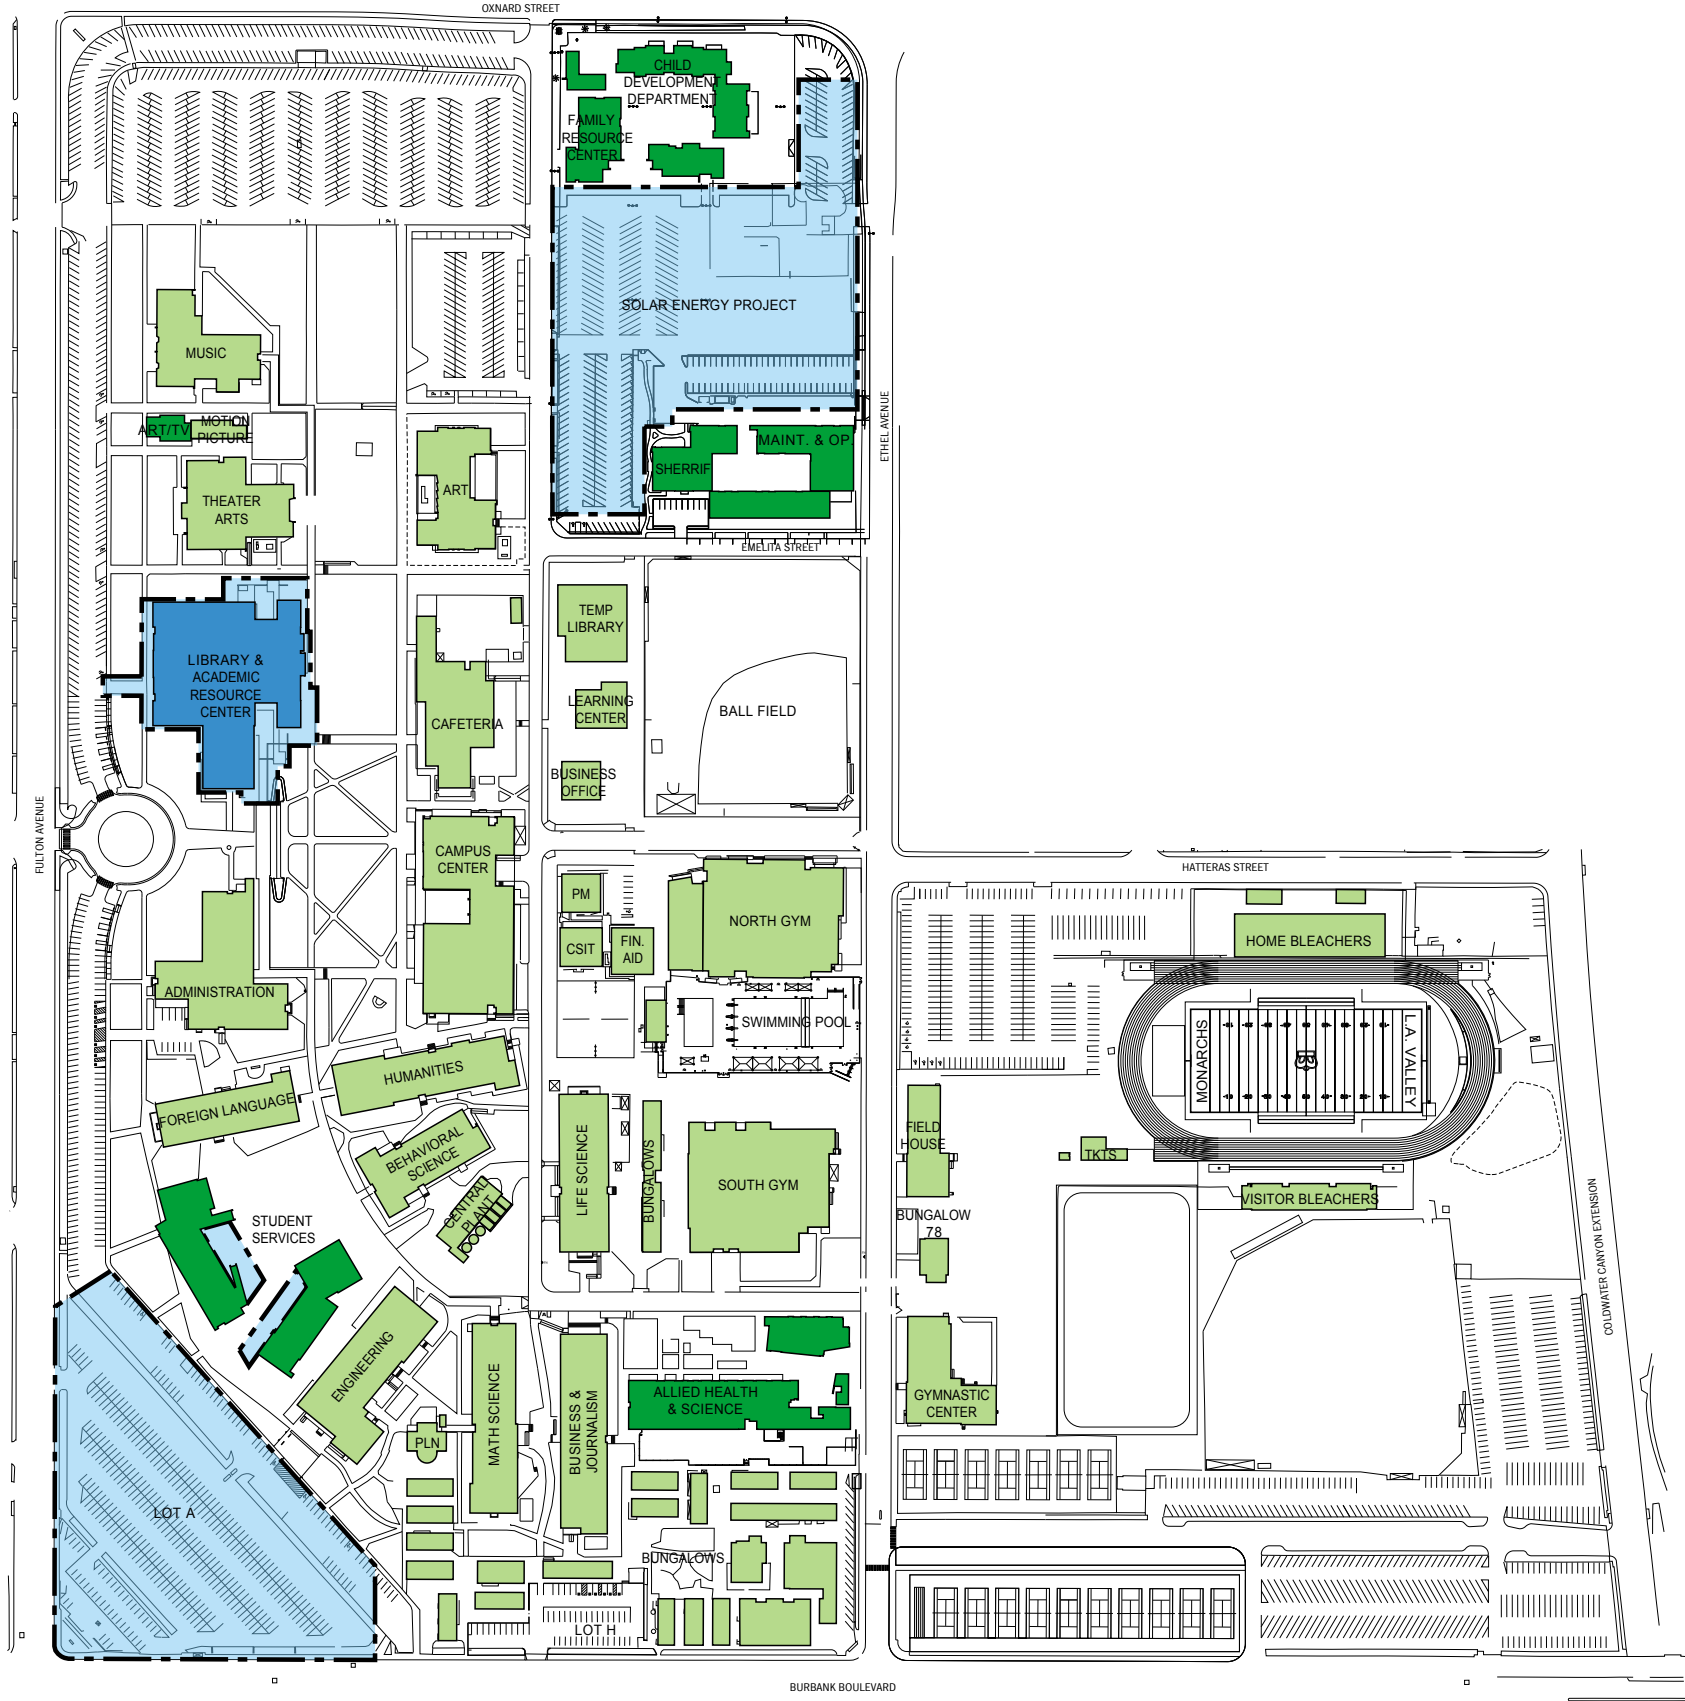


- Existing Building
- New Building
- Area Under Construction
- Building To Be Demolished Or Relocated




JUL - AUG - SEP
Q3/2011

Legend

- IT Phase 2 Construction Begins (not shown)
- Building Retrofit Ongoing
- Gymnasium & Pool Phase II Construction Ongoing (not shown)
- Solar Energy Project and Parking Lot D Construction Ongoing
- Parking Lot A Improvements, Student Services Canopy Construction Ongoing
- Library & Academic Resource Center Construction Completed

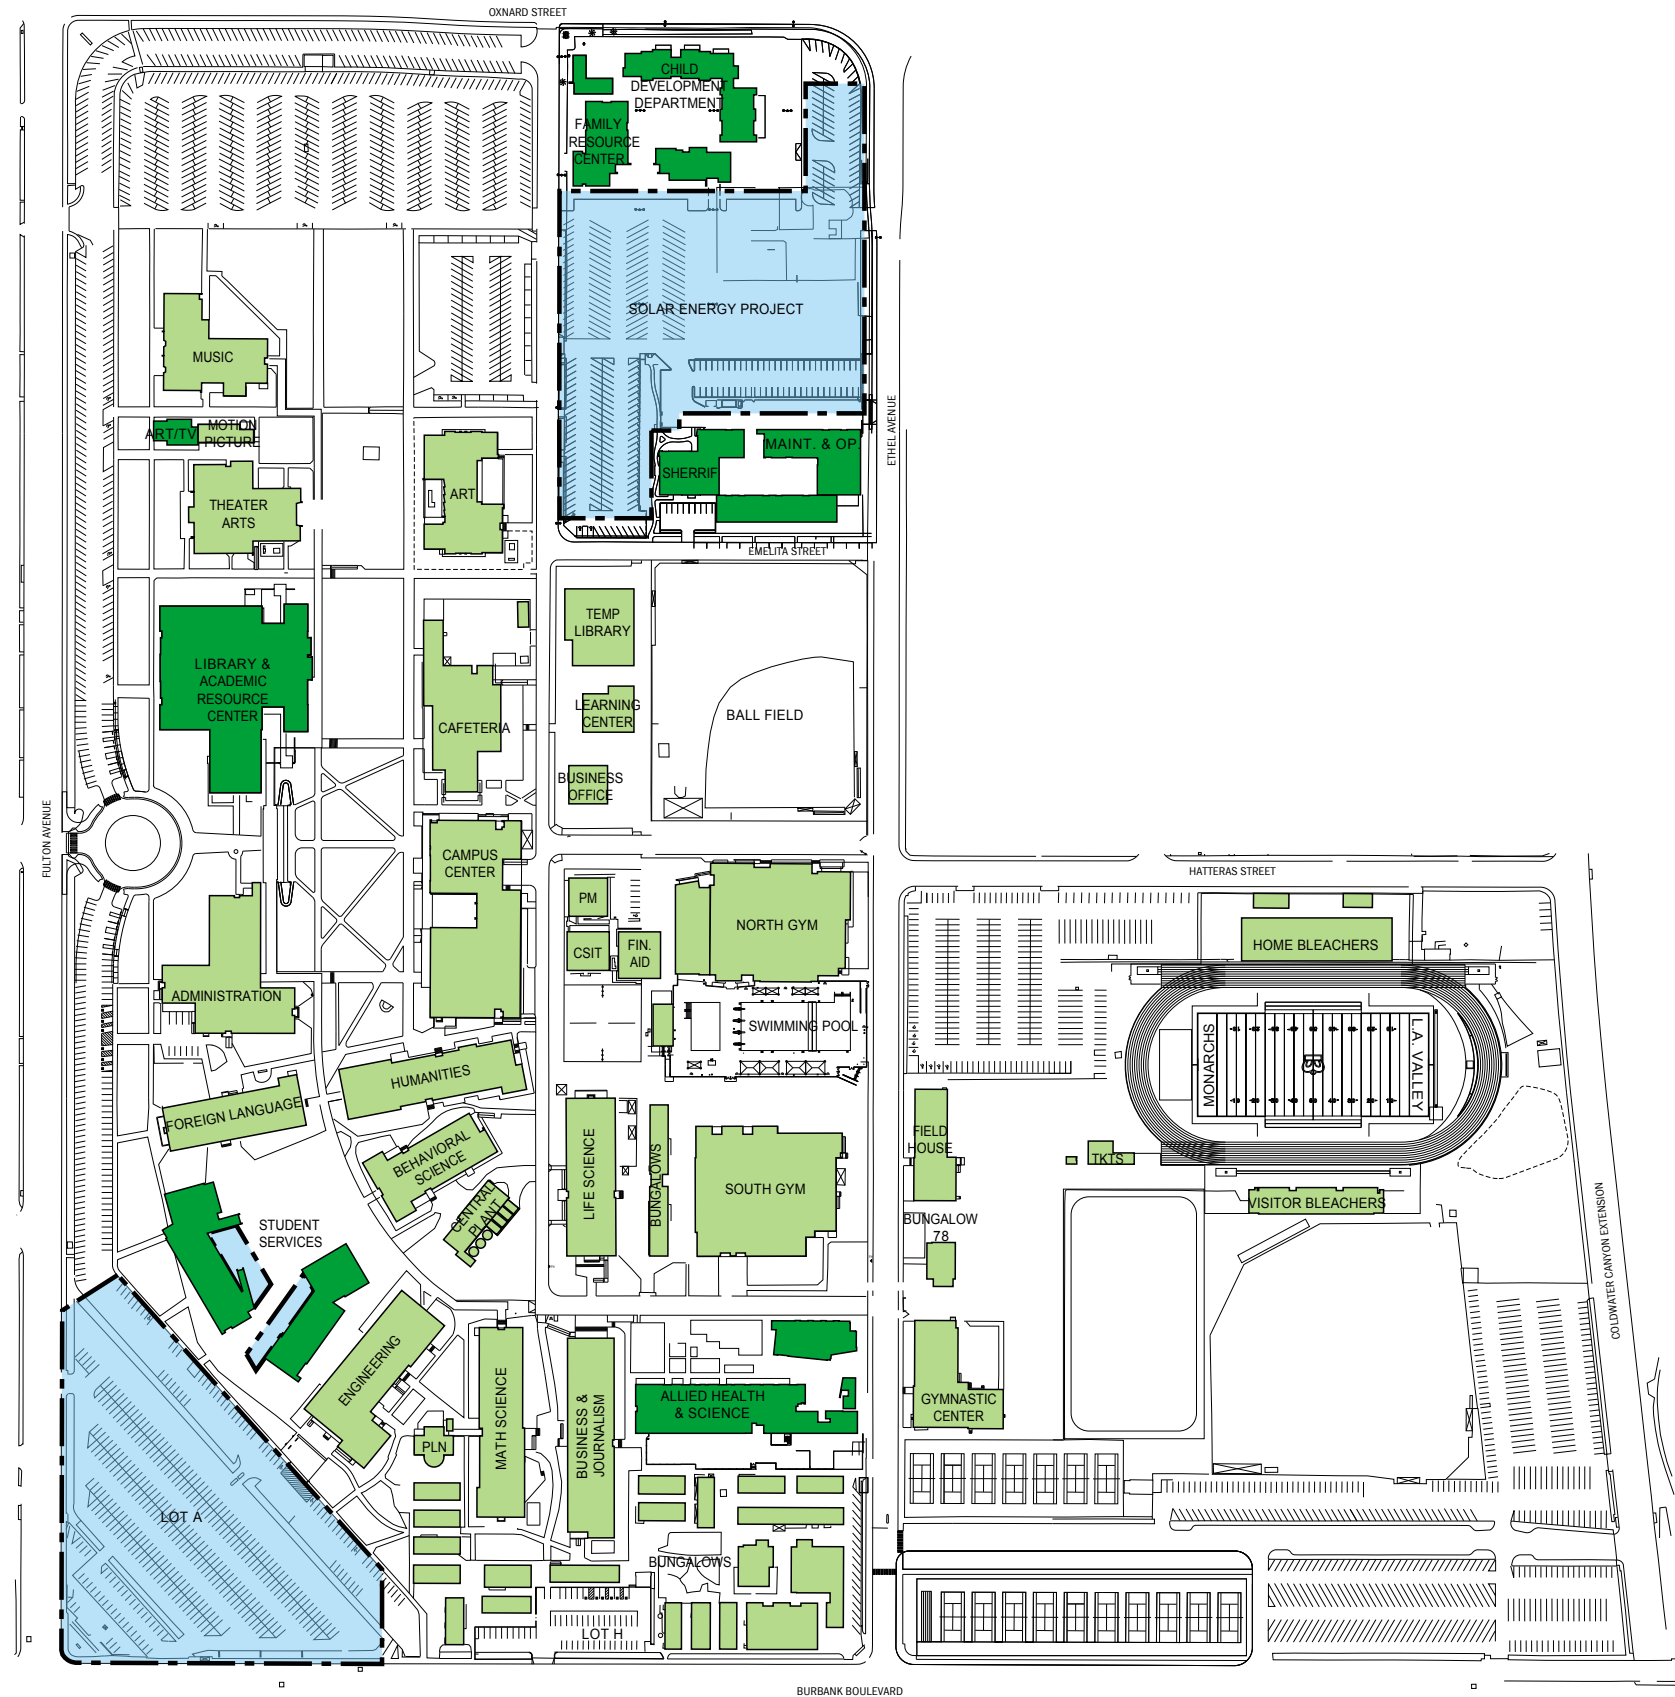


-  Existing Building
 -  New Building
 -  Area Under Construction
 -  Building To Be Demolished Or Relocated




OCT - NOV - DEC
Q4/2011

Legend

- Athletic Field Construction Begins
- Athletic Training Facility Construction Begins
- Gymnasium & Pool Phase II Construction Ongoing (not shown)
- IT Phase 2 Construction Ongoing (not shown)
- Building Retrofit Completed
- Solar Energy Project and Parking Lot D Construction Completed
- Parking Lot A Improvements, Student Services Canopy Construction Completed

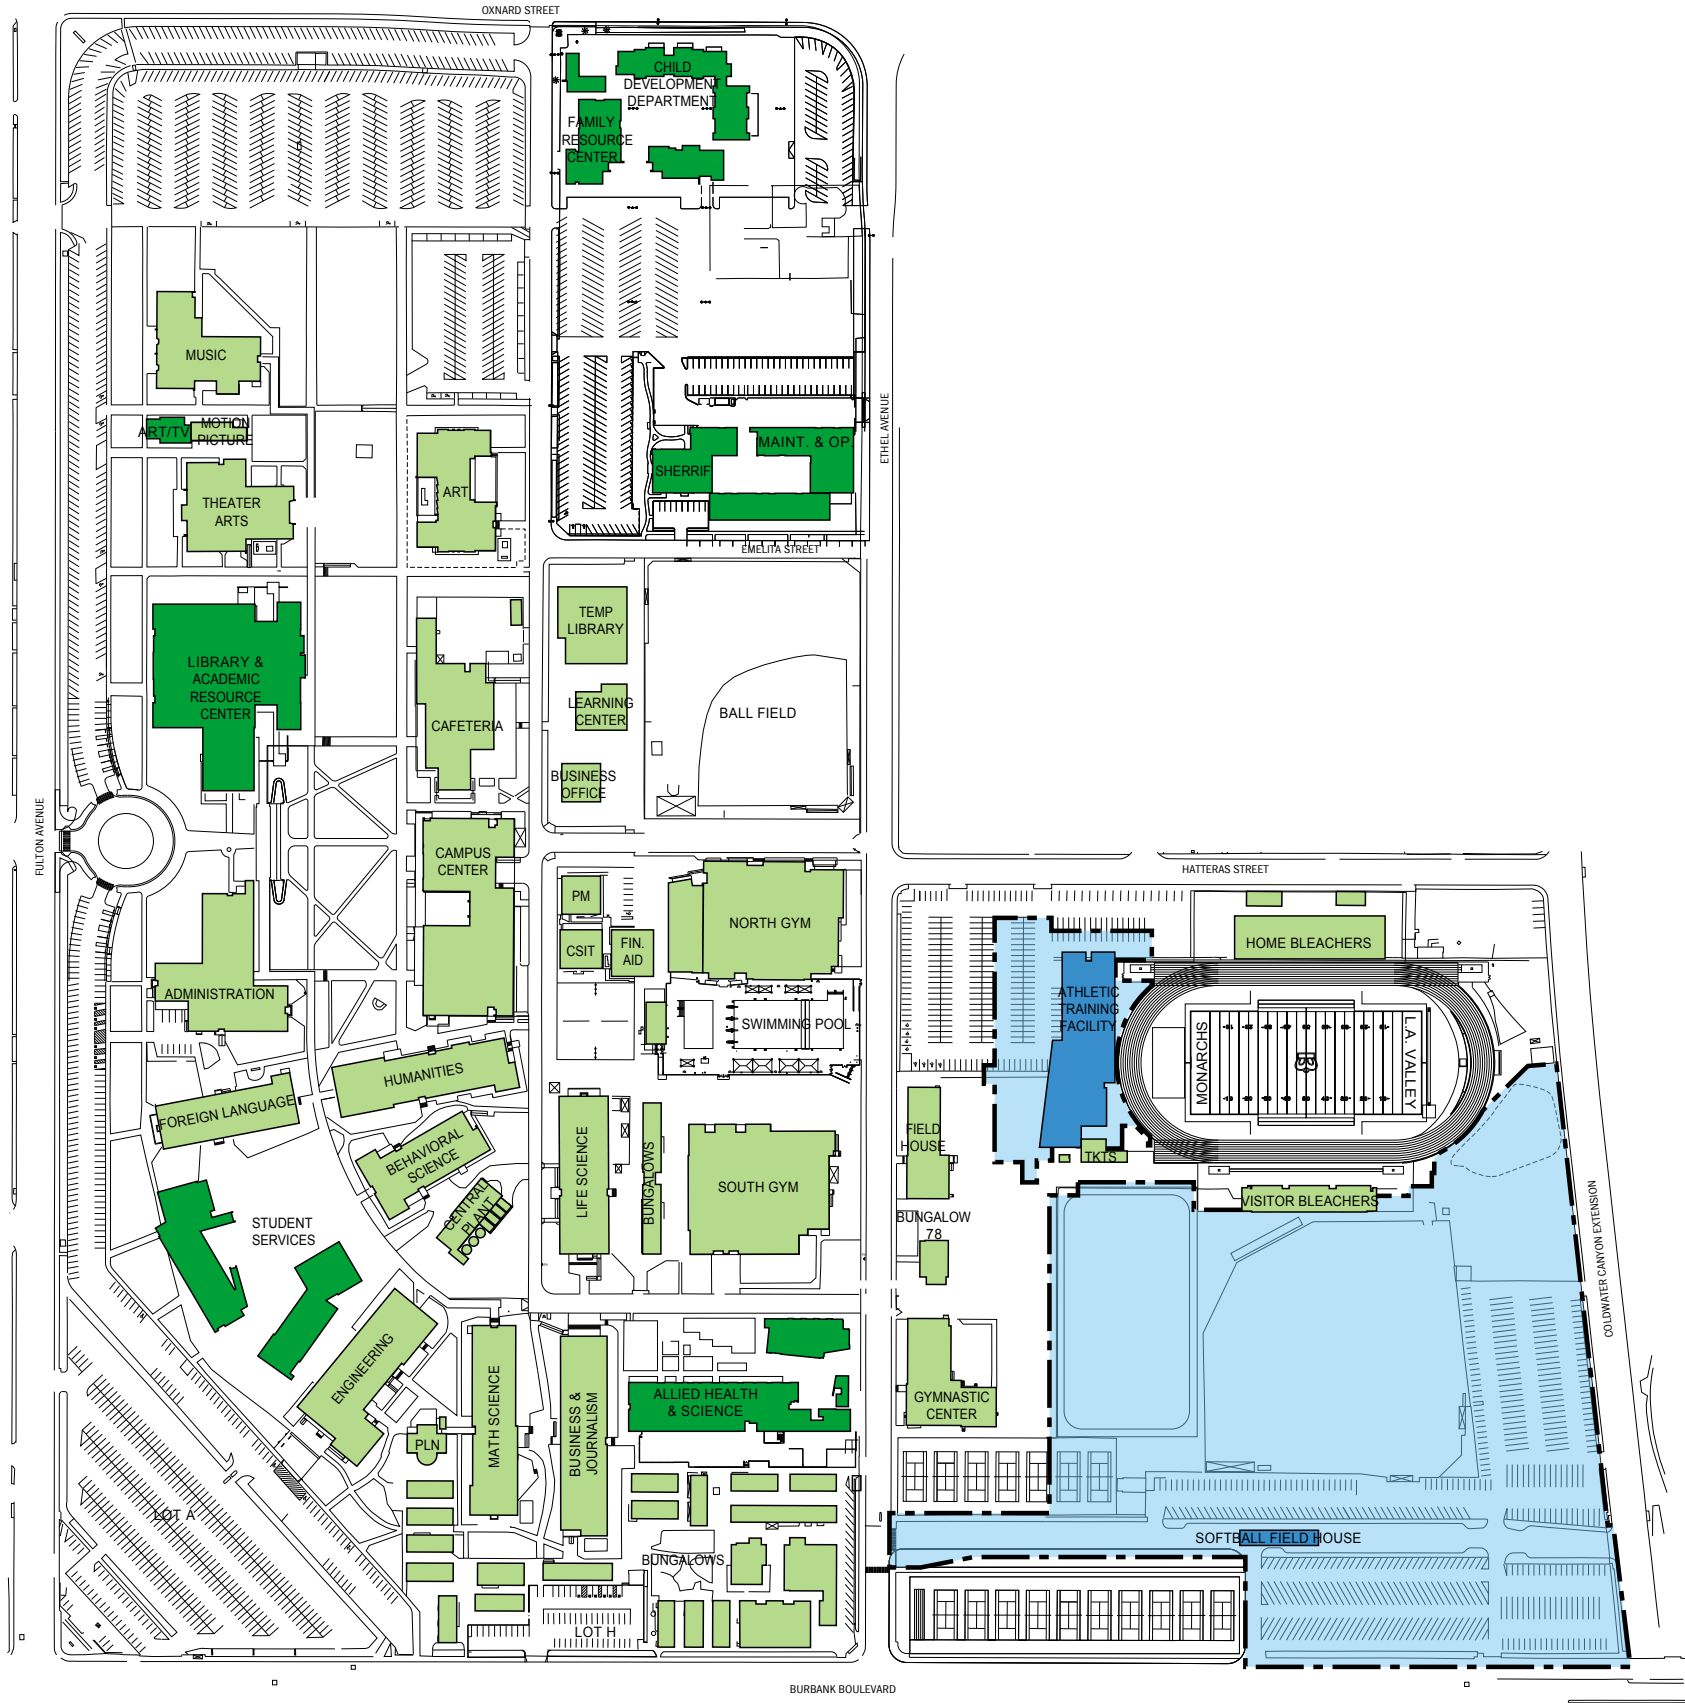

- Existing Building
- New Building
- Area Under Construction
- Building To Be Demolished Or Relocated





JAN - FEB - MAR
Q1/2012

Legend

- Emergency Lighting, Fire Alarm, & Security Systems Construction Begins (not shown)
- Ball Field Demo Begins
- West Hatteras Street Re-Striping (not shown)
- Omega Data Center Construction Begins
- Media & Performing Arts Center Construction Begins
- Athletic Field Construction Ongoing
- Athletic Training Facility Construction Ongoing
- IT Phase 2 Construction Ongoing (not shown)
- Gymnasium & Pool Phase II Construction Completed (not shown)


- Existing Building
- New Building
- Area Under Construction
- Building To Be Demolished Or Relocated

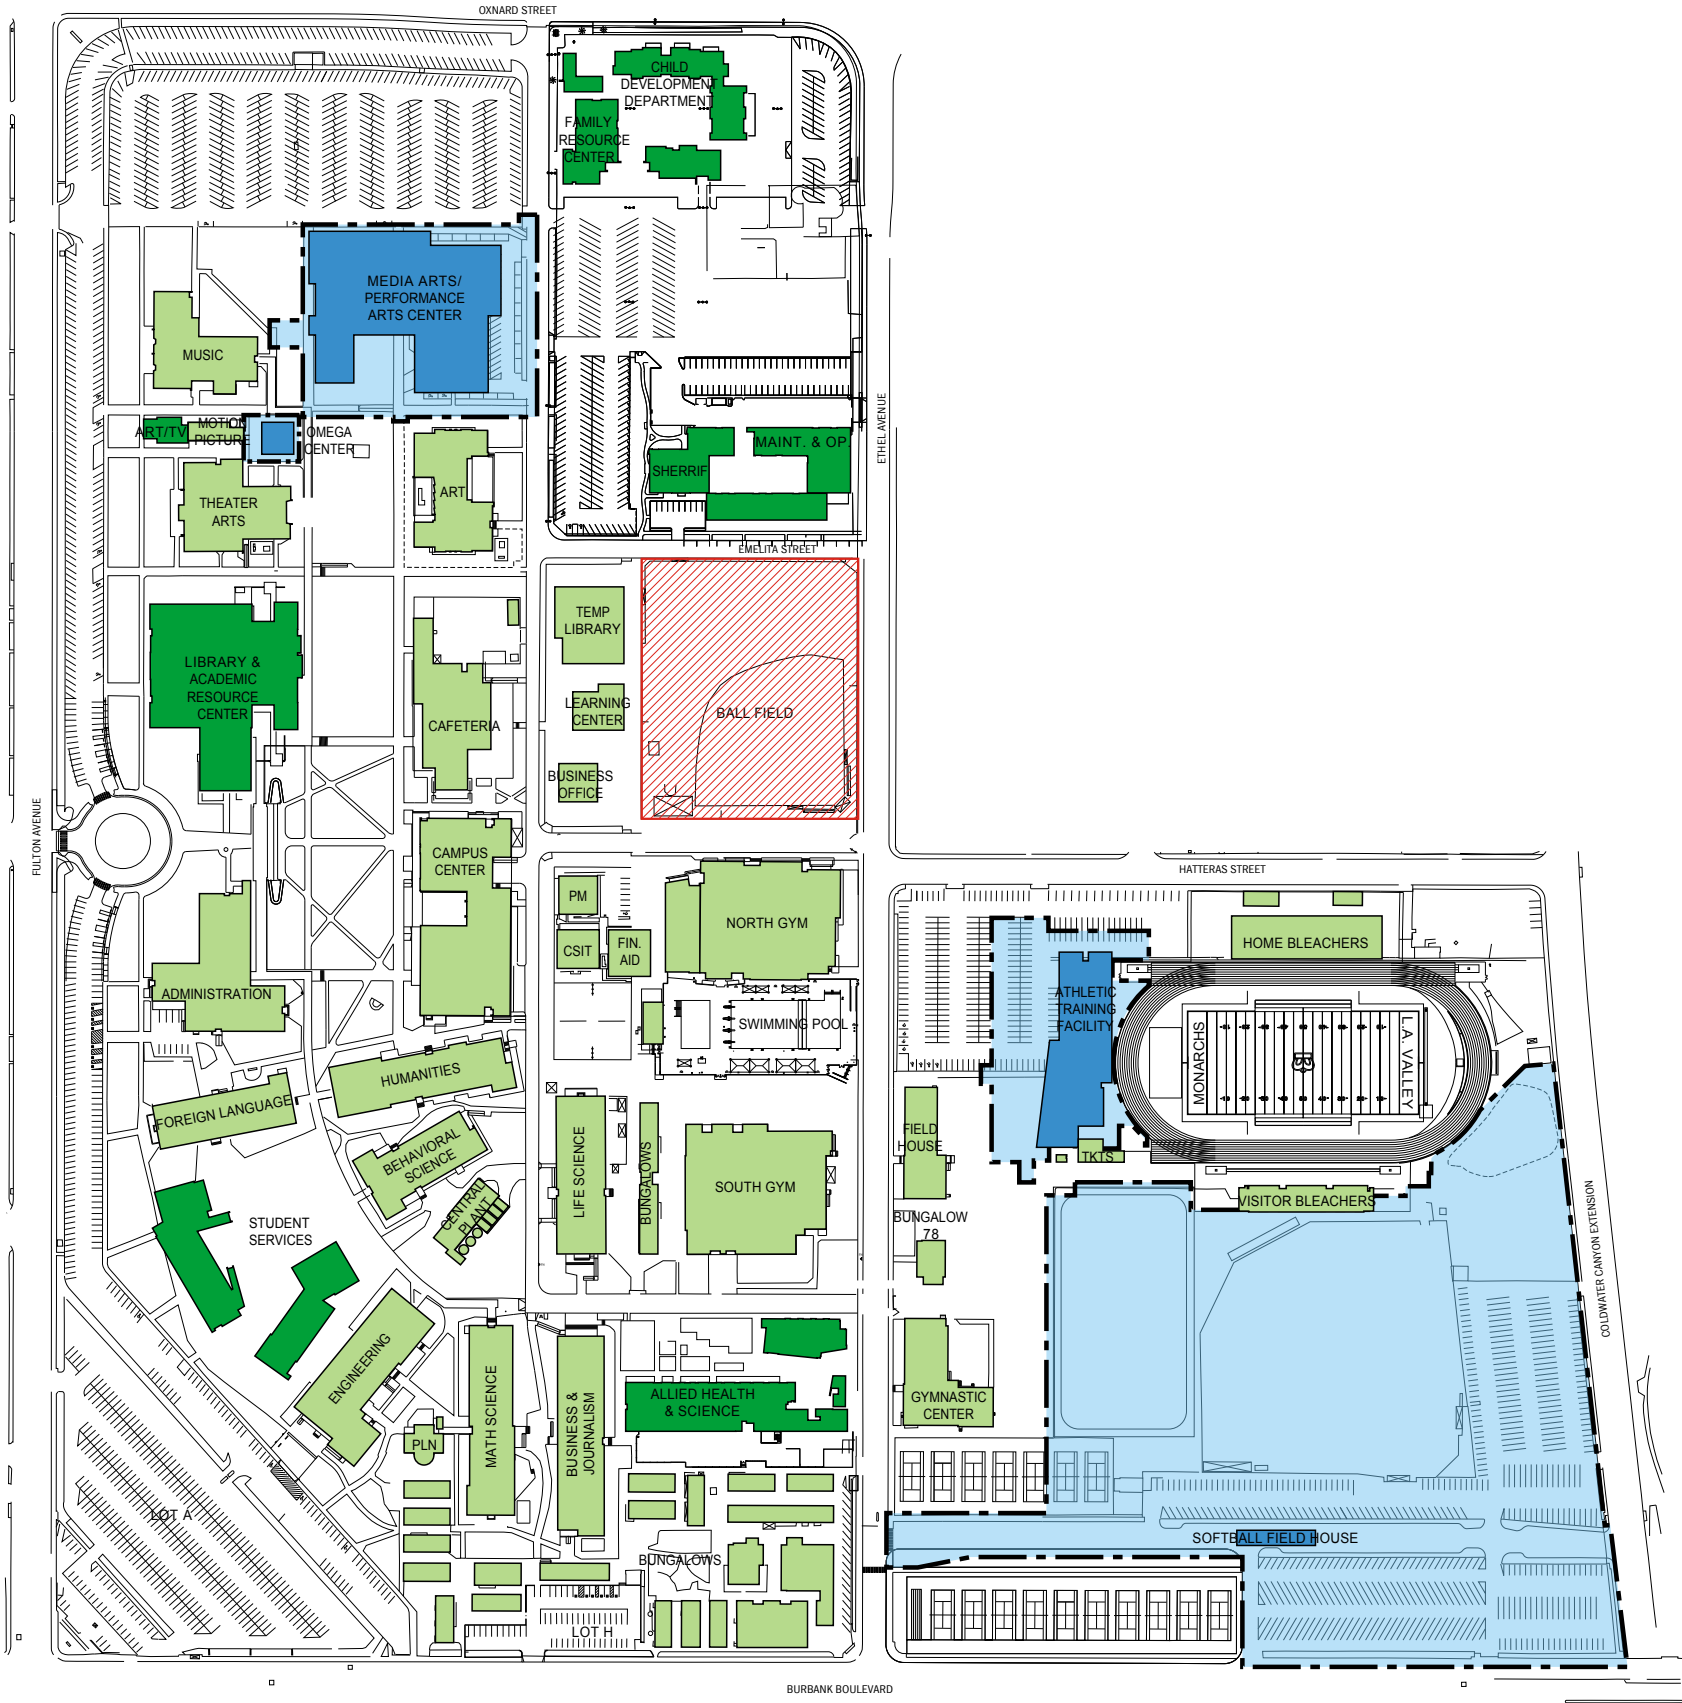

Q2/2012

- Parking Structure Construction Begins

-  Existing Building
 -  New Building
 -  Area Under Construction
 -  Building To Be Demolished Or Relocated



JUL - AUG - SEP
Q3/2012

Legend



- Widen Emilita Street
- Demo Cafeteria, Temp Library Begins
- Multi-Purpose Community Services Center Construction Begins
- Parking Structure Construction Ongoing
- Swing Space Improvements Construction Ongoing (not shown)
- Omega Data Center Construction Ongoing
- Media Arts/Performance Arts Center Construction Ongoing
- Central Plant Expansion Construction Ongoing (not shown)
- Athletic Training Facility Construction Ongoing
- Emergency Lighting, Fire Alarm, & Security Systems Construction Completed (not shown)

Existing Building

New Building

Area Under Construction

Building To Be Demolished Or Relocated

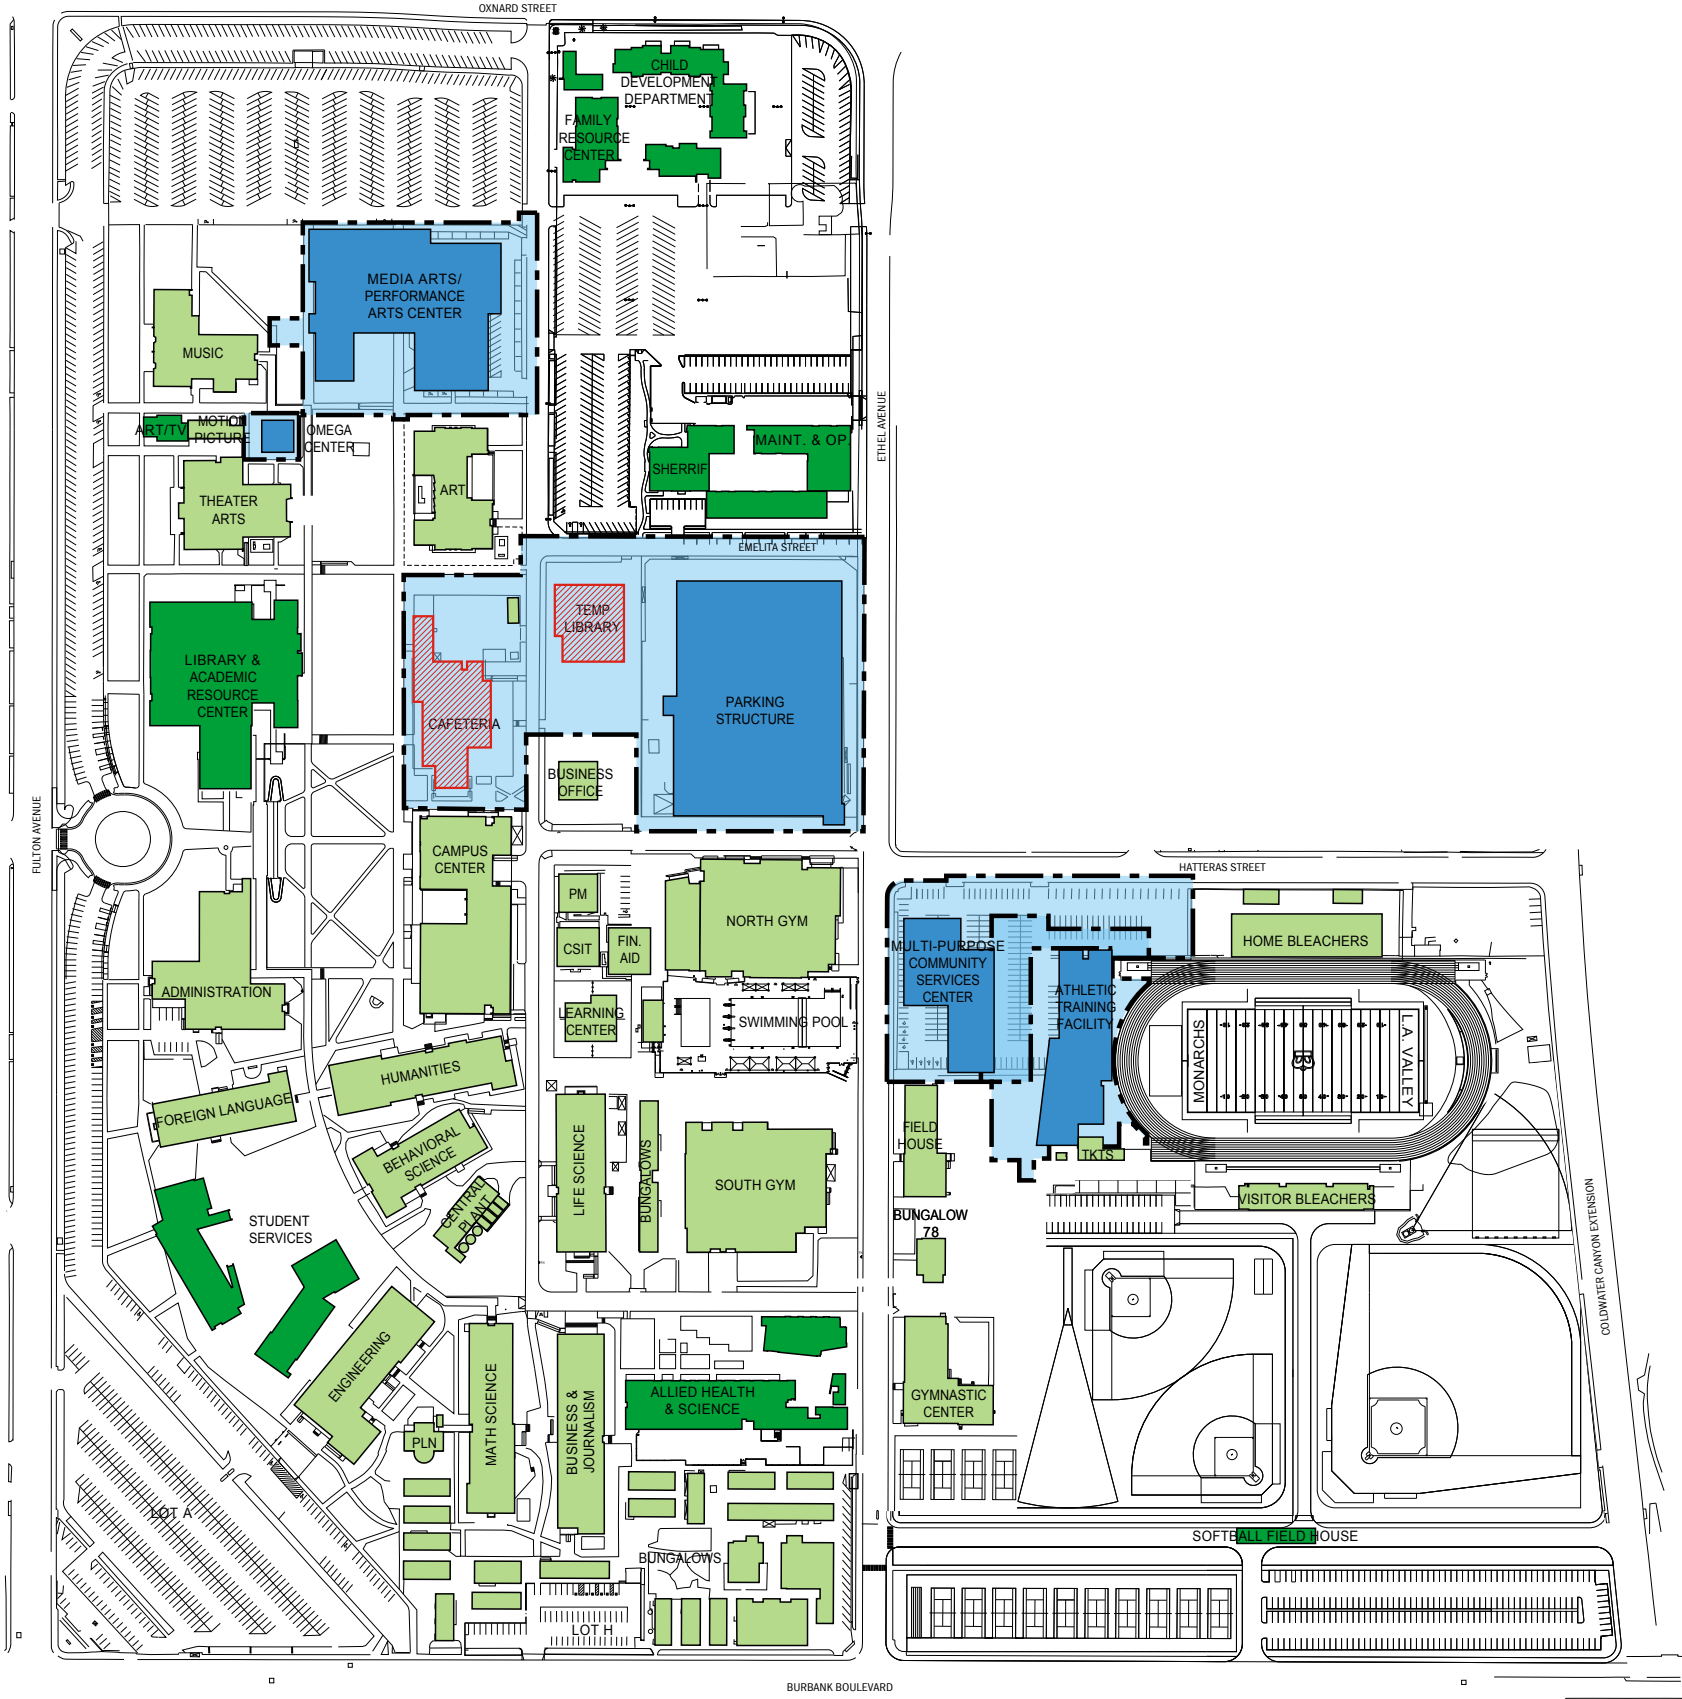

OCT - NOV - DEC
Q4/2012

Legend



- Monarch Center Construction Begins
- Demo Administration Building Begins
- Campus Infrastructure II Project Begins (not shown)
- Multi-Purpose Community Services Center Construction Ongoing
- Parking Structure Construction Ongoing
- Media Arts/Performance Arts Center Construction Ongoing
- Central Plant Expansion Construction Ongoing (not shown)
- Athletic Training Facility Construction Ongoing
- Swing Space Improvement Construction Completed (not shown)
- Demo Cafeteria, Temp Library Completed
- Omega Data Center Construction Completed

Existing Building

New Building

Area Under Construction

Building To Be Demolished Or Relocated

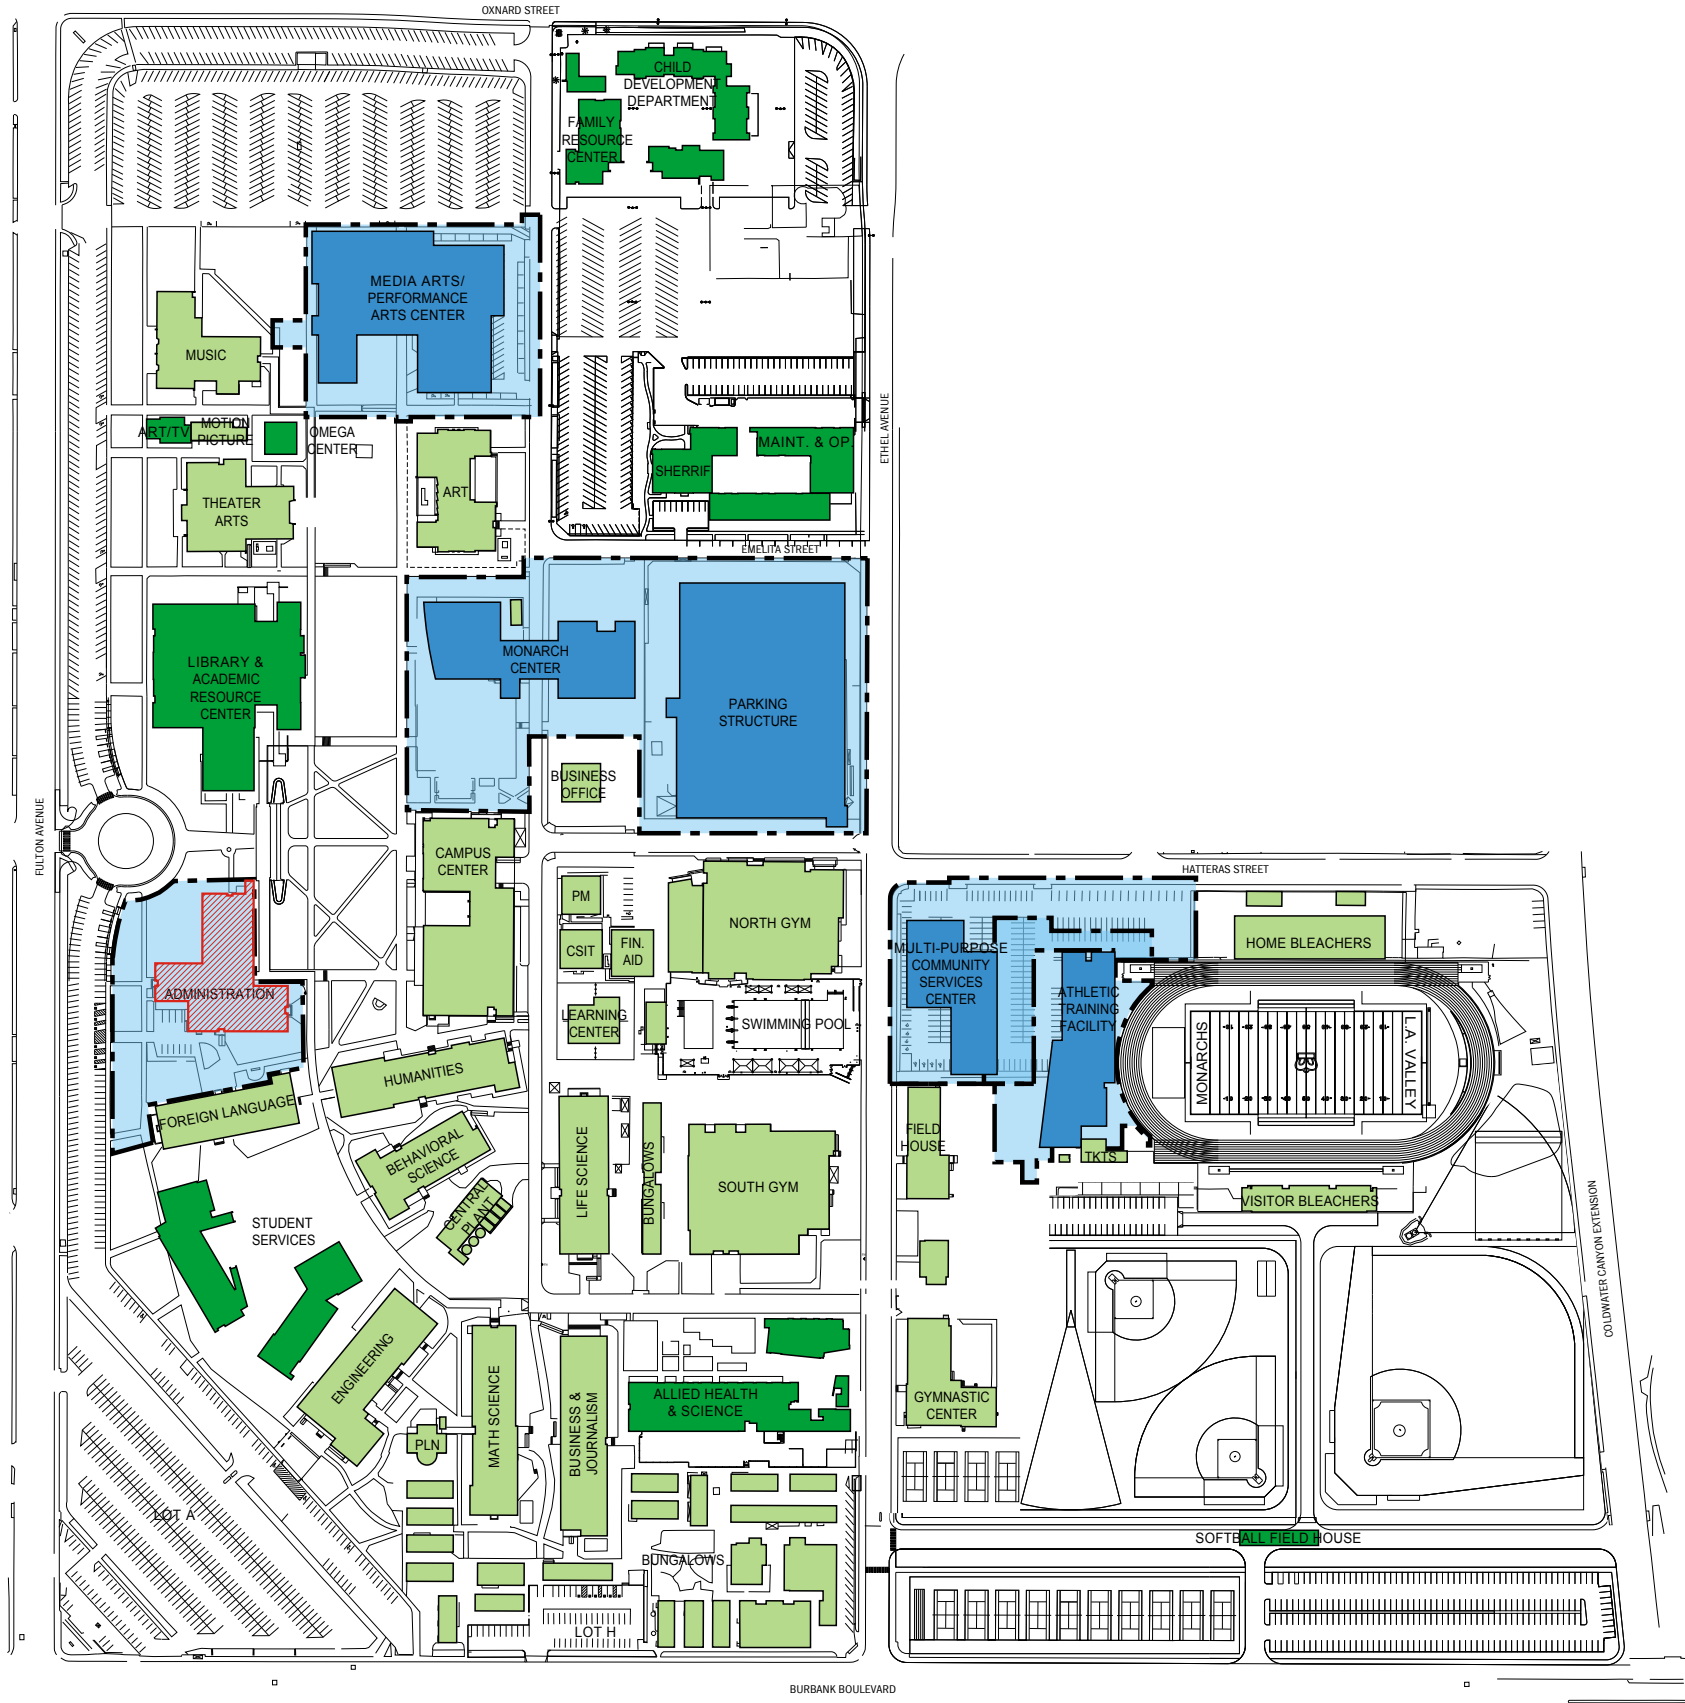

JAN - FEB - MAR
Q1/2013

Legend


- Valley Glen Gateway Building Construction Begins
- Demo Bungalows 9-12
- Motion Picture Renovation Construction Begins
- Monarch Center Construction Ongoing
- Campus Infrastructure II Project Ongoing (not shown)
- Central Plant Expansion Construction Ongoing (not shown)
- Multi-Purpose Community Services Center Construction Ongoing
- Parking Structure Construction Ongoing
- Media Arts/Performance Arts Center Construction Ongoing
- Demo Administration Building Completed
- Athletic Training Facility Construction Completed

Existing Building

New Building

Area Under Construction


Building To Be Demolished Or Relocated




APR - MAY - JUN
Q2/2013

Legend

- Planetarium Expansion Construction Begins
- Valley Glen Gateway Building Construction Ongoing
- Motion Picture Renovation Construction Ongoing
- Monarch Center Construction Ongoing
- Campus Infrastructure II Project Ongoing (not shown)
- Multi-Purpose Community Services Center Construction Ongoing
- Parking Structure Construction Ongoing
- Media Arts/Performance Arts Center Construction Ongoing
- Central Plant Expansion Construction Completed (not shown)

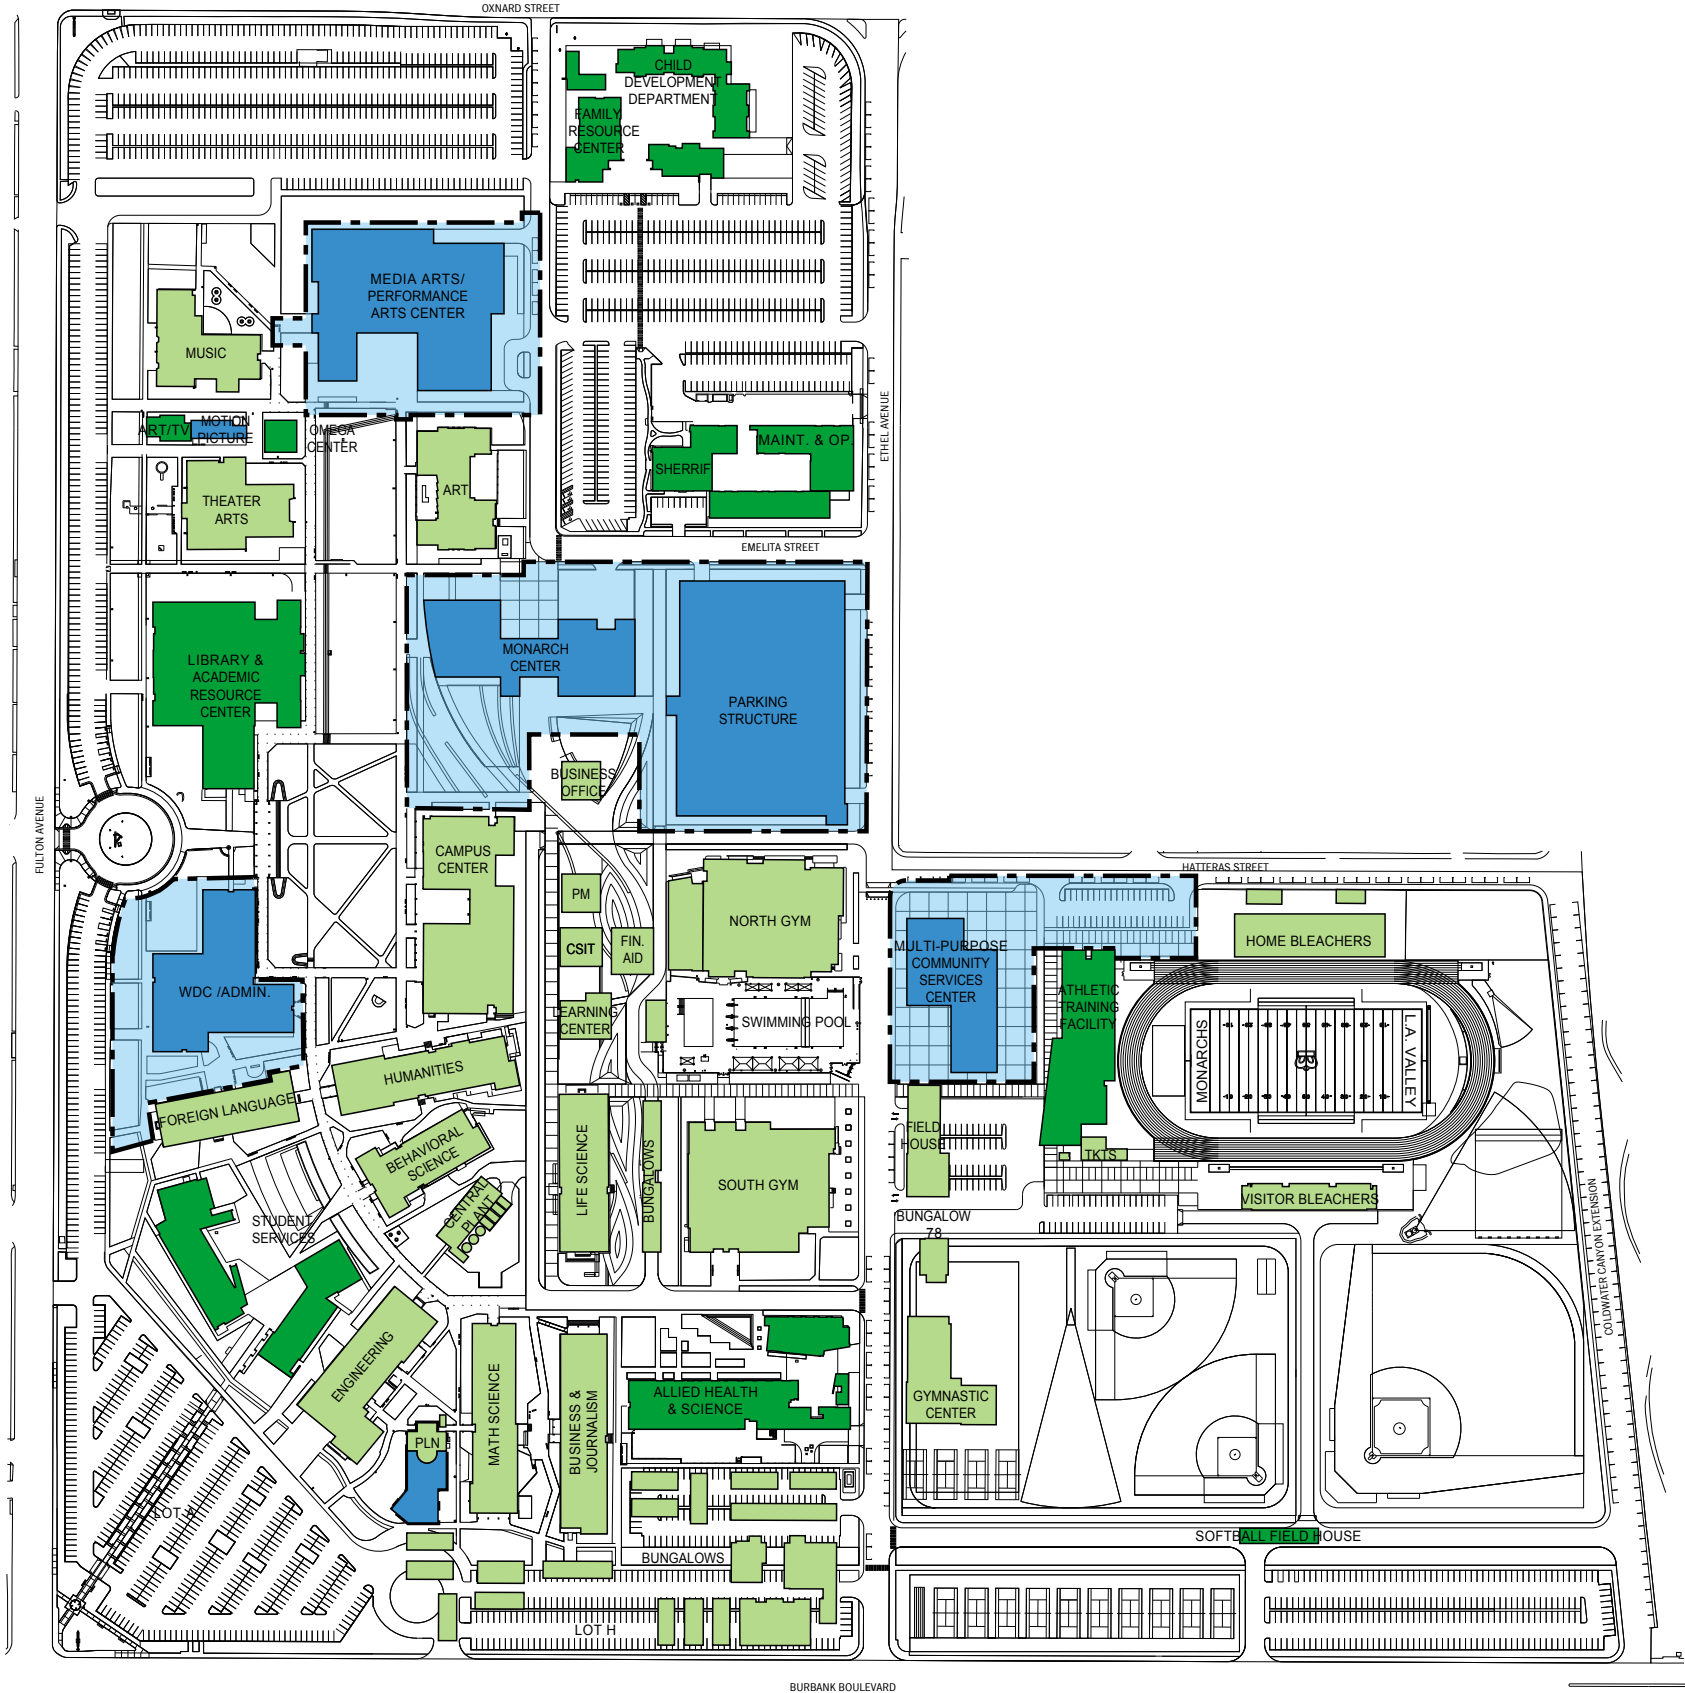


- Existing Building
- New Building
- Area Under Construction
- Building To Be Demolished Or Relocated




JUL - AUG - SEP
Q3/2013

Legend

- Planetarium Expansion Construction Ongoing
- Valley Glen Gateway Building Construction Ongoing
- Motion Picture Renovation Construction Ongoing
- Monarch Center Construction Ongoing
- Campus Infrastructure II Project Ongoing (not shown)
- Multi-Purpose Community Services Center Construction Ongoing
- Media Arts/Performance Arts Center Construction Ongoing
- Parking Structure Construction Completed

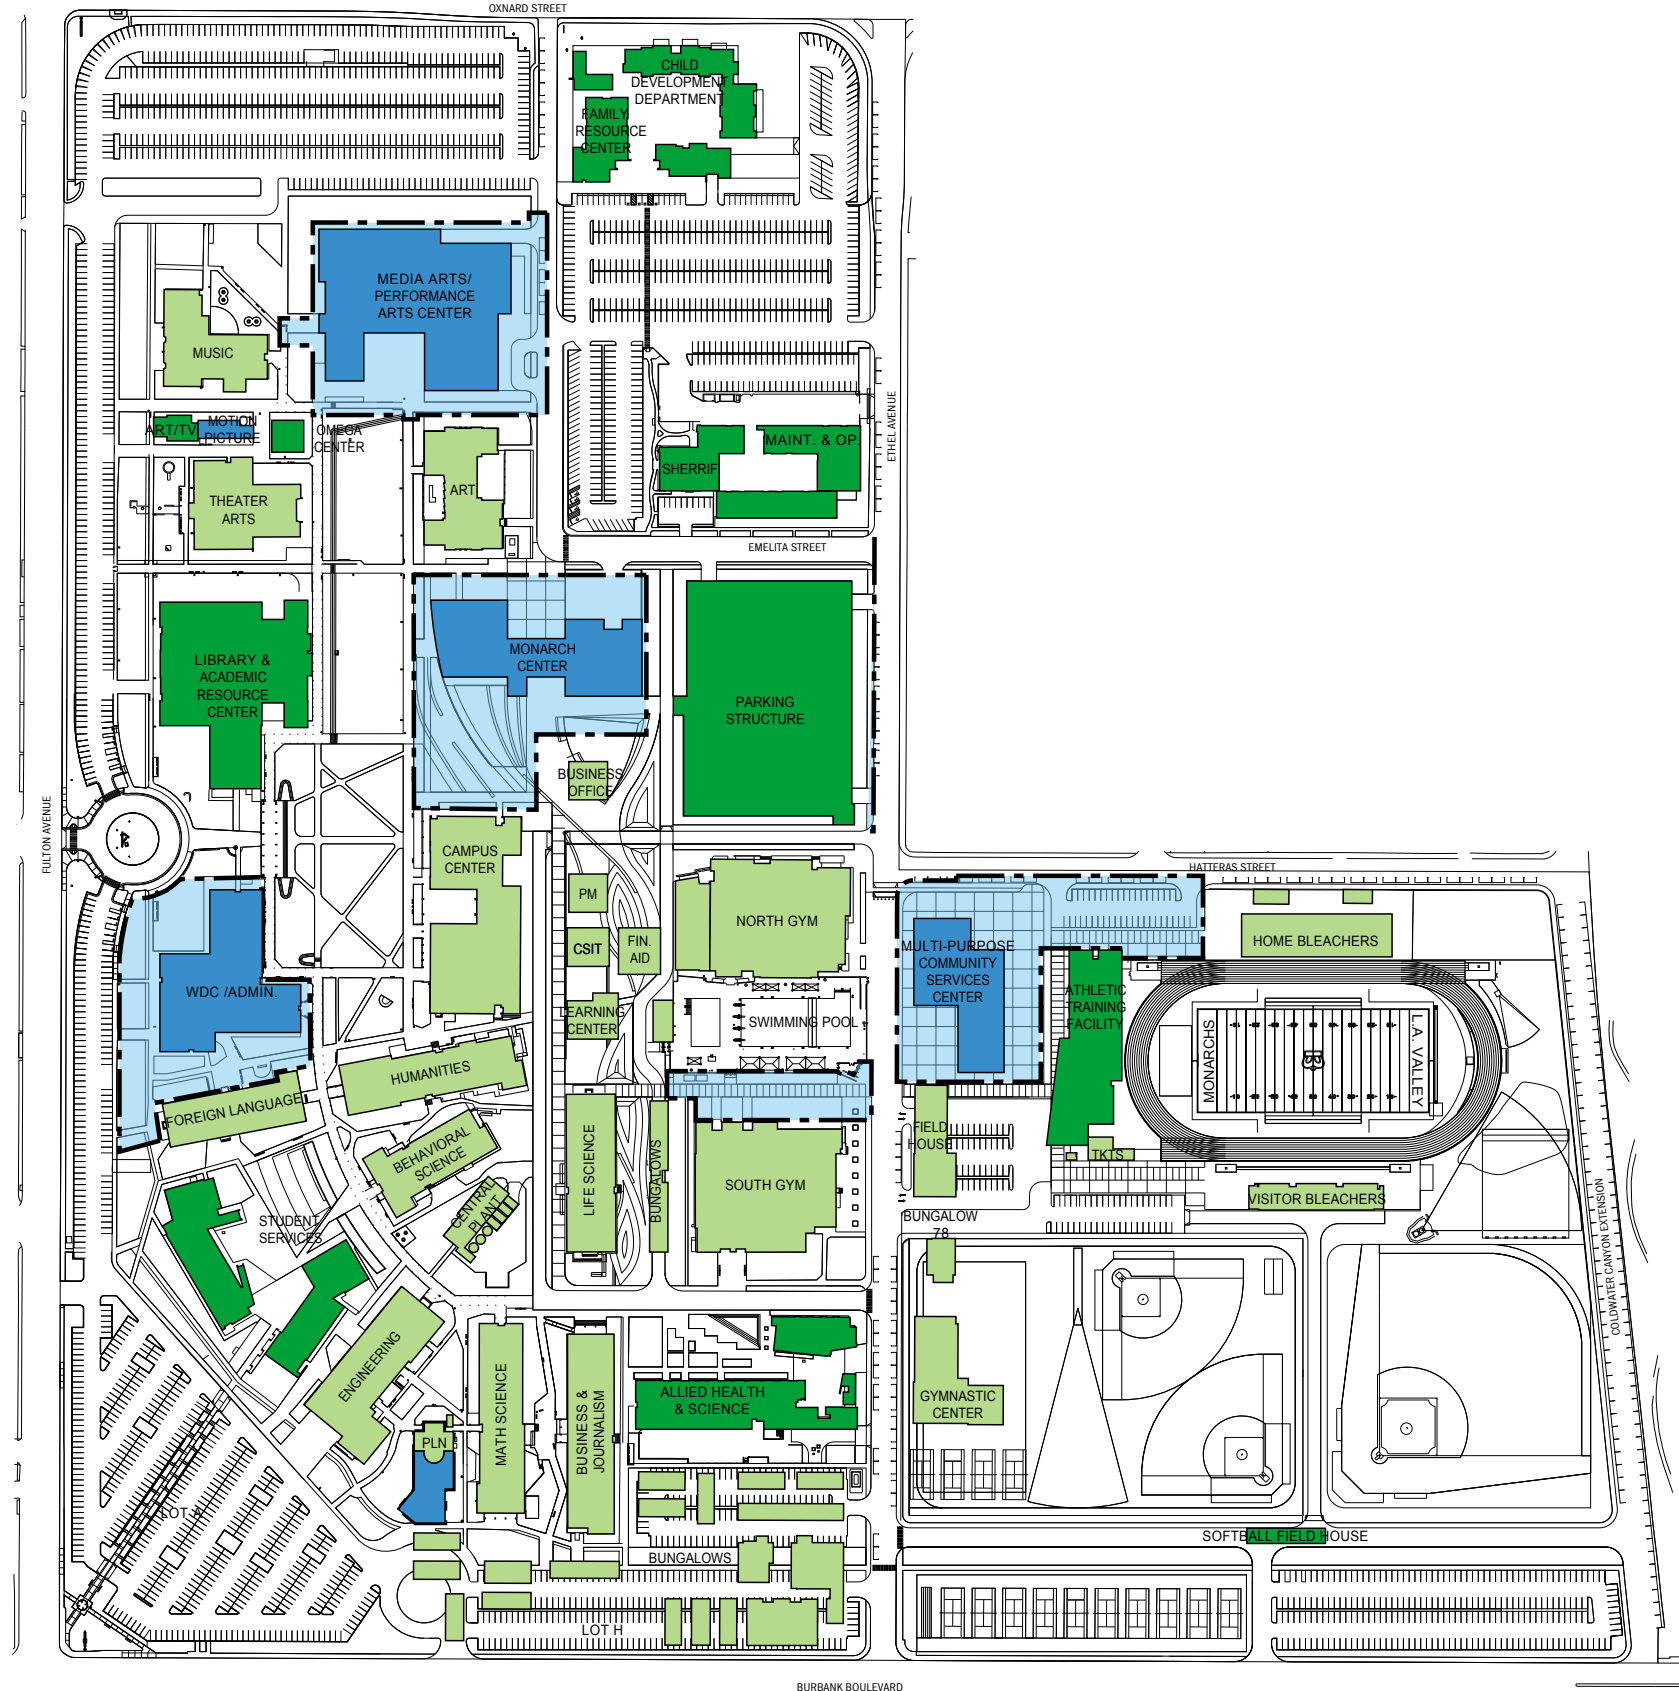

- Existing Building
- New Building
- Area Under Construction
- Building To Be Demolished Or Relocated



OCT - NOV - DEC
Q4/2013

Legend

- Demo Gymnastic Center, Field House, Weight Room
- Multi-Purpose Community Services Center Site Improvements Begin

- Planetarium Expansion Construction Ongoing
- Valley Glen Gateway Building Construction Ongoing
- Monarch Center Construction Ongoing

- Campus Infrastructure II Project Ongoing (not shown)
- Media Arts/Performance Arts Center Construction Ongoing



- Motion Picture Renovation Construction Completed
- Multi-Purpose Community Services Center Construction Completed

Existing Building

New Building

Area Under Construction

Building To Be Demolished Or Relocated

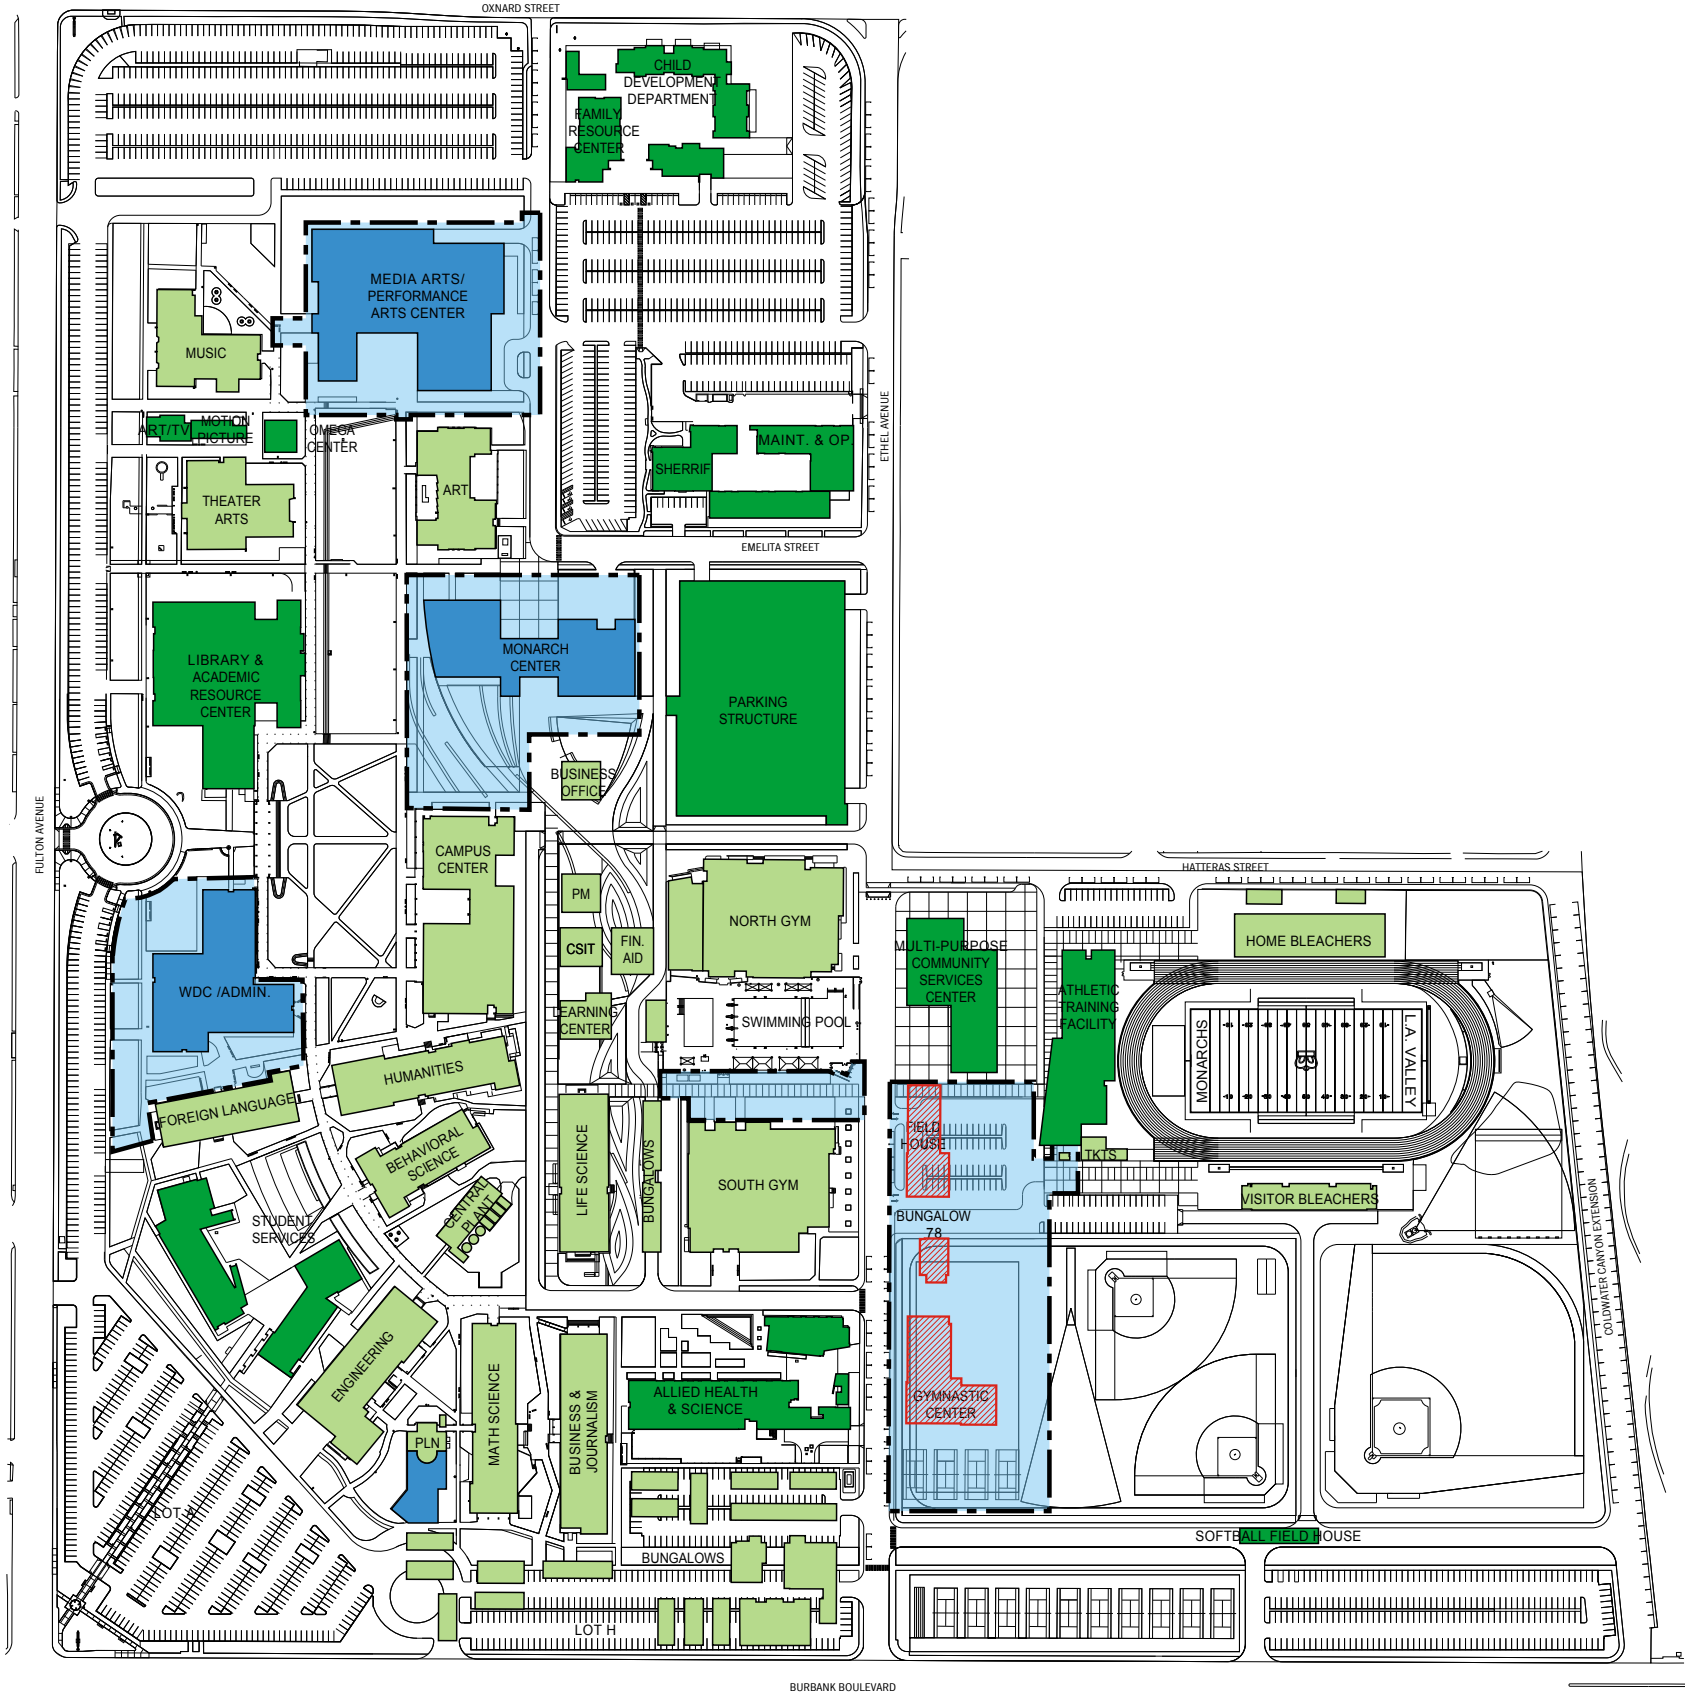

JAN - FEB - MAR
Q1/2014

Legend


- Demo Business Office
- Monarch Center Site Improvements Begin
- Campus Center Renovation Construction Begins
- Multi-Purpose Community Services Center Site Improvements Ongoing
- Planetarium Expansion Construction Ongoing
- Valley Glen Gateway Building Construction Ongoing
- Monarch Center Construction Completed
- Campus Infrastructure II Project Completed (not shown)
- Media Arts/Performance Arts Center Construction Completed

Existing Building

New Building

Area Under Construction


Building To Be Demolished Or Relocated




APR - MAY - JUN
Q2/2014

Legend

- Demo Financial Aid, CSIT, PM, Bungalows 82-86, Temp LRC Begins
- Demo Bungalows Begins
- Demo Theater Arts Begins
- Lots H & J Construction Begins
- Monarch Center Site Improvements Ongoing
- Campus Center Renovation Construction Ongoing
- Valley Glen Gateway Building Construction Completed
- Multi-Purpose Community Services Center Site Improvements Completed
- Planetarium Expansion Construction Completed

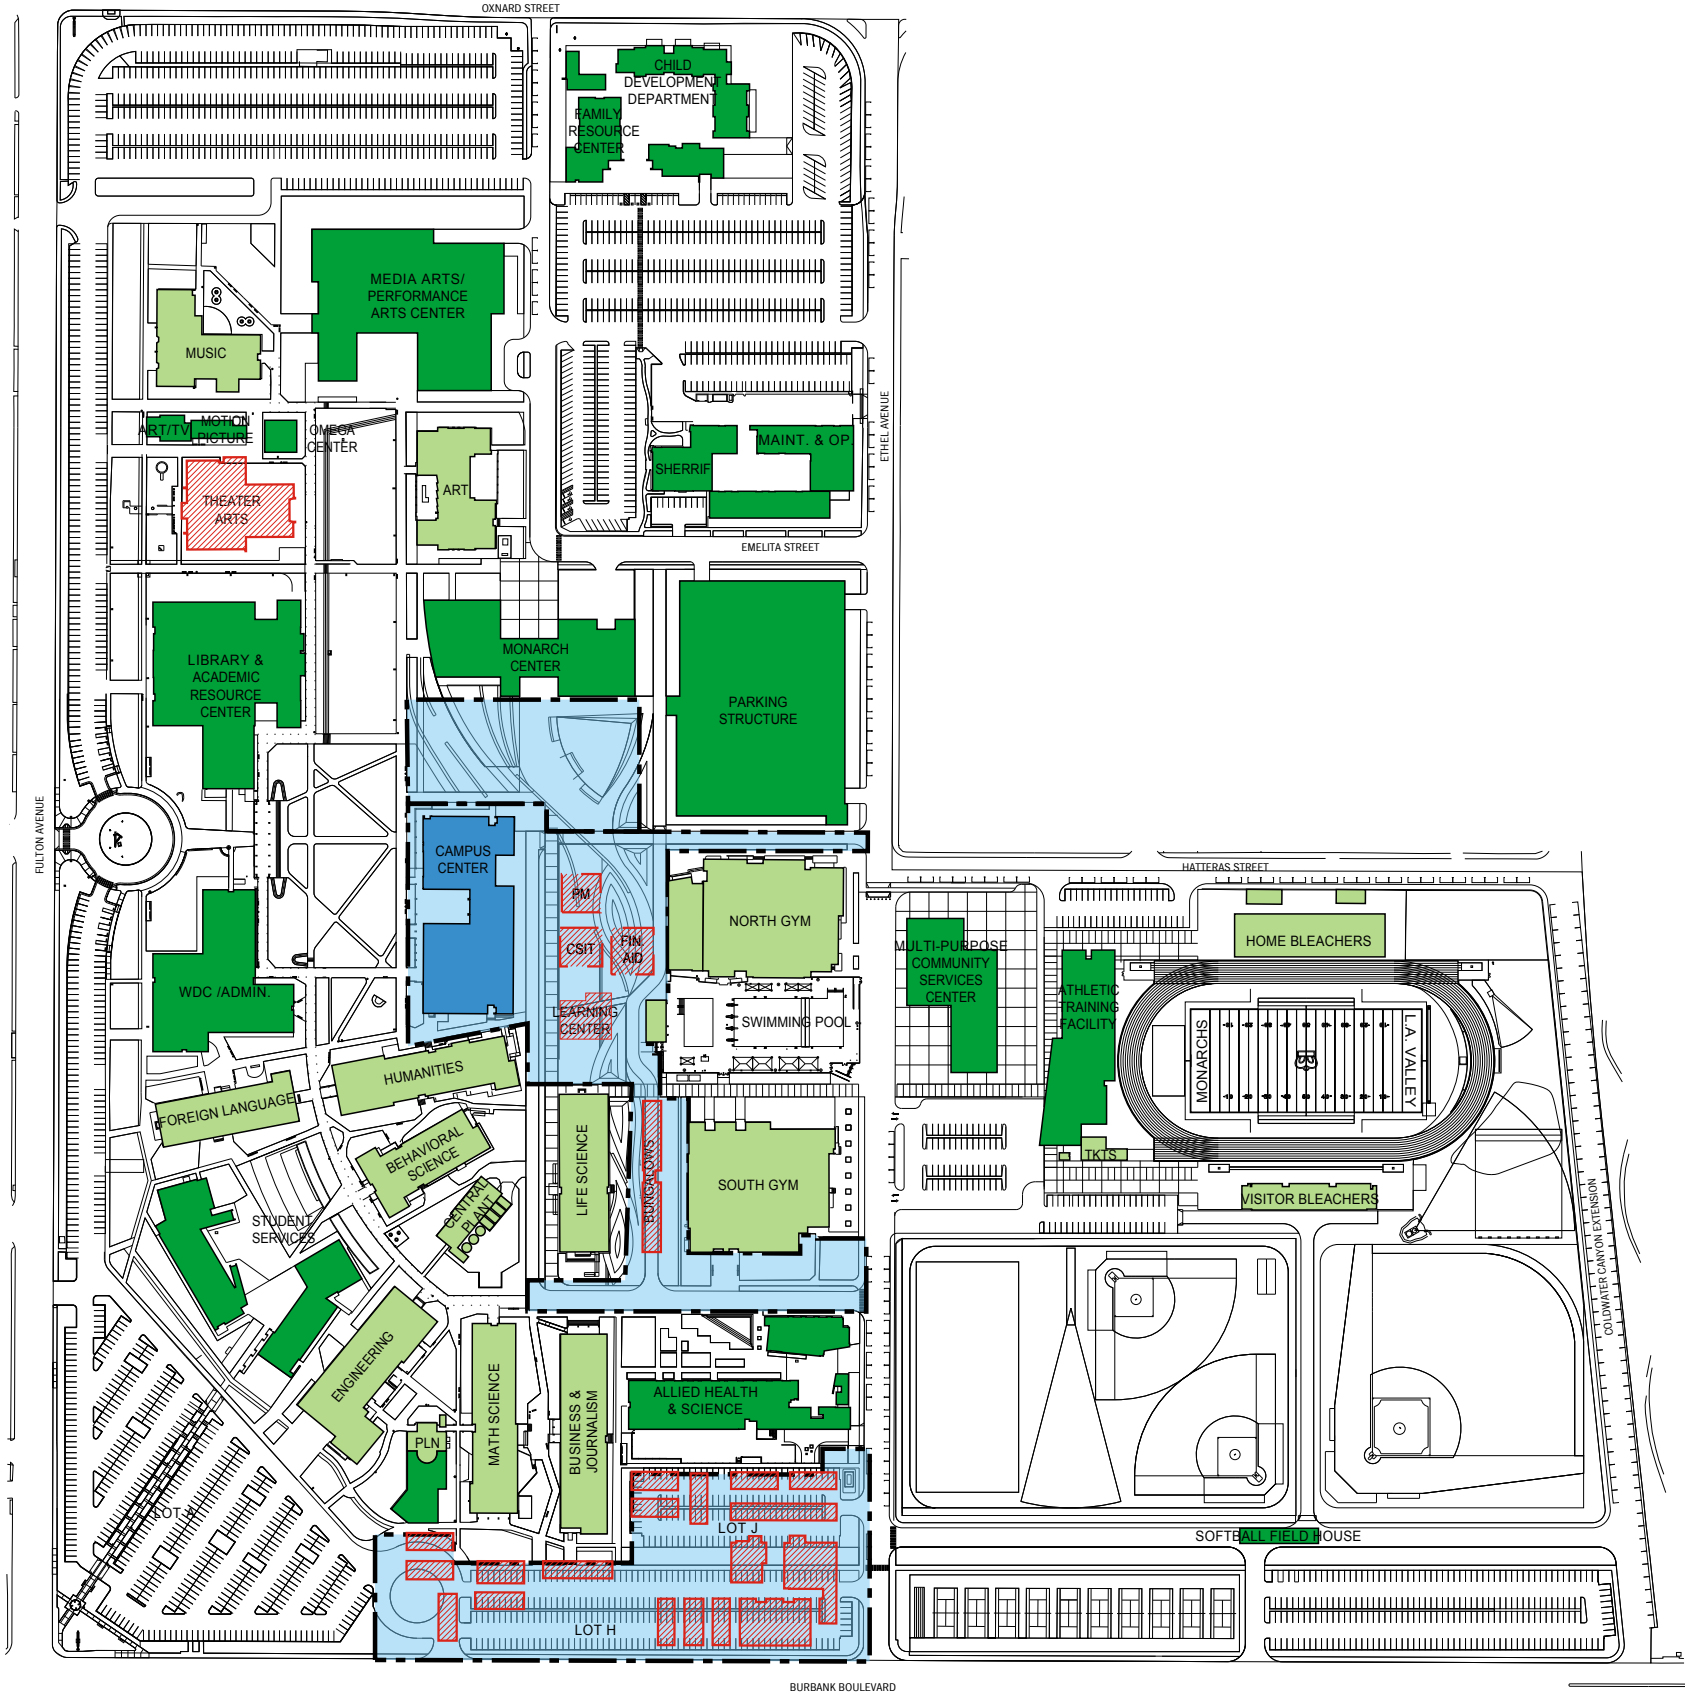


- Existing Building
- New Building
- Area Under Construction
- Building To Be Demolished Or Relocated




JUL - AUG - SEP
Q3/2014

Legend

- Sustainable Mall Construction Begins
- Lots H & J Construction Ongoing
- Campus Center Renovation Construction Ongoing
- Demo Financial Aid, CSIT, PM, Bungalows 82-86
Temp LRC Completed
- Monarch Center Site Improvements Completed

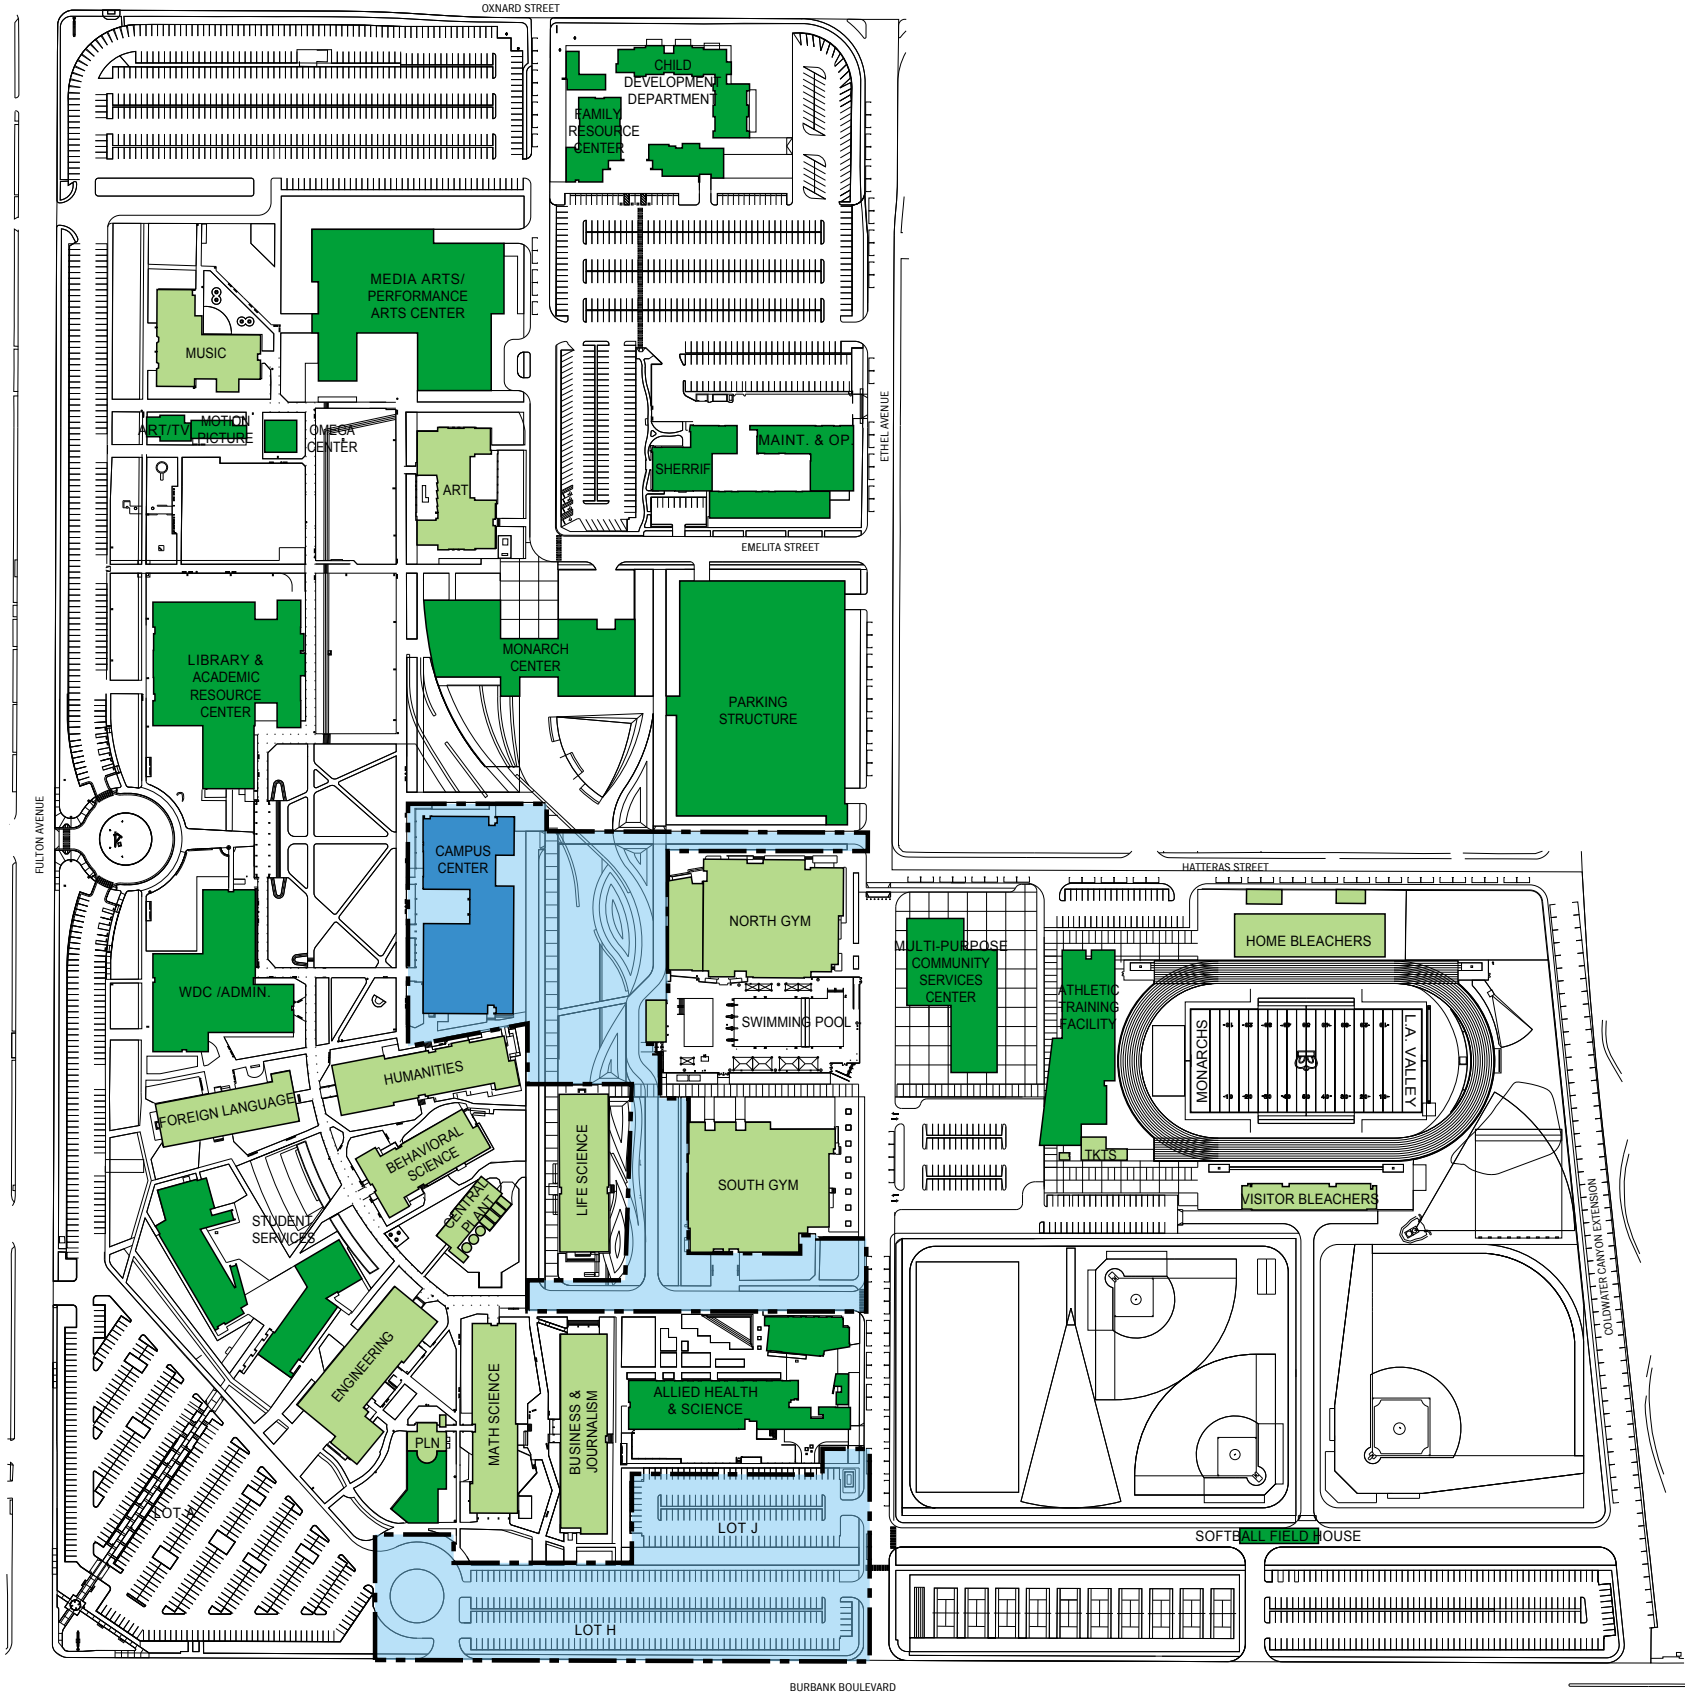


- Existing Building
- New Building
- Area Under Construction
- Building To Be Demolished Or Relocated



OCT - NOV - DEC
Q4/2014

Legend

- Sustainable Mall Construction Completed
- Lots H & J Construction Completed
- Campus Center Renovation Construction Completed

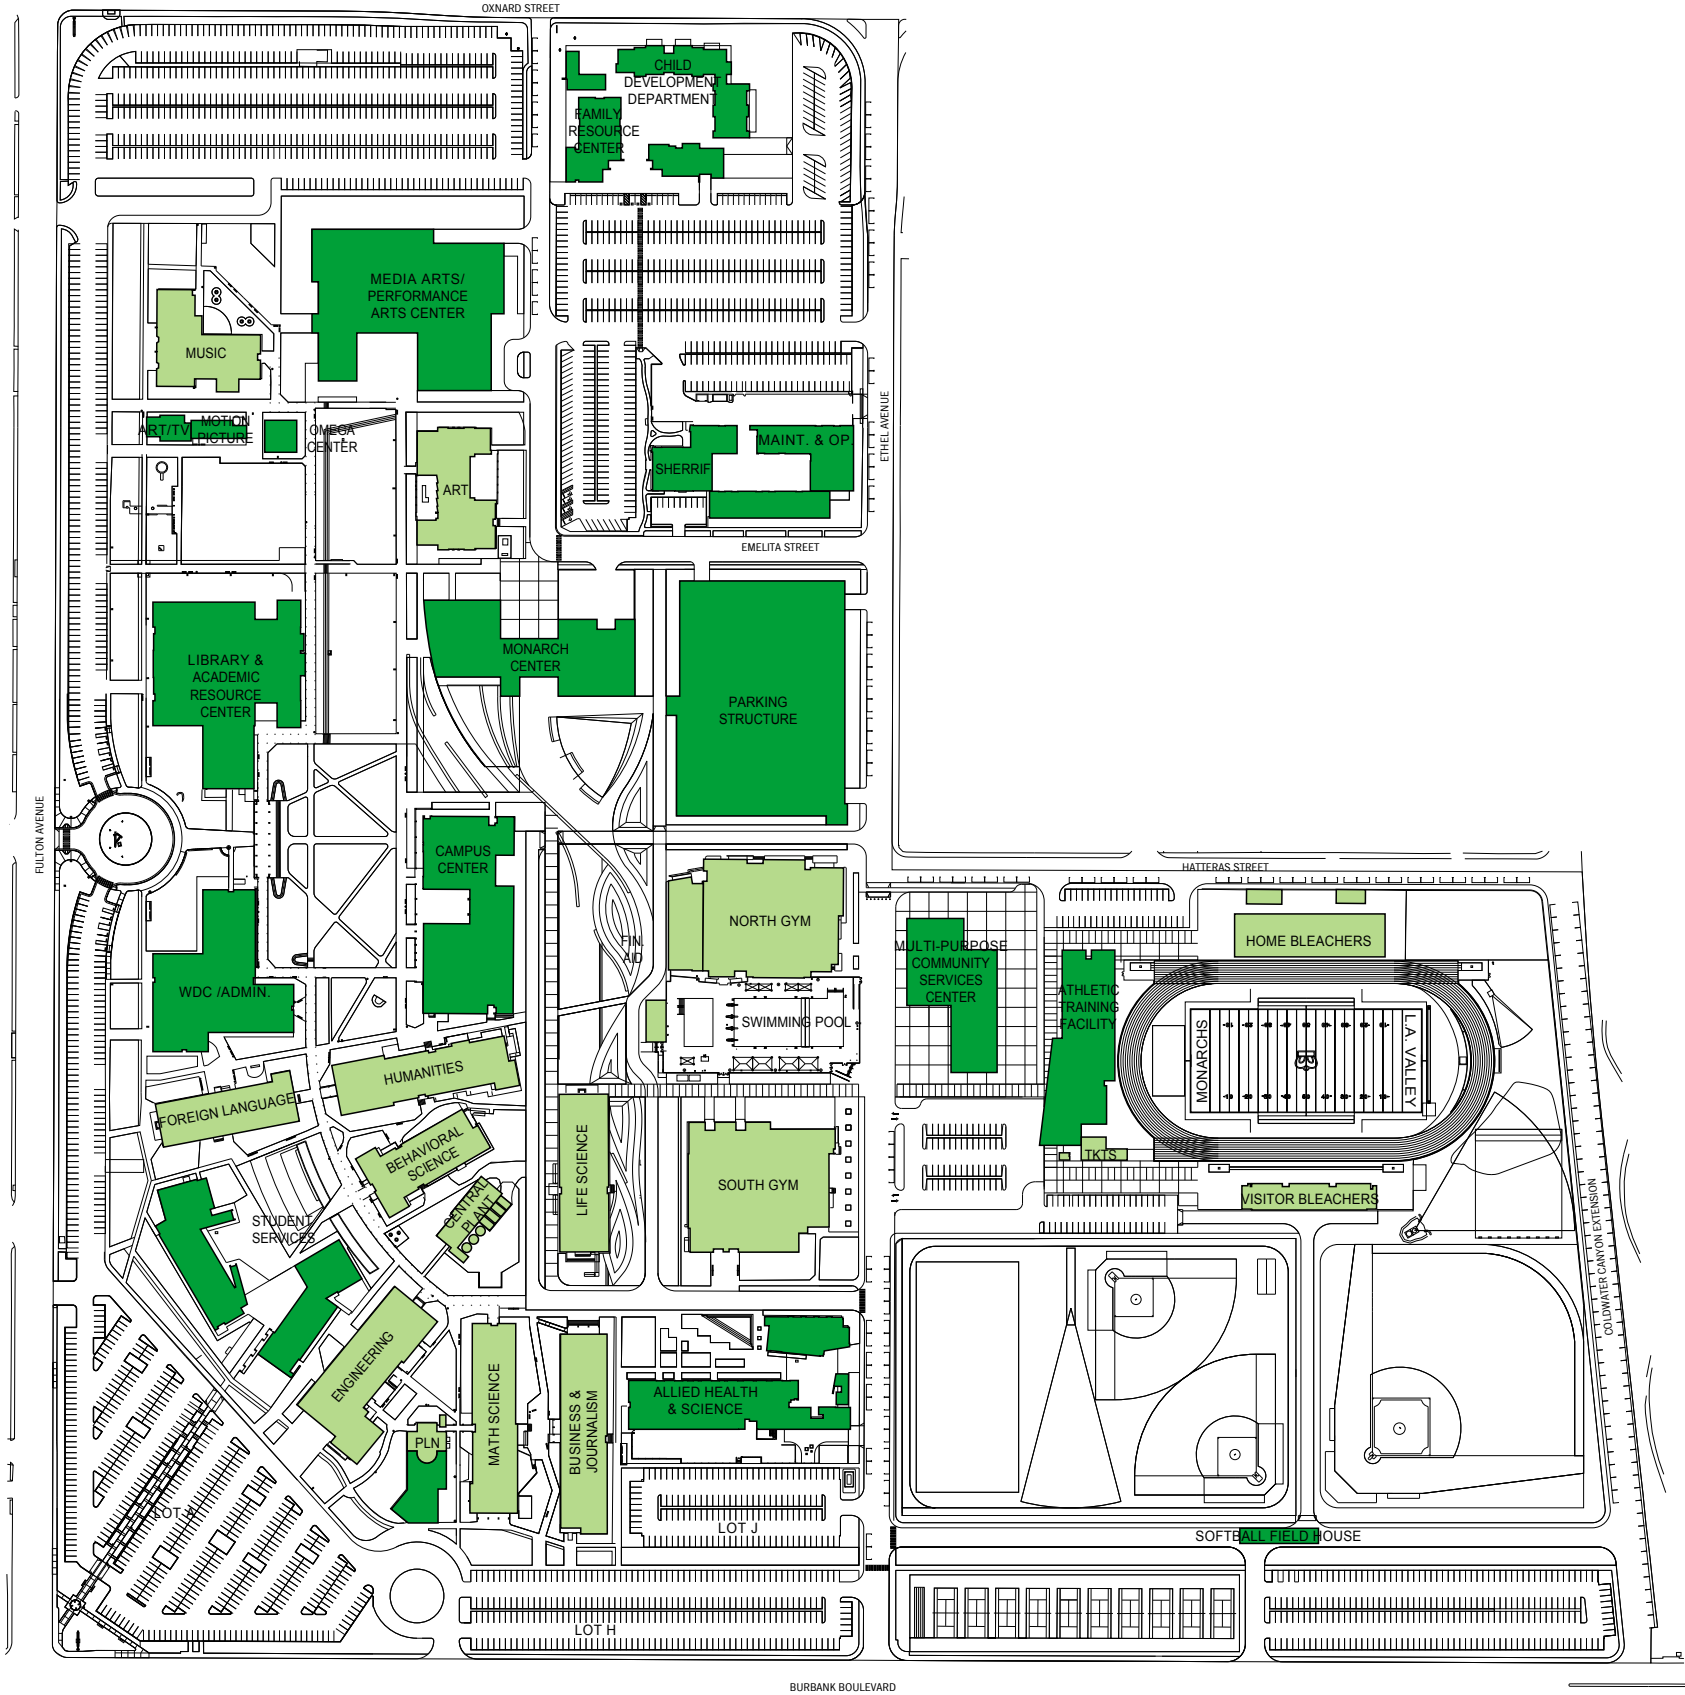

- Existing Building
- New Building
- Area Under Construction
- Building To Be Demolished Or Relocated

