


APR - MAY - JUN

Q2/2013


Project Status

- Demo Softball Field
- Parking Structure Construction Begins
- Community Services Center Construction Begins
- Learning Resource Center Relocation & Remodel Begins
- Building Retrofit Project Construction Begins (not shown)

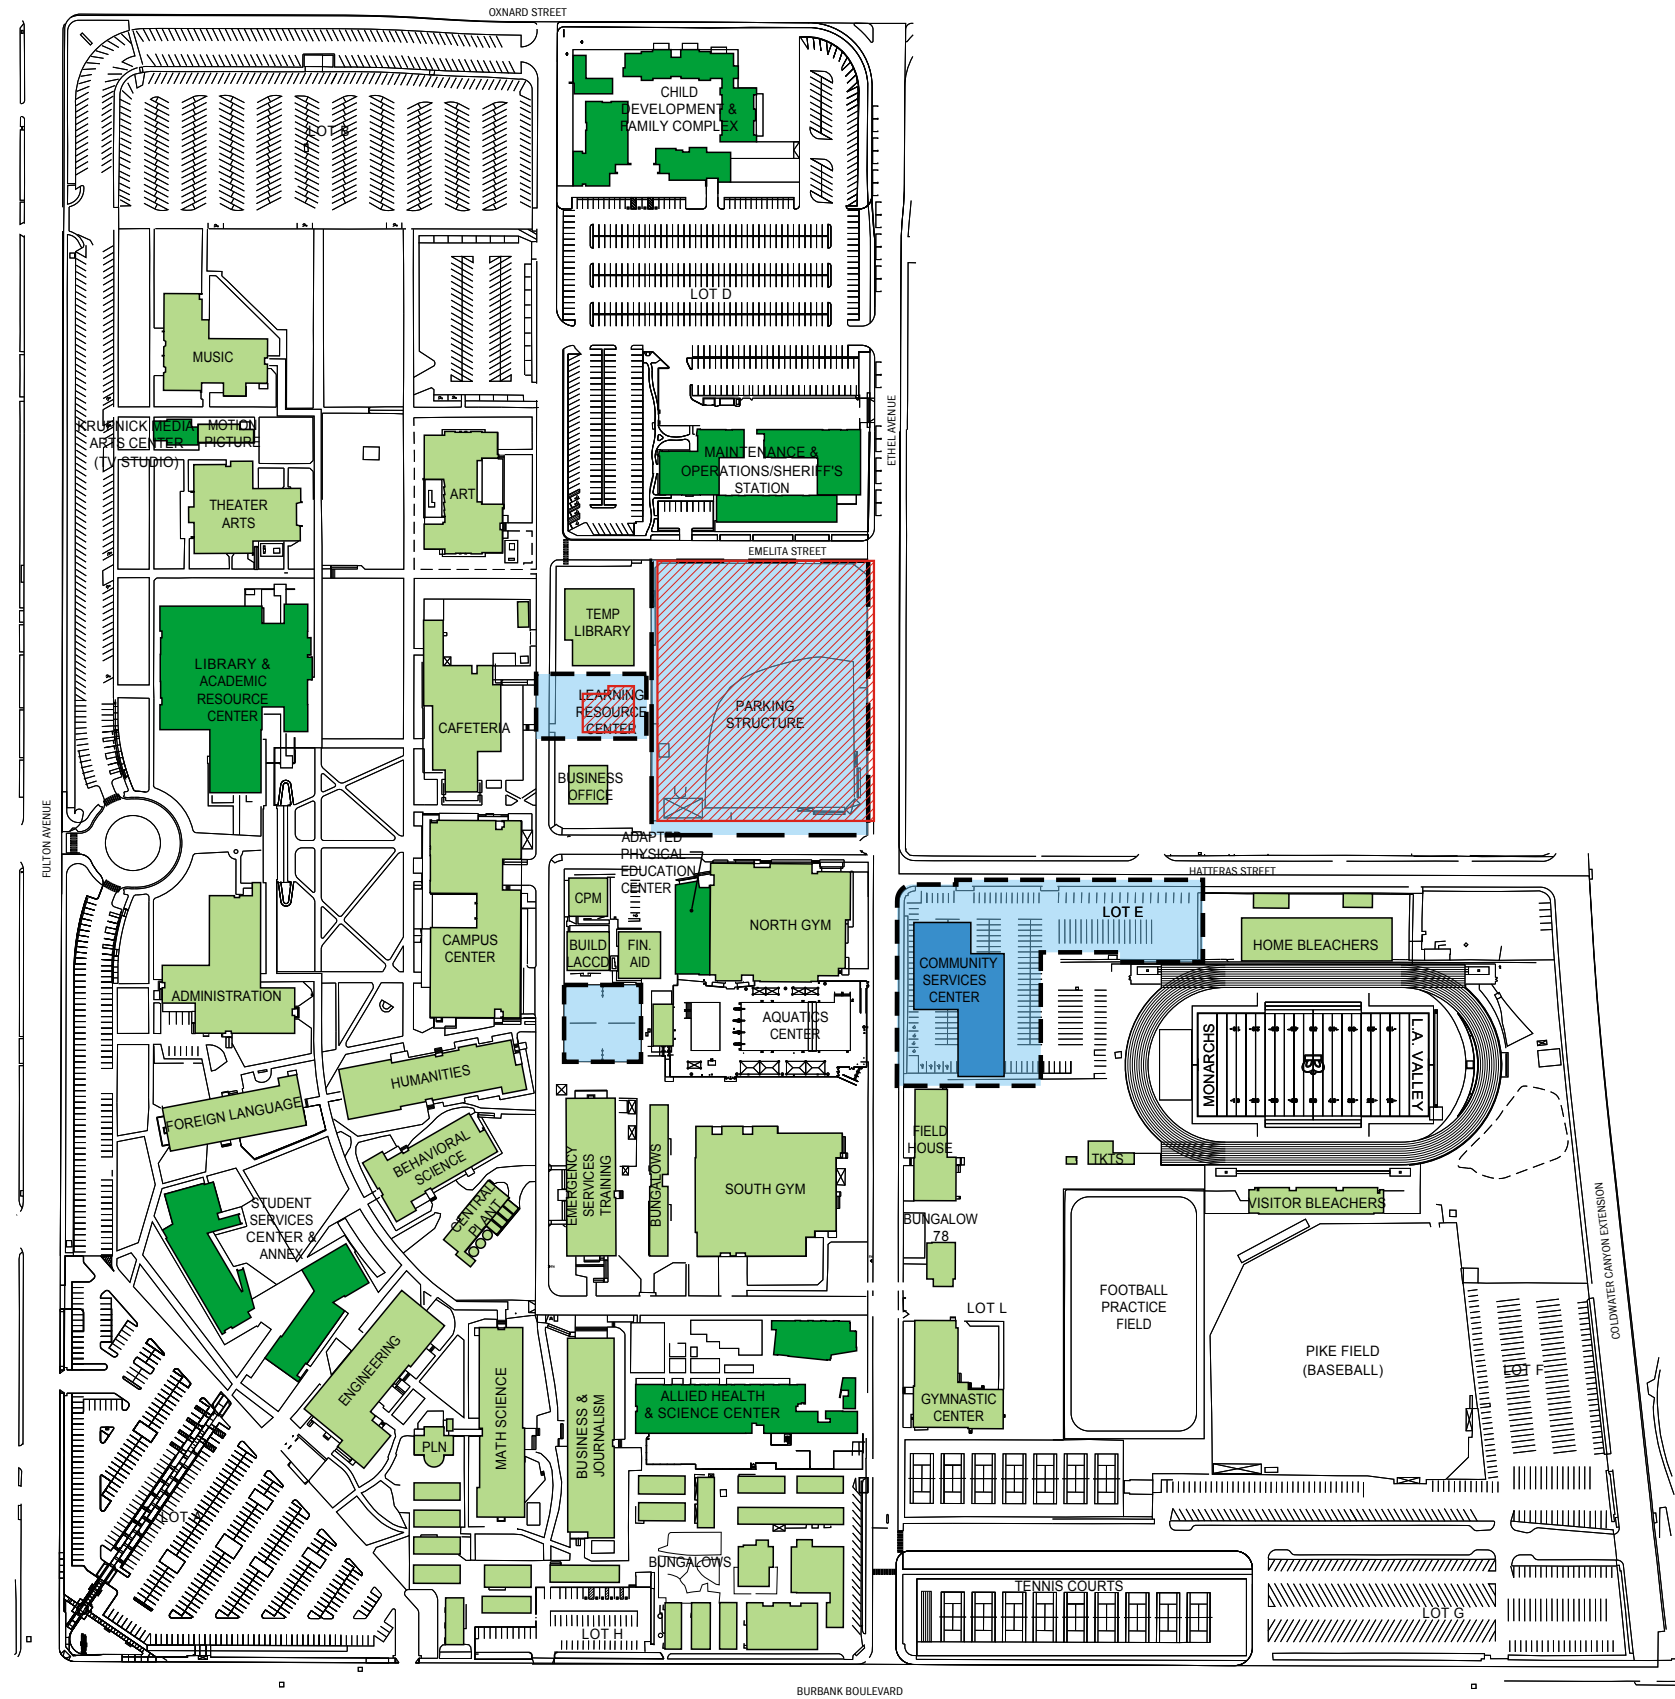

Legend

- Existing Building
- New Building / Major Renovation
- Area Under Construction
- Building To Be Demolished Or Relocated




JUL - AUG - SEP

Q3/2013


Project Status

- Swing Space Improvements Begins (not shown)
- Emergency Lighting, Fire Alarm & Security Systems Construction Begins (not shown)
- Parking Structure Construction Ongoing
- Community Services Center Construction Ongoing
- Learning Resource Center Relocation & Remodel Completed
- Building Retrofit Project Construction Completed (not shown)

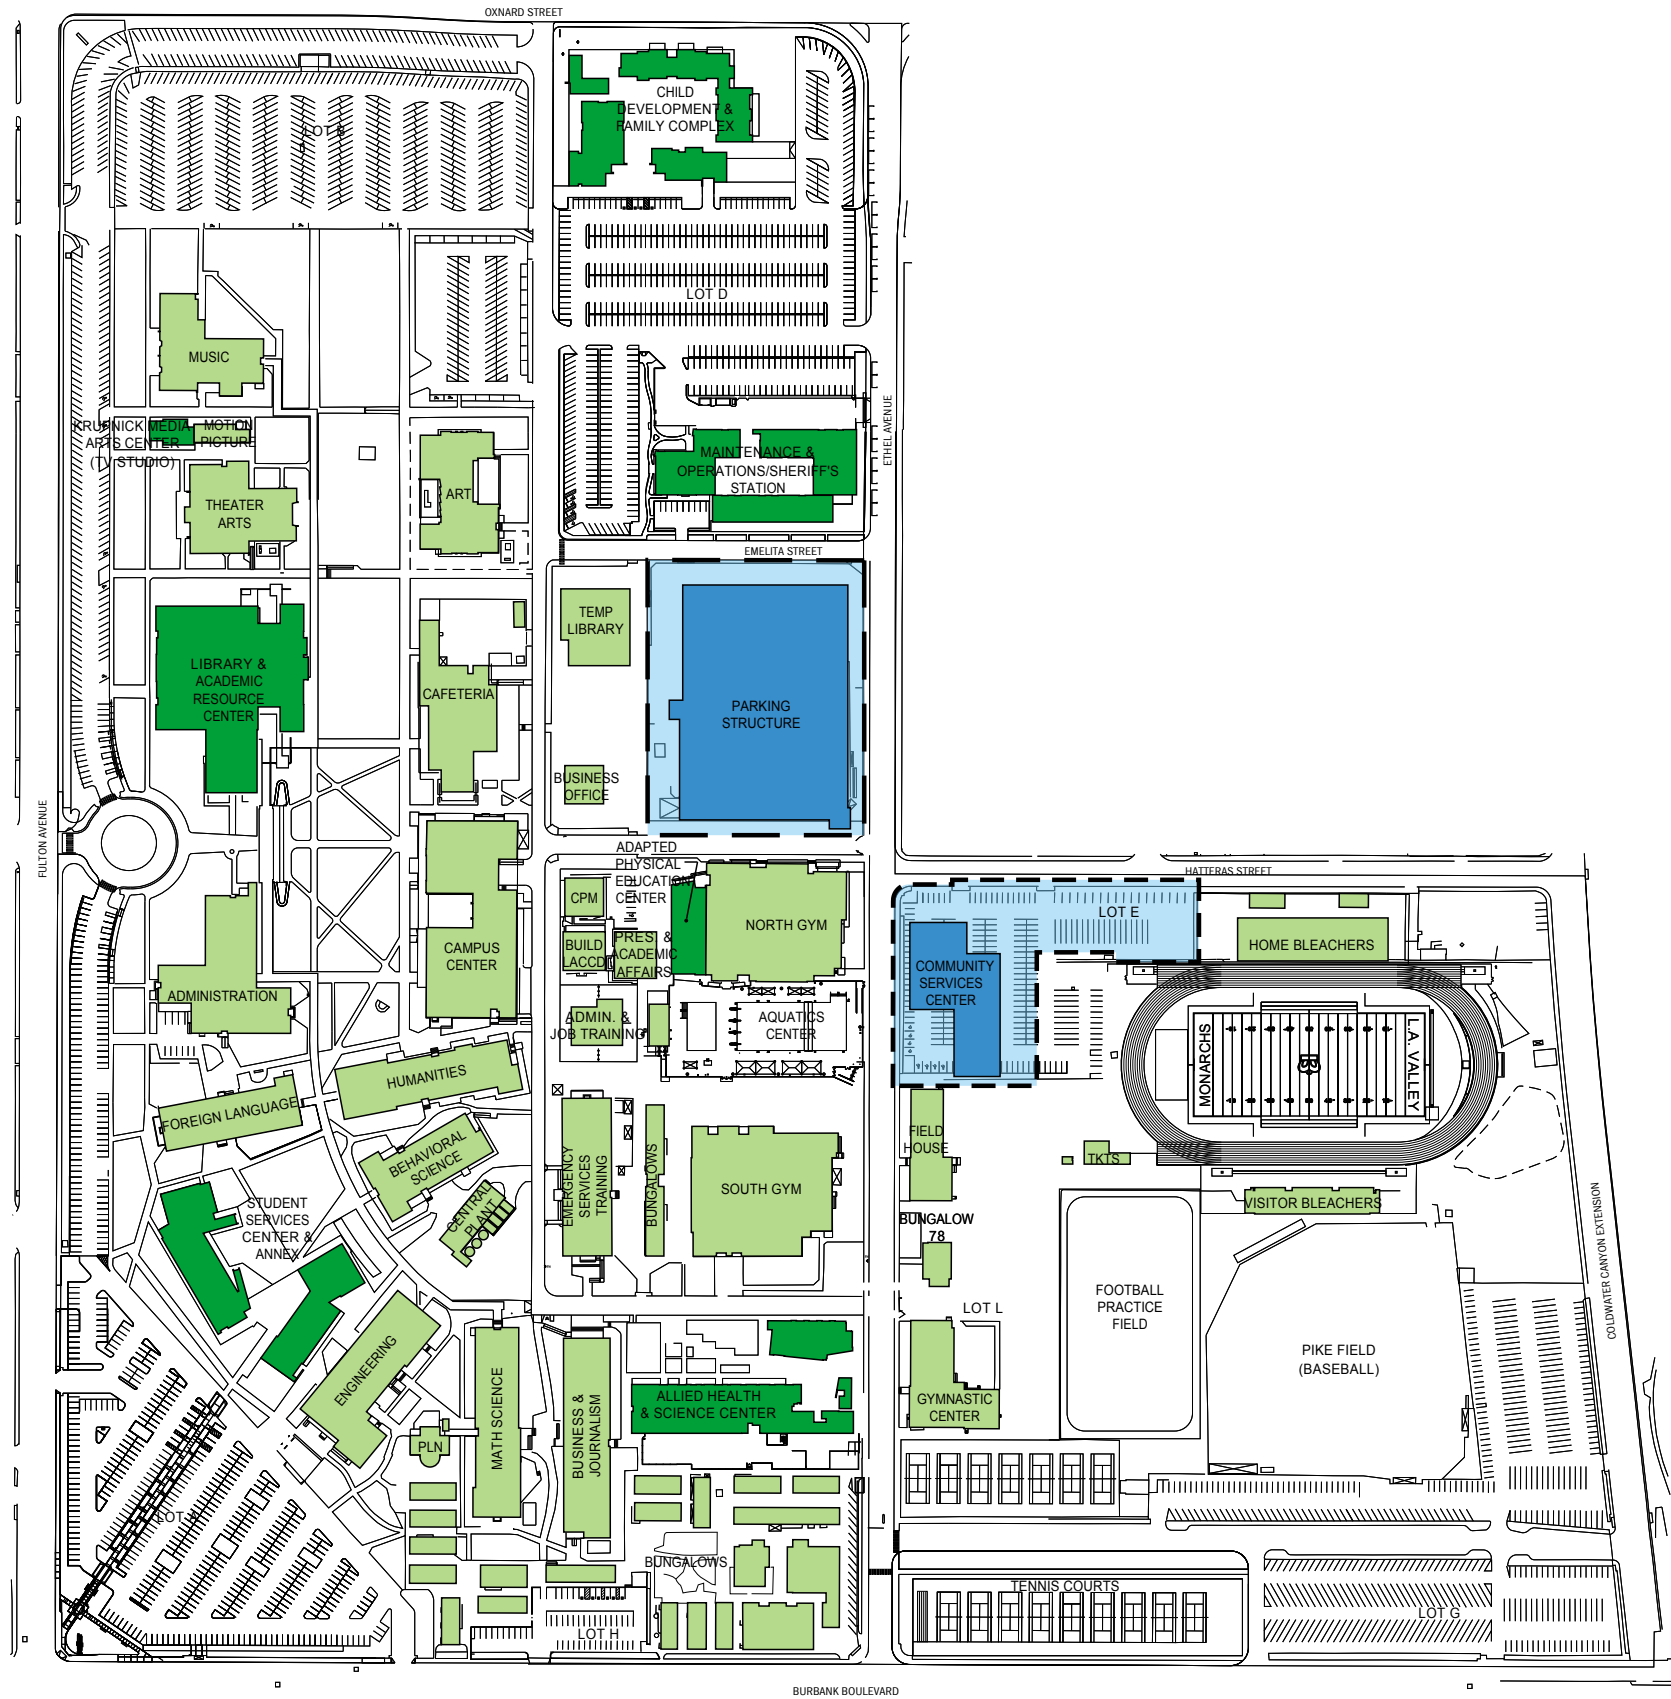

Legend

- Existing Building
- New Building / Major Renovation
- Area Under Construction
- Building To Be Demolished Or Relocated




OCT - NOV - DEC

Q4/2013


Project Status

- Performing & Media Arts Center Construction Begins
- Omega Data Center Construction Begins
- Stadium Field House Construction Begins
- Athletic Training Facility Fields Construction Begins
- Student Health Center (SHC) Temporary Relocation Construction Begins (not shown)
- Demo Cafeteria
- Removal of Temporary Library
- ADA Upgrades & Allied Health Services Corrective Construction - Phase 1 Begins (not shown)
- Parking Structure Construction Ongoing
- Community Services Center Construction Ongoing
- Performing & Media Arts Center Construction Ongoing
- Emergency Lighting, Fire Alarm & Security Systems Construction Ongoing (not shown)
- Swing Space Improvements Completed (not shown)

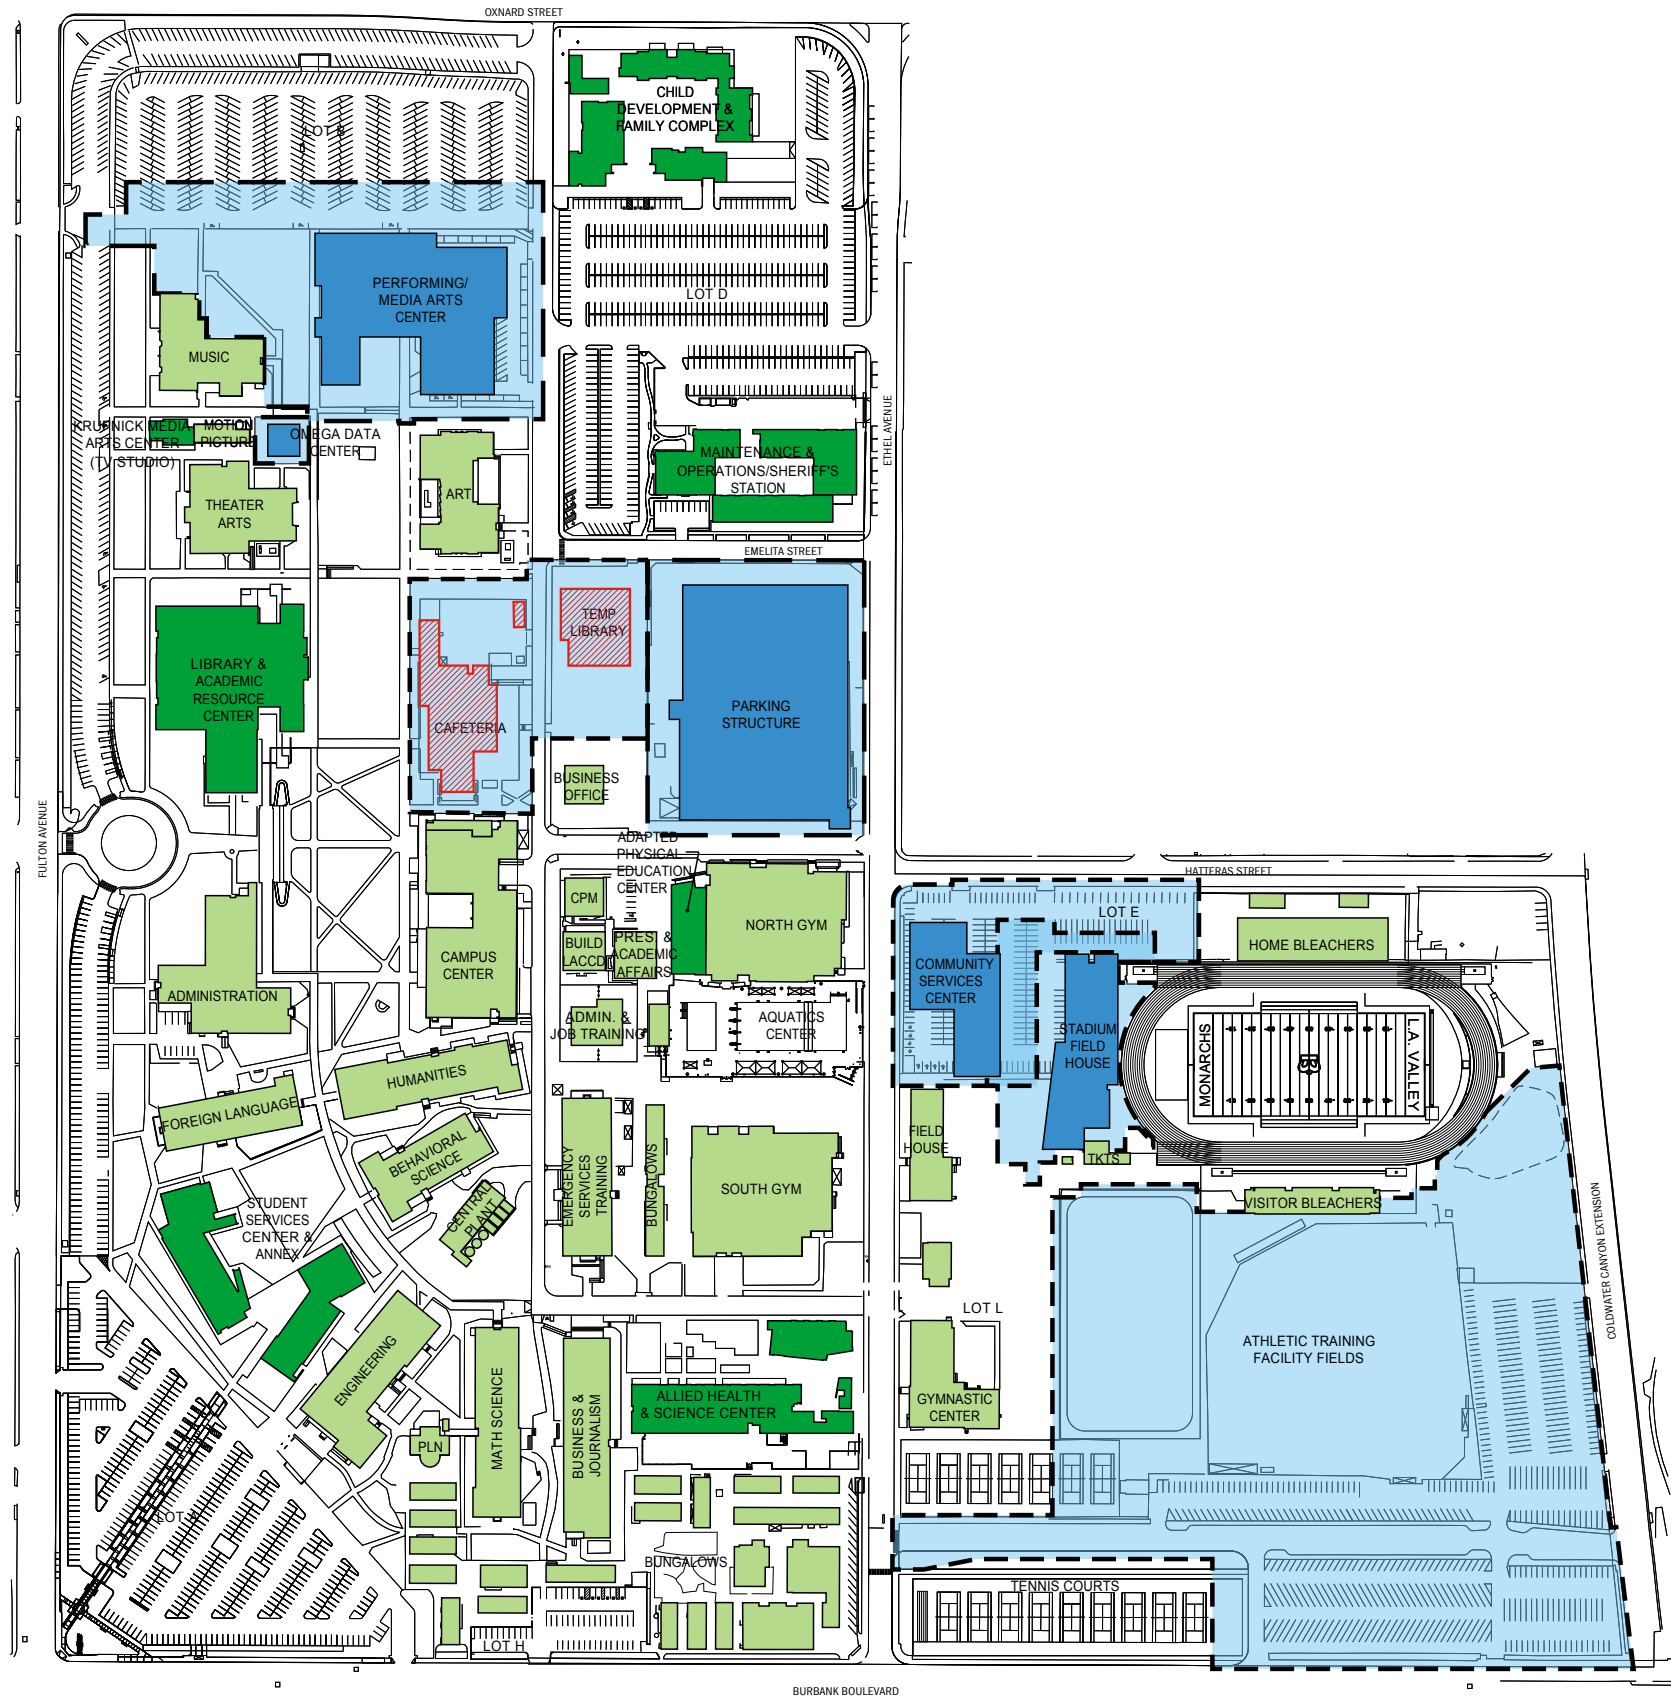

Legend

- Existing Building
- New Building / Major Renovation
- Area Under Construction
- Building To Be Demolished Or Relocated




JAN - FEB - MAR

Q1/2014


Project Status

- Monarch Center Construction Begins
- IT Phase 3 Construction Begins
- Motion Picture Renovation Construction Begins
- ADA Upgrades & Allied Health Services Corrective Construction - Phase 2 Begins (not shown)
- Gymnasium & Pool Phase II Construction Begins (not shown)
- Community Services Center Construction Ongoing
- Performing & Media Arts Center Construction Ongoing
- Stadium Field House Construction Ongoing
- Athletic Training Facility Fields Construction Ongoing
- Parking Structure Construction Completed
- Student Health Center (SHC) Temporary Relocation Construction Completed (not shown)
- ADA Upgrades & Allied Health Services Corrective Construction - Phase 1 Completed (not shown)
- Omega Data Center Construction Completed

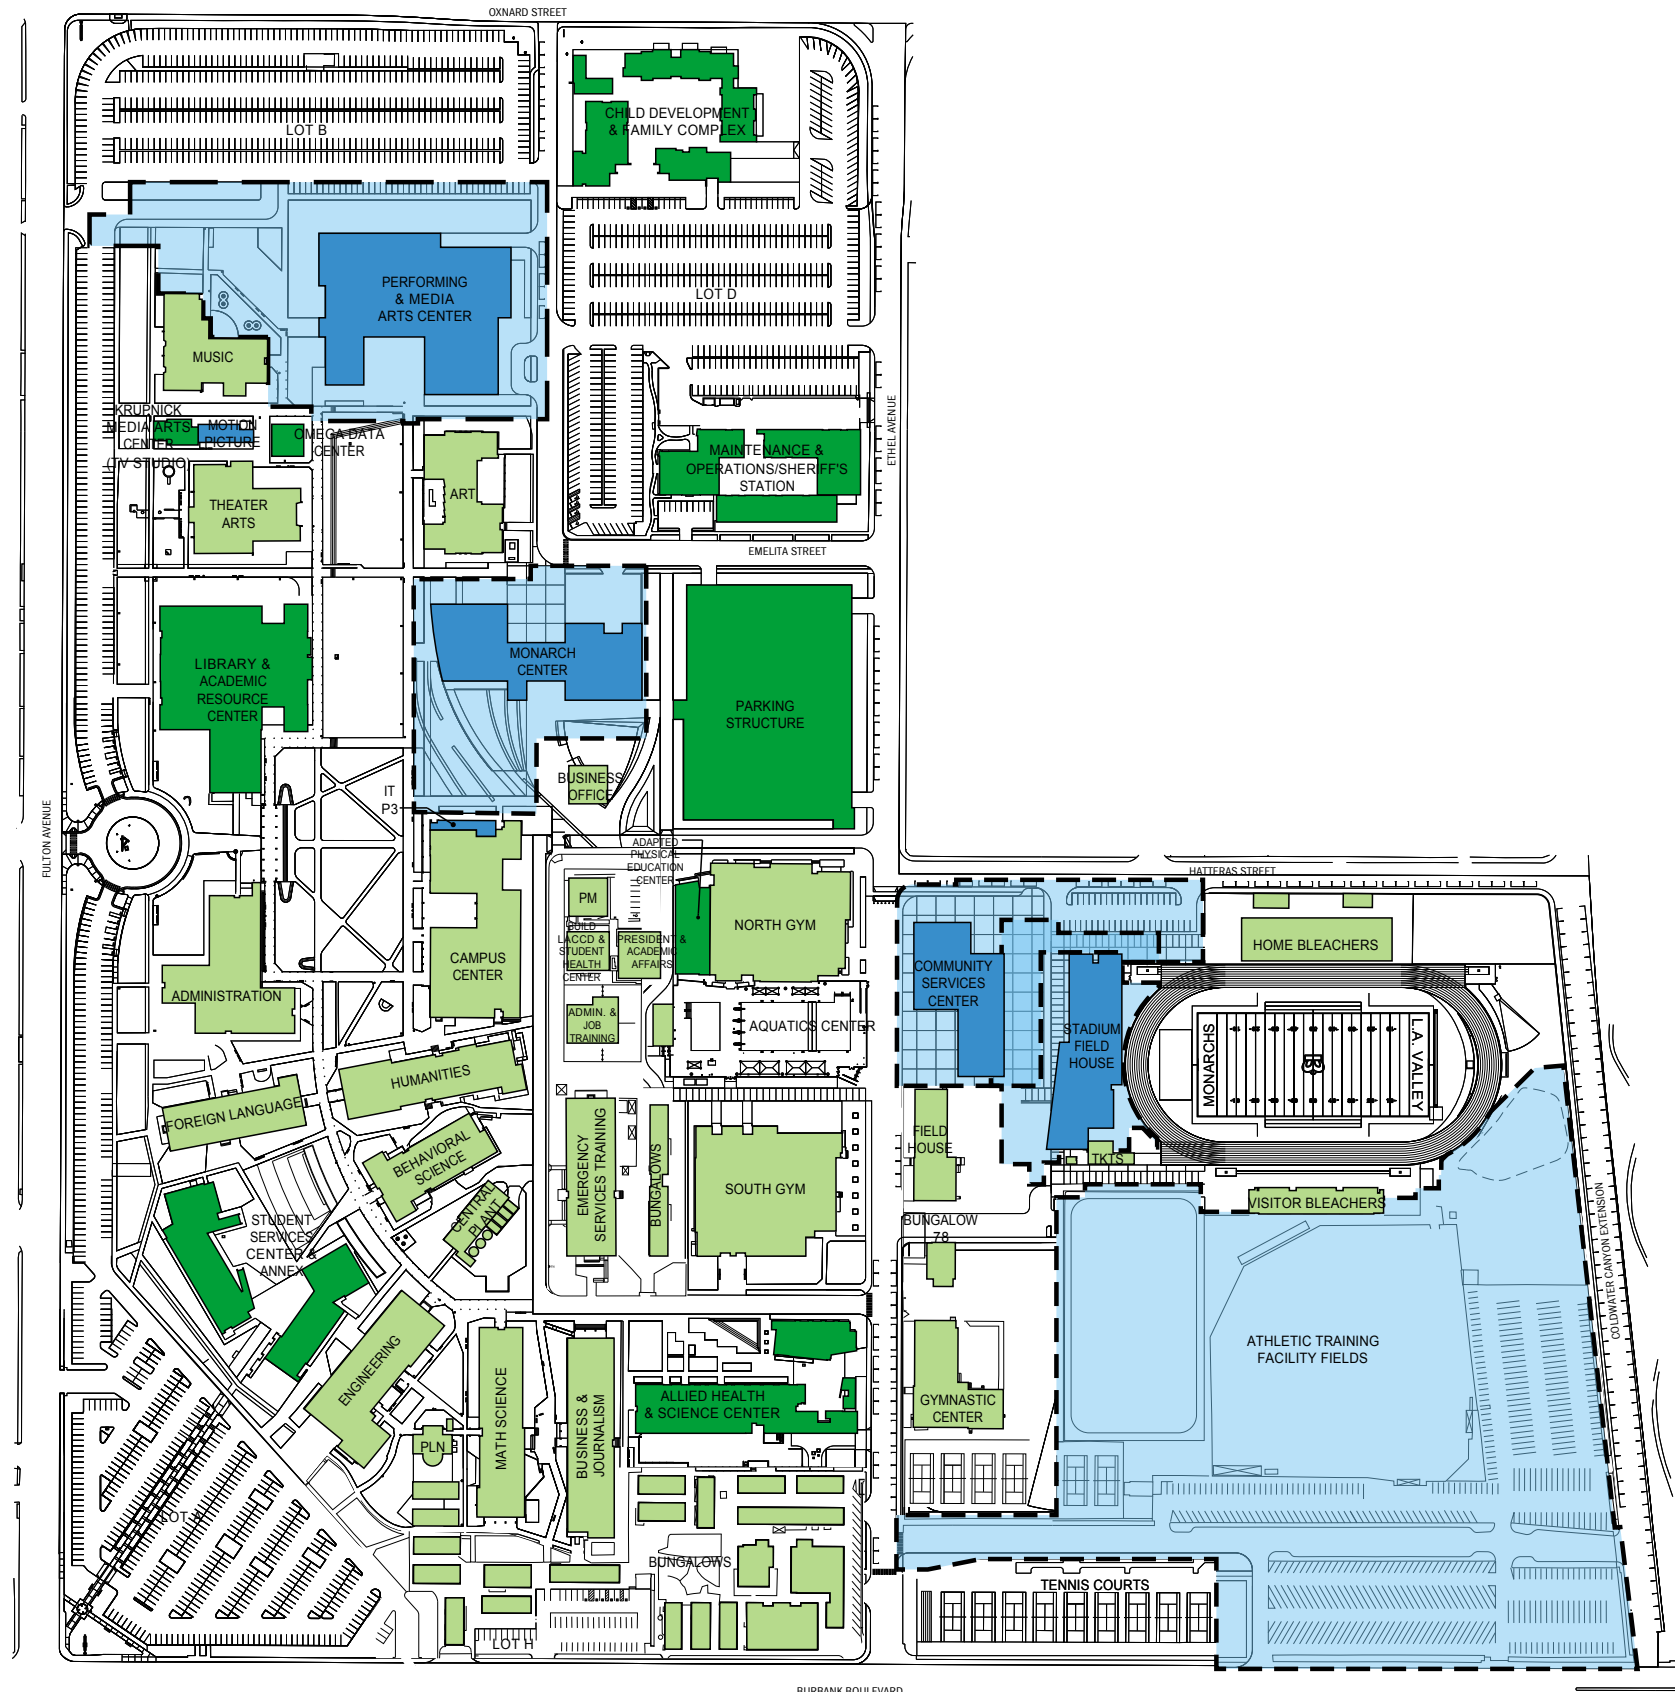

Legend

- Existing Building
- New Building / Major Renovation
- Area Under Construction
- Building To Be Demolished Or Relocated







JUL - AUG - SEP

Q3/2014

Project Status

- Vacate Admin (not shown)
- Demo Administration Building / Valley Glen Gateway Construction Begins
- Demo Bungalows 9, 10, 11, 12 / Planetarium Expansion Construction Begins
- Infrastructure Upgrades Begin
- Performing & Media Arts Center Construction Ongoing
- Central Plant & Utility Infrastructure (TES Tank) Upgrades Construction Ongoing
- Stadium Field House Construction Ongoing
- Gymnasium & Pool Phase II Construction Ongoing (not shown)
- Community Services Center Site Improvements Ongoing
- Monarch Center Construction Completed
- IT Phase 3 Construction Completed
- Motion Picture Renovation Construction Completed
- ADA Upgrades & Allied Health Services Corrective Construction - Phase 2 Completed (not shown)
- Athletic Training Facility Fields Construction Completed

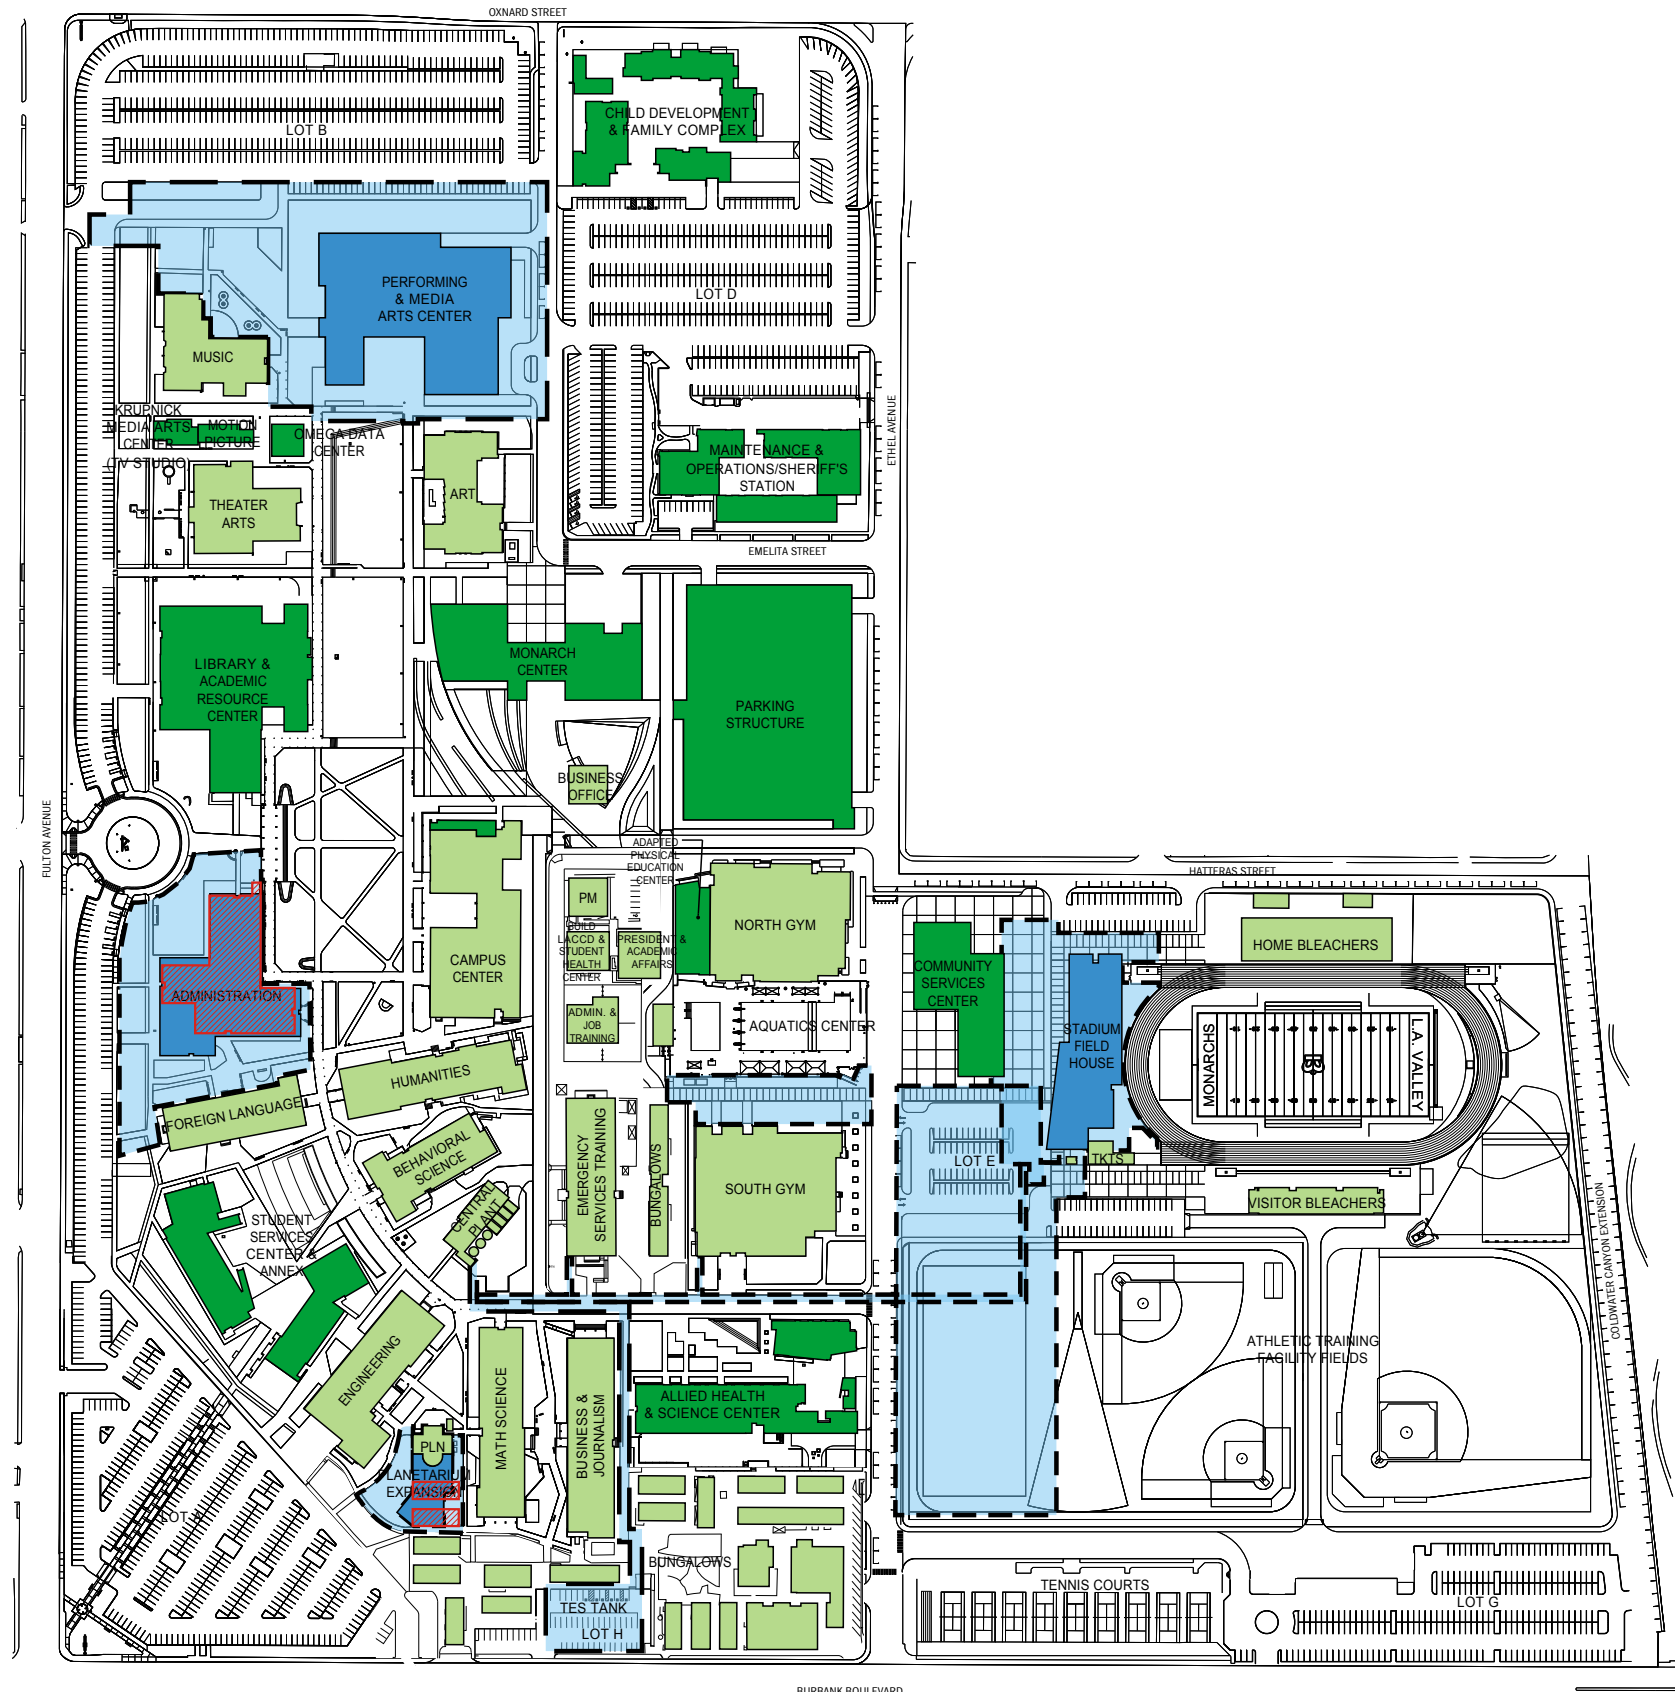

Legend


- Existing Building
- New Building / Major Renovation
- Area Under Construction
- Building To Be Demolished Or Relocated

OCT - NOV - DEC

Q4/2014


Project Status

- ADA Upgrades - Phase 3 Begins (not shown)
- Demo Business Office
- Monarch Center Site Work Completion Begins
- Performing & Media Arts Center Construction Ongoing
- Valley Glen Gateway Building Construction Ongoing
- Stadium Field House Construction Ongoing
- Central Plant & Utility Infrastructure (TES Tank) Upgrades Construction Ongoing
- Planetarium Expansion Construction Ongoing
- Gymnasium & Pool Phase II Construction Completed (not shown)
- Community Services Center Site Construction Completed
- Infrastructure Upgrades Completed (not shown)

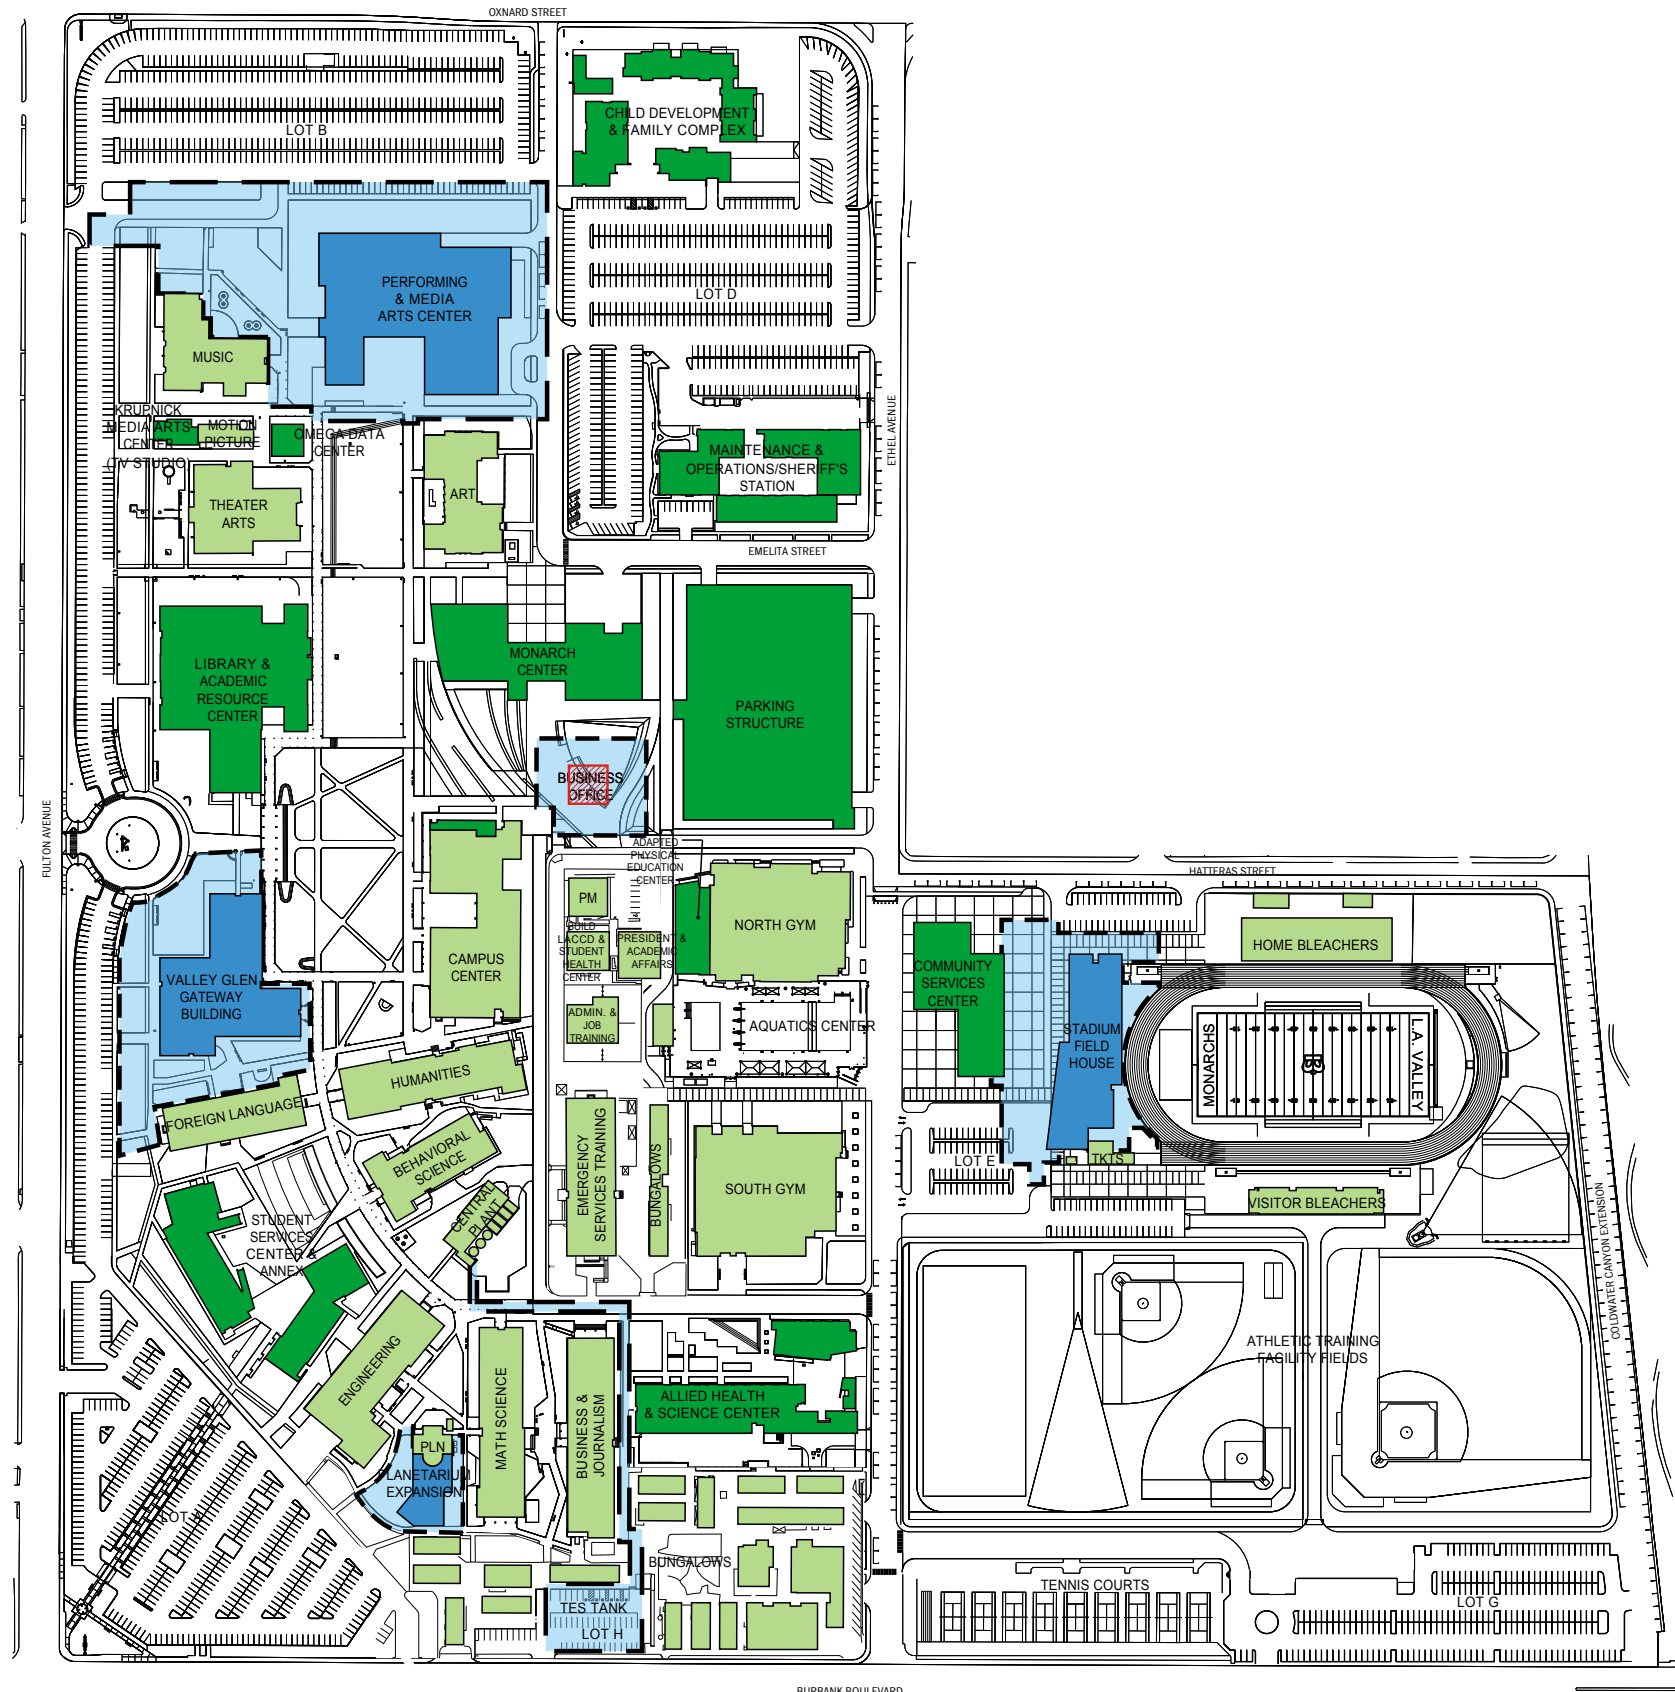

Legend

- Existing Building
- New Building / Major Renovation
- Area Under Construction
- Building To Be Demolished Or Relocated




JAN - FEB - MAR

Q1/2015


Project Status

- Performing & Media Arts Center Construction Ongoing
- Valley Glen Gateway Building Construction Ongoing
- ADA Upgrades - Phase 3 Ongoing (not shown)
- Central Plant & Utility Infrastructure (TES Tank) Upgrades Construction Ongoing
- Planetarium Expansion Construction Ongoing
- Stadium Field House Construction Completed
- Monarch Center Site Improvements Completed

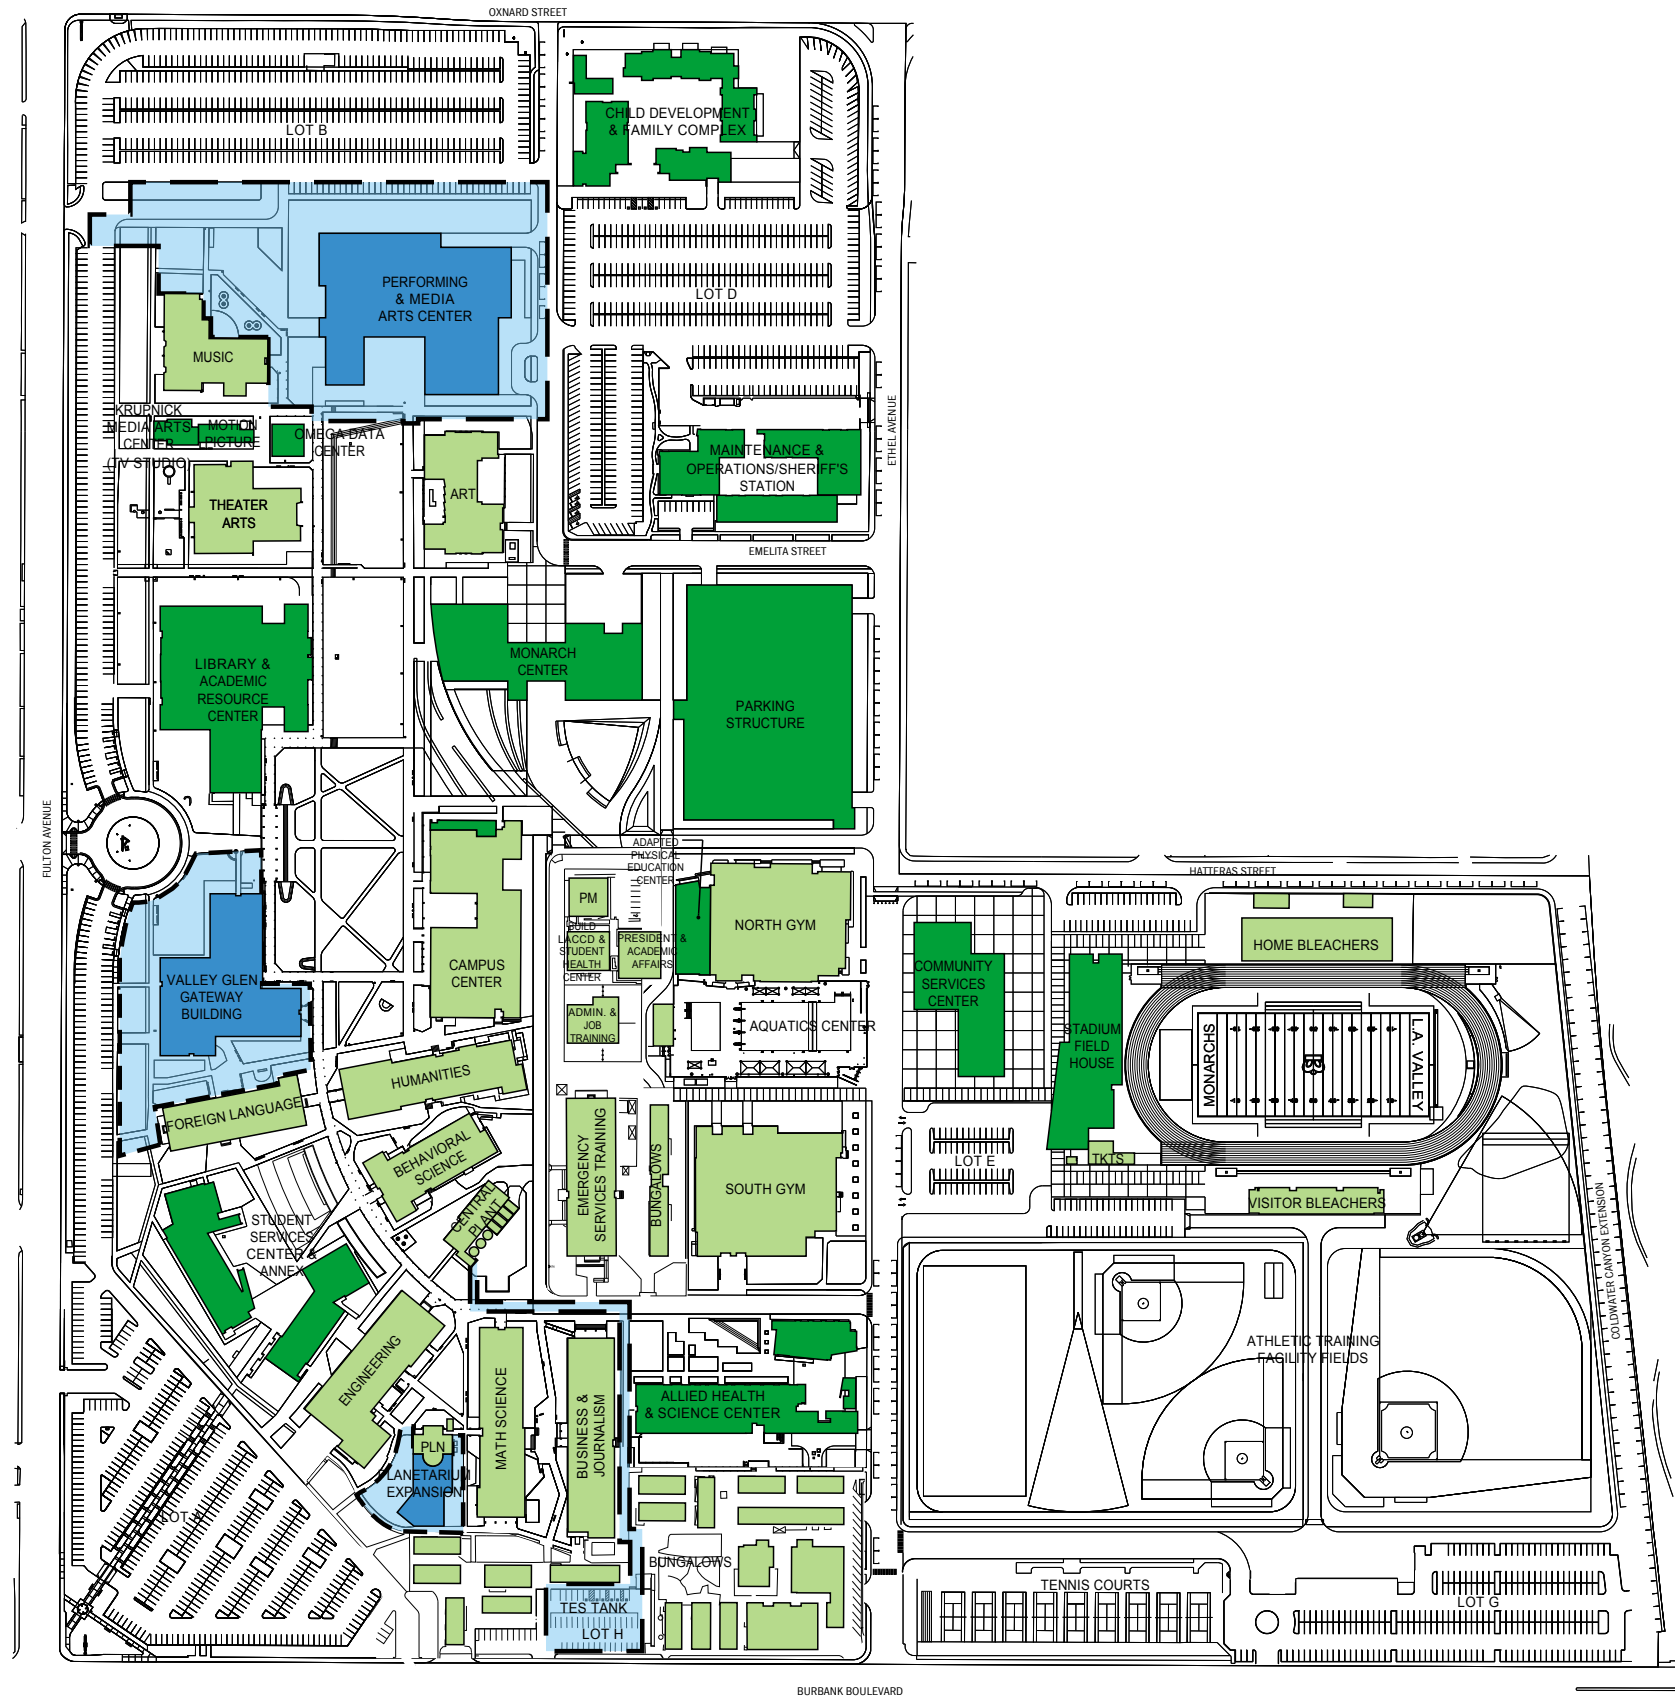

Legend

- Existing Building
- New Building / Major Renovation
- Area Under Construction
- Building To Be Demolished Or Relocated




APR - MAY - JUN

Q2/2015


Project Status

- Performing & Media Arts Center Construction Ongoing
- Valley Glen Gateway Building Construction Ongoing
- ADA Upgrades - Phase 3 Ongoing (not shown)
- Planetarium Expansion Construction Ongoing
- Central Plant & Utility Infrastructure (TES Tank) Upgrades Construction Completed (not shown)

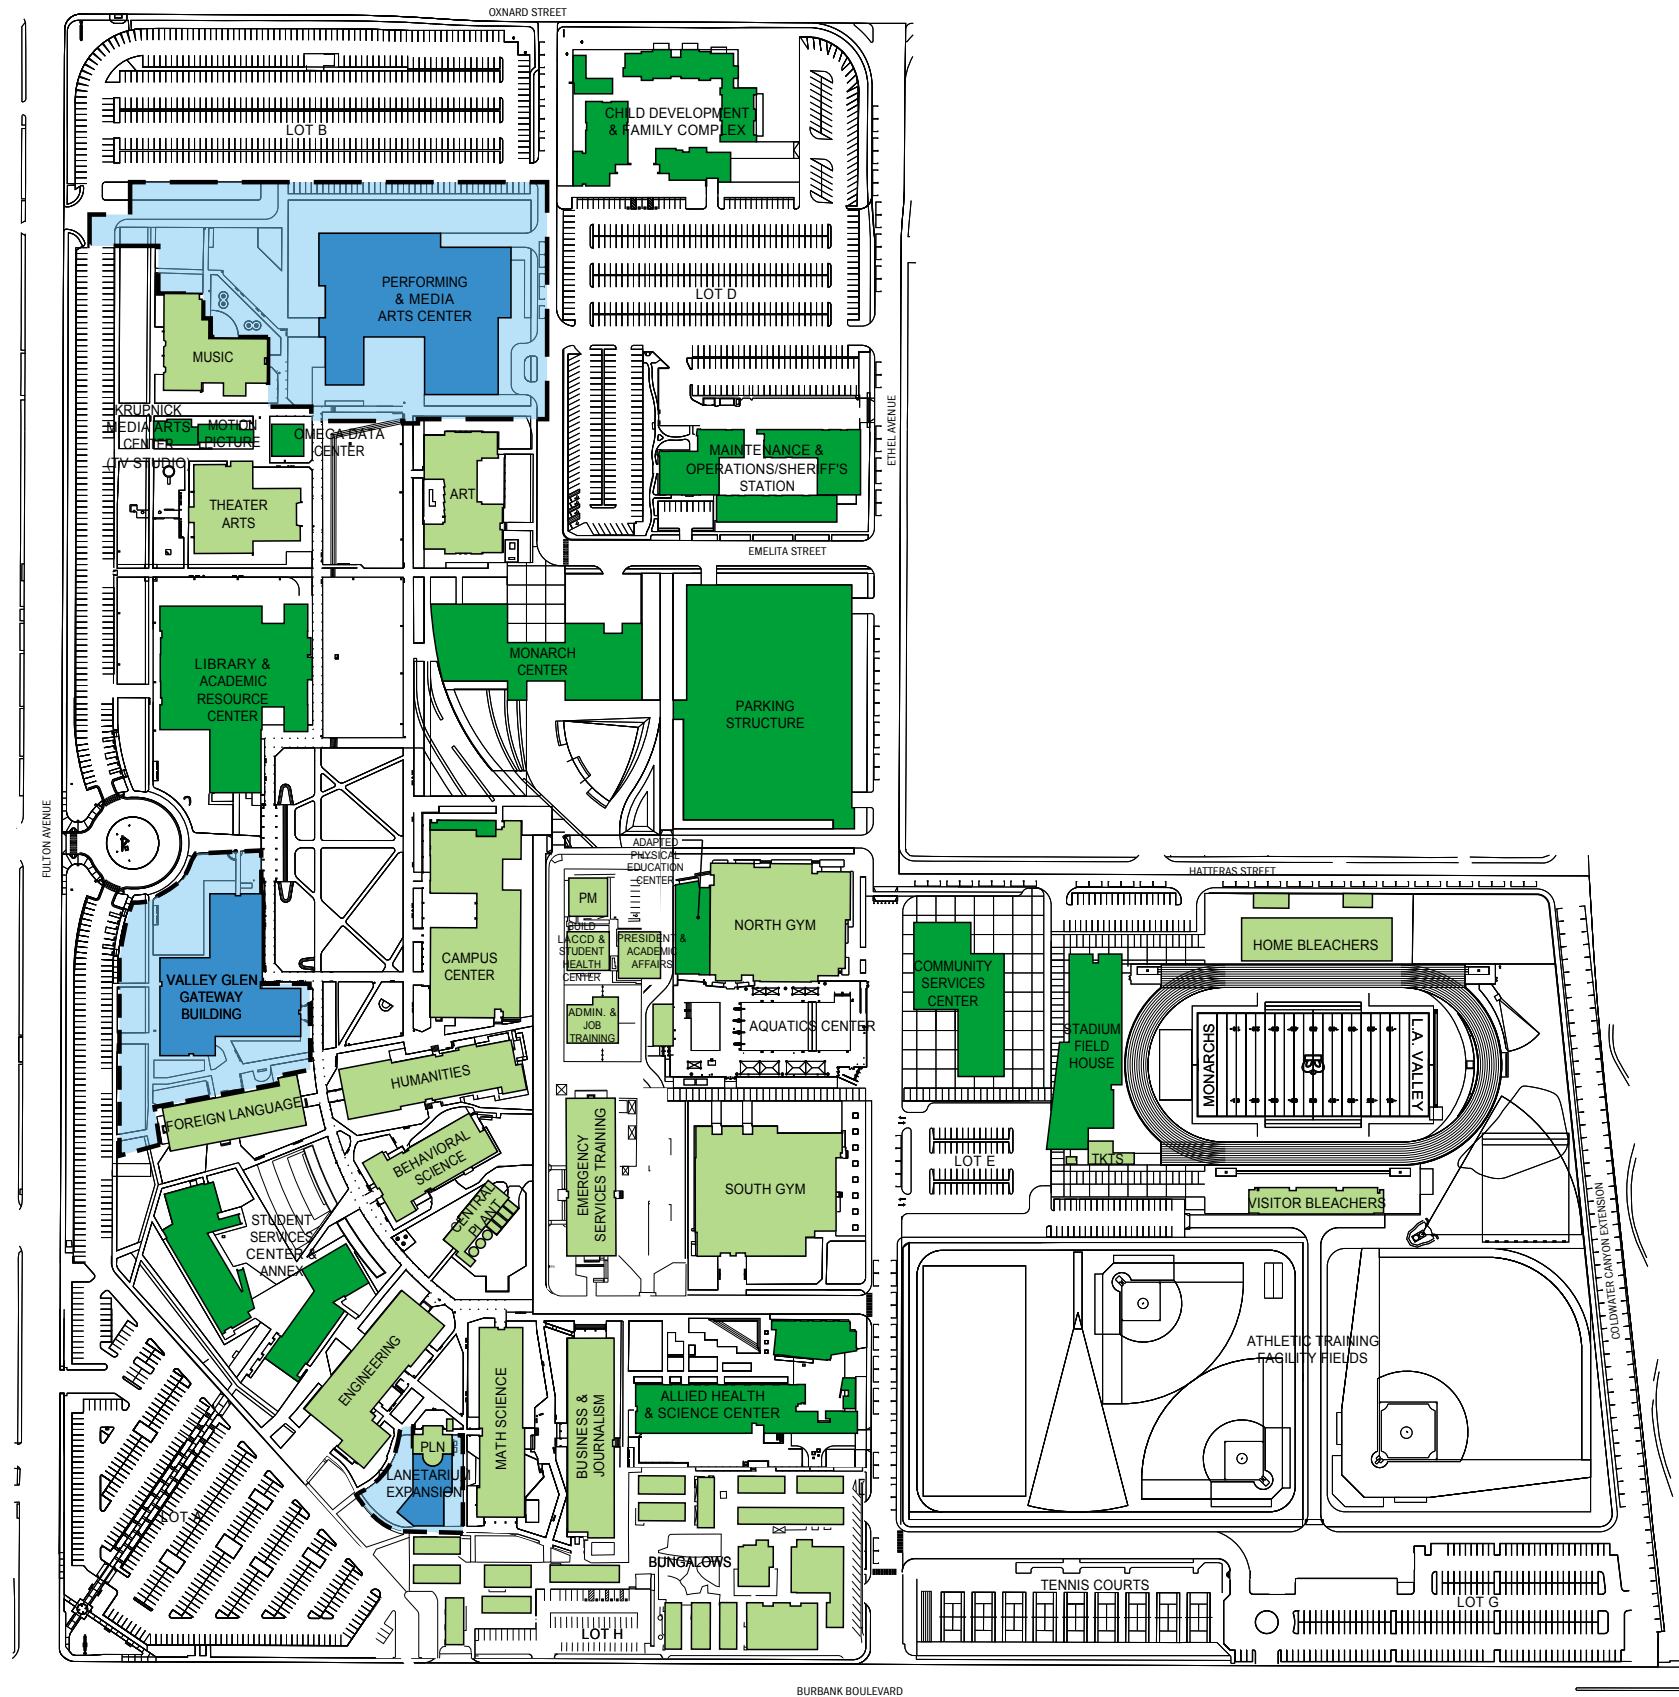

Legend

- Existing Building
- New Building / Major Renovation
- Area Under Construction
- Building To Be Demolished Or Relocated




JUL - AUG - SEP

Q3/2015


Project Status

- Parking Lot B Construction Begins
- Performing & Media Arts Center Construction Ongoing
- Valley Glen Gateway Building Construction Ongoing
- Planetarium Expansion Construction Ongoing
- ADA Upgrades - Phase 3 Completed (not shown)

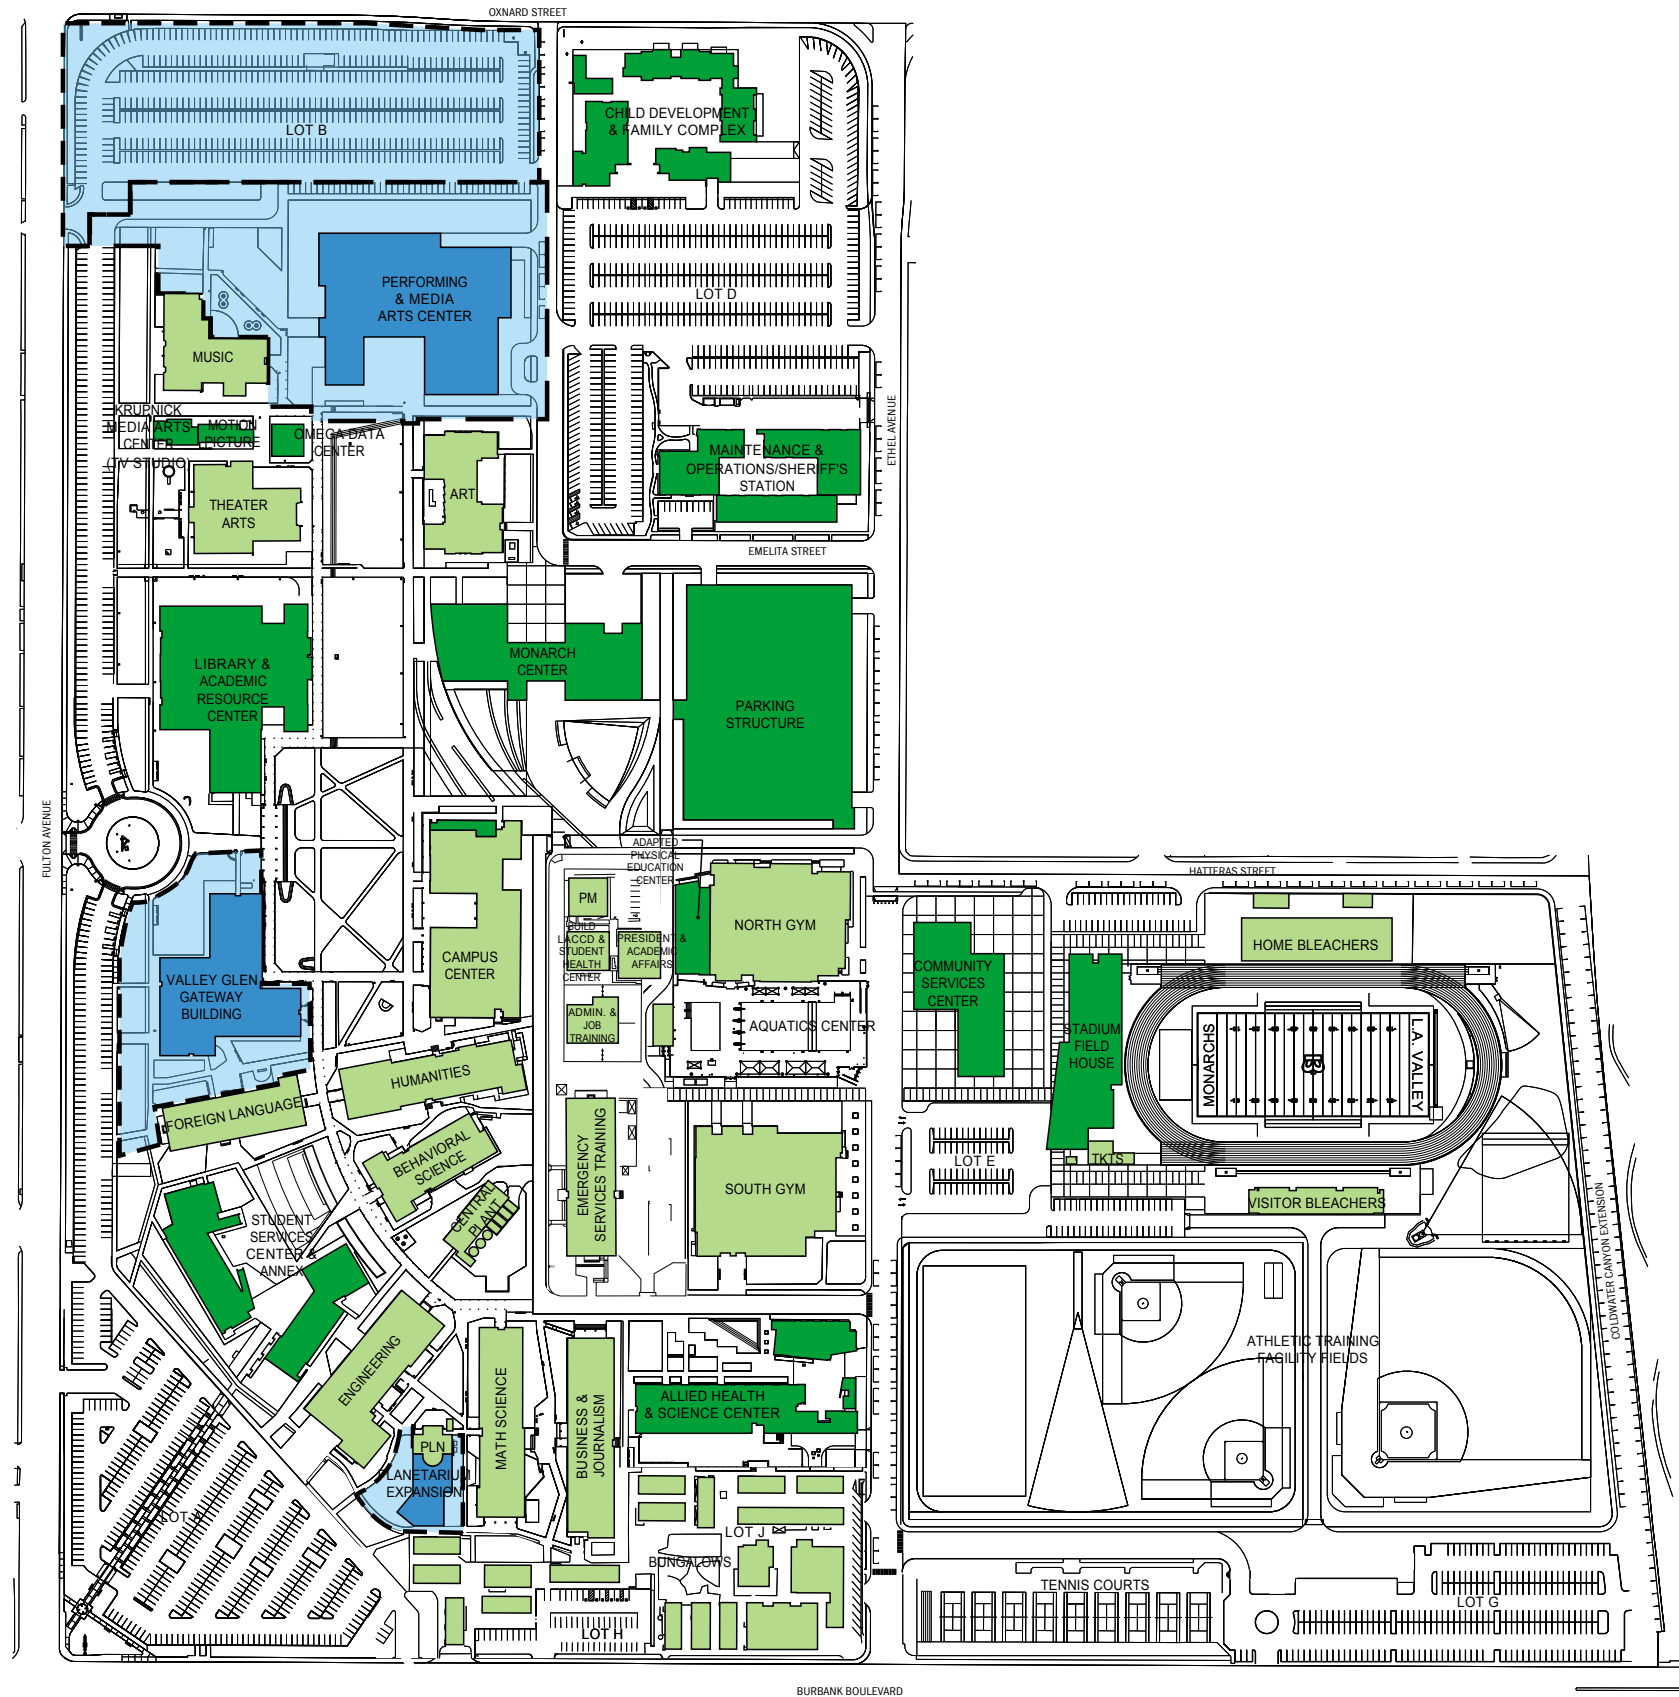

Legend

- Existing Building
- New Building / Major Renovation
- Area Under Construction
- Building To Be Demolished Or Relocated




OCT - NOV - DEC

Q4/2015


Project Status

- Performing & Media Arts Center Construction Ongoing
- Parking Lot B Construction Ongoing
- Planetarium Expansion Construction Completed
- Valley Glen Gateway Building Construction Completed

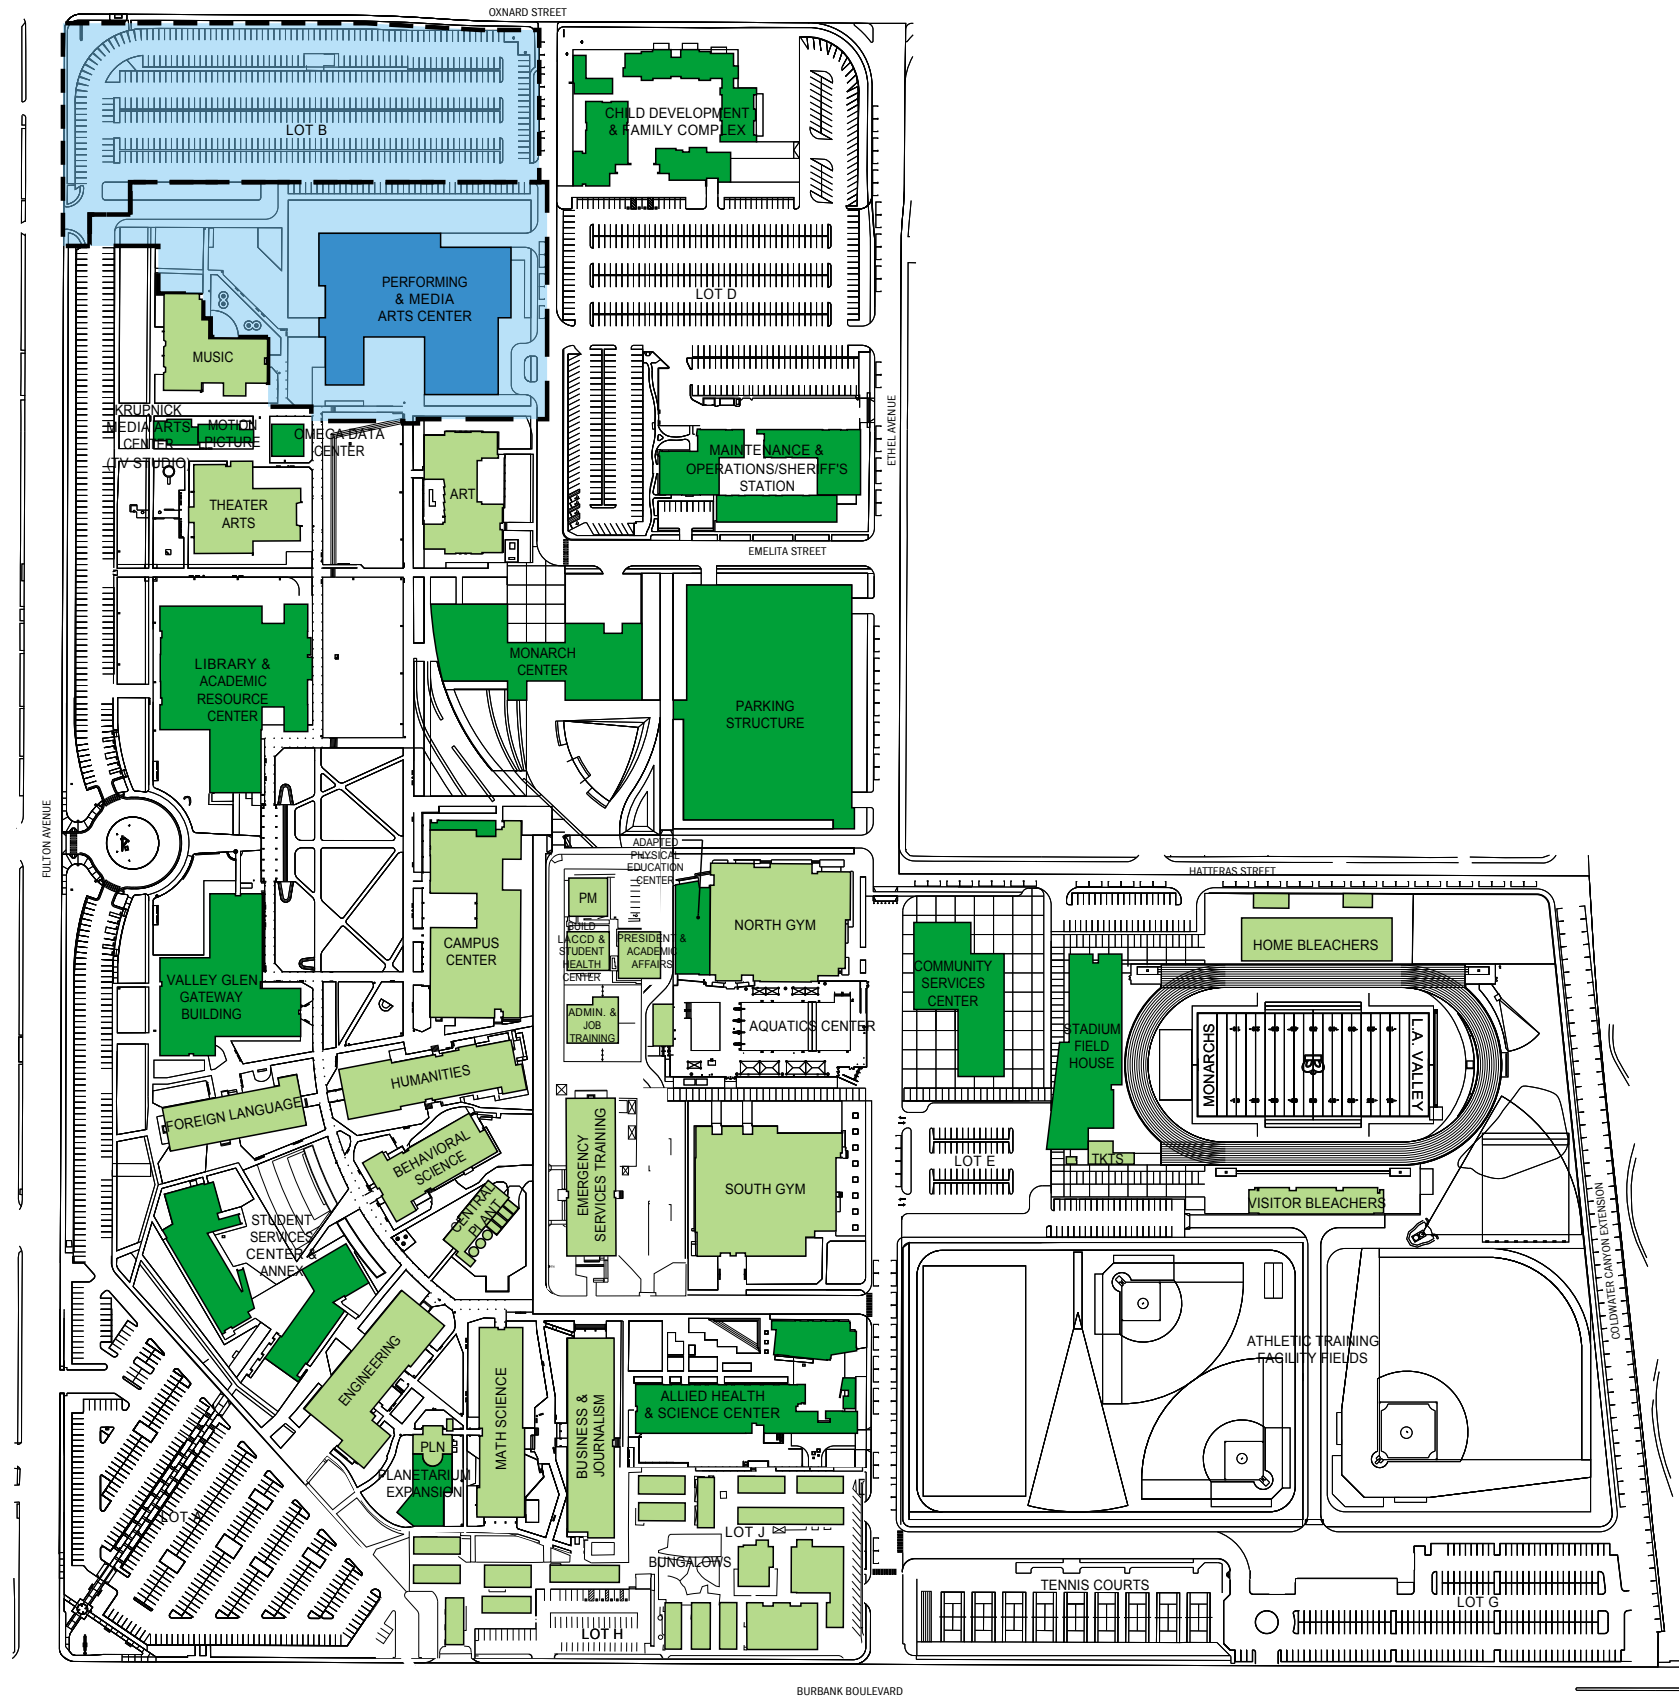

Legend

- Existing Building
- New Building / Major Renovation
- Area Under Construction
- Building To Be Demolished Or Relocated




JAN - FEB - MAR

Q1/2016


Project Status

- Campus Center Renovations Ph.1 (Admin Swing Space) Begins
- Demo Financial Aid, CSIT, CPM, Bungalows 82 - 86, Temp. LRC
- Stormwater Management (Sustainable Mall) Construction Begins
- Demo Bungalows Begins
  
- Parking Lots H & J Construction Begins
  
- Performing & Media Arts Center Construction Ongoing
- Parking Lot B Construction Ongoing

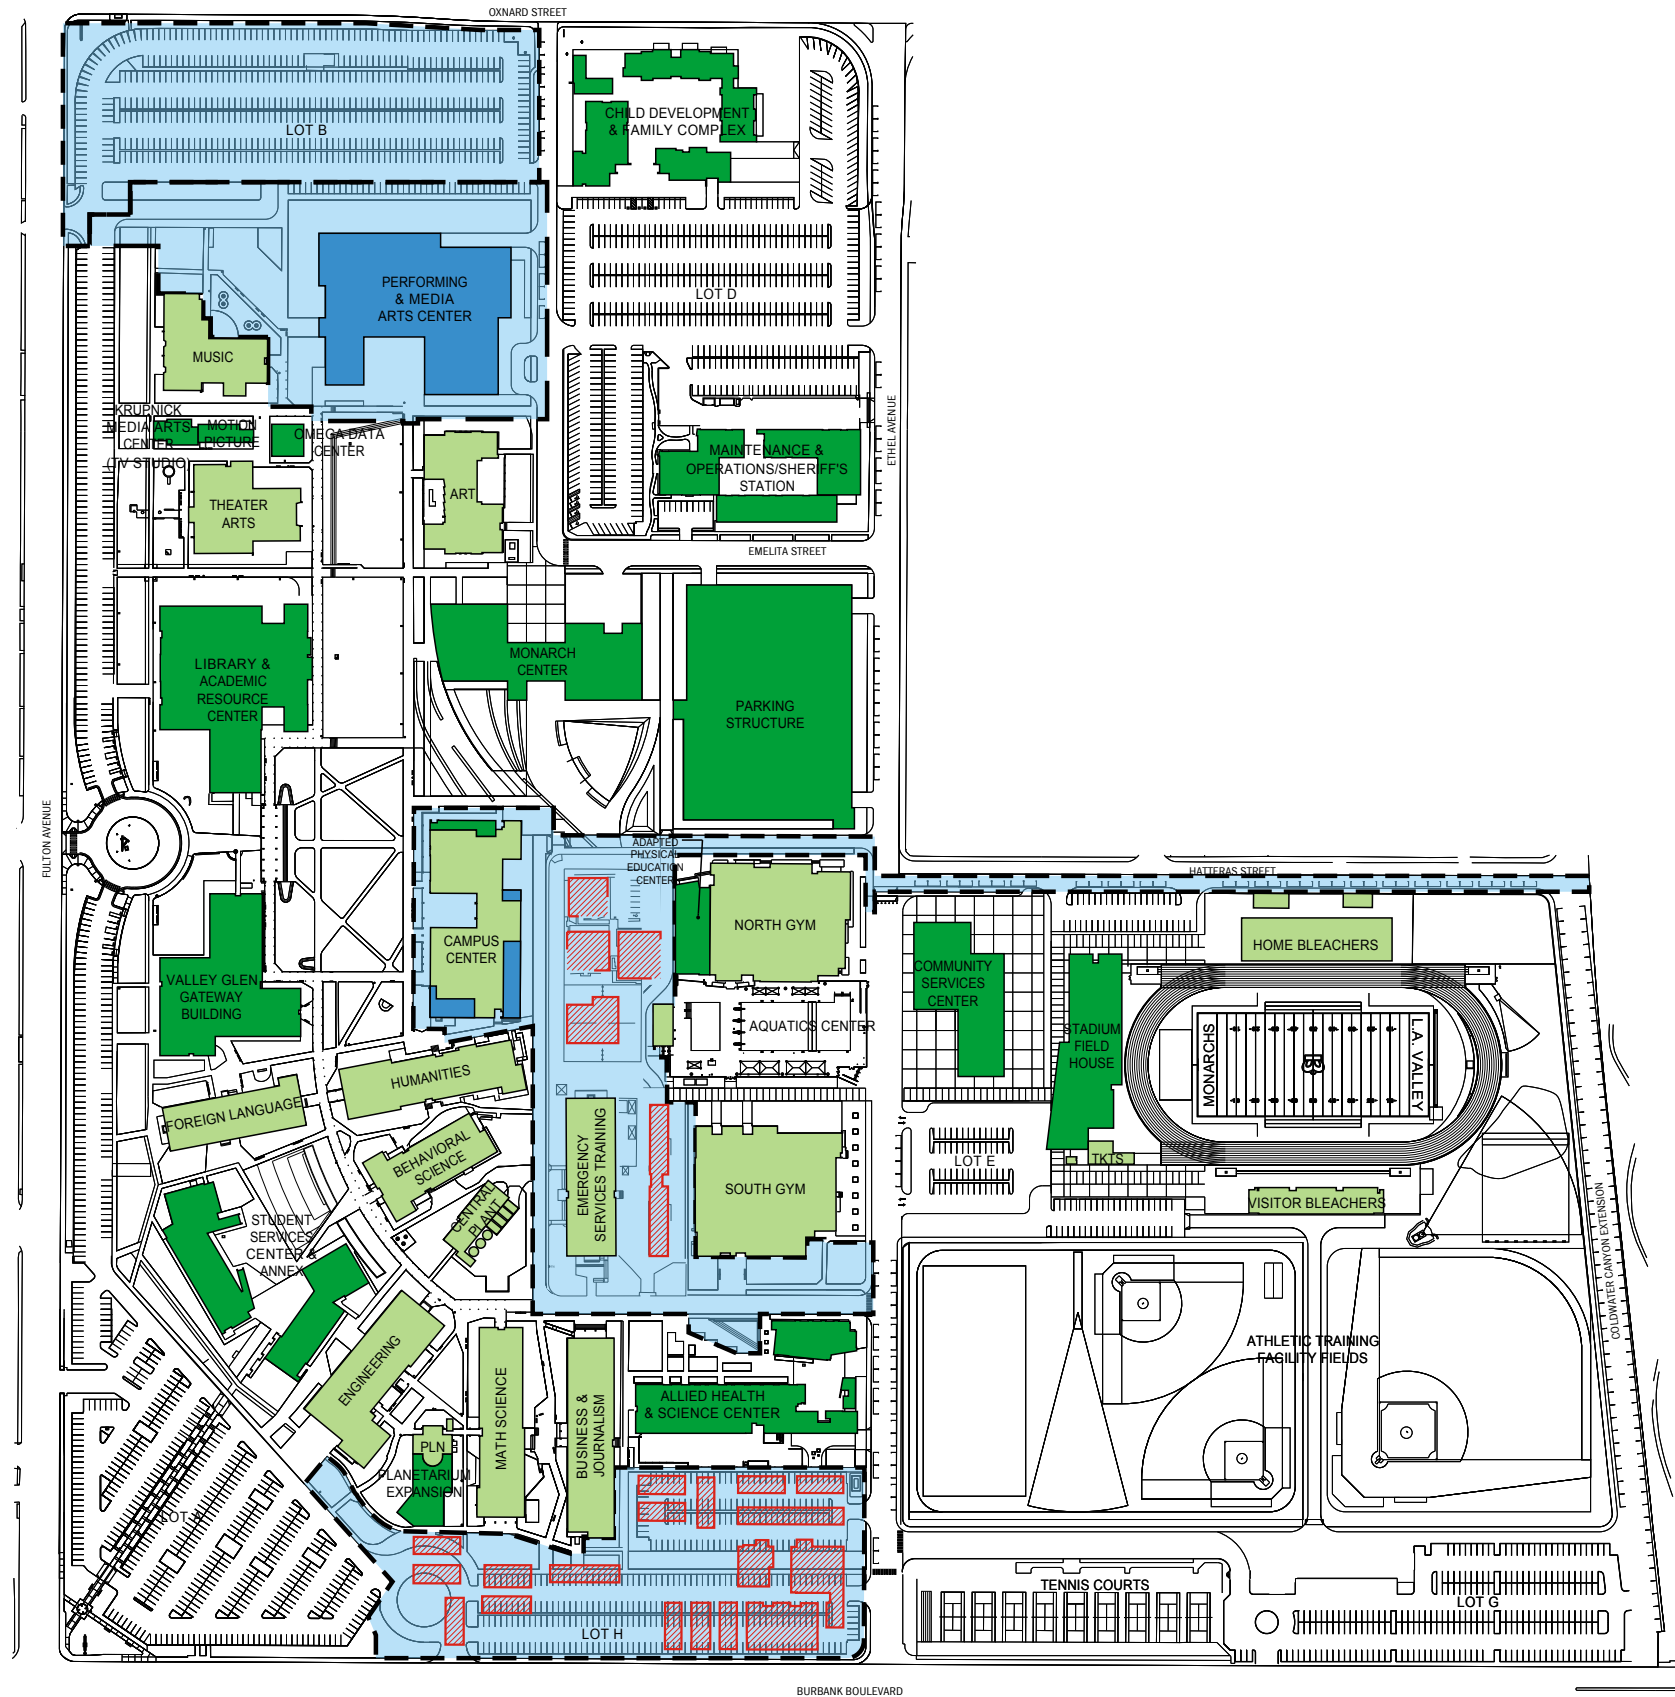

Legend

- Existing Building
- New Building / Major Renovation
- Area Under Construction
- Building To Be Demolished Or Relocated




APR - MAY - JUN

Q2/2016


Project Status

- Campus Center Renovations Ph.2 (Media Arts, Bookstore) Begins
- Demo Theater Arts/Site Repair
- Parking Lots H & J Construction Ongoing
- Performing & Media Arts Center Construction Completed
- Campus Center Renovations Ph.1 (Admin Swing Space) Completed
- Parking Lot B Construction Completed
- Stormwater Management (Sustainable Mall) Construction Completed

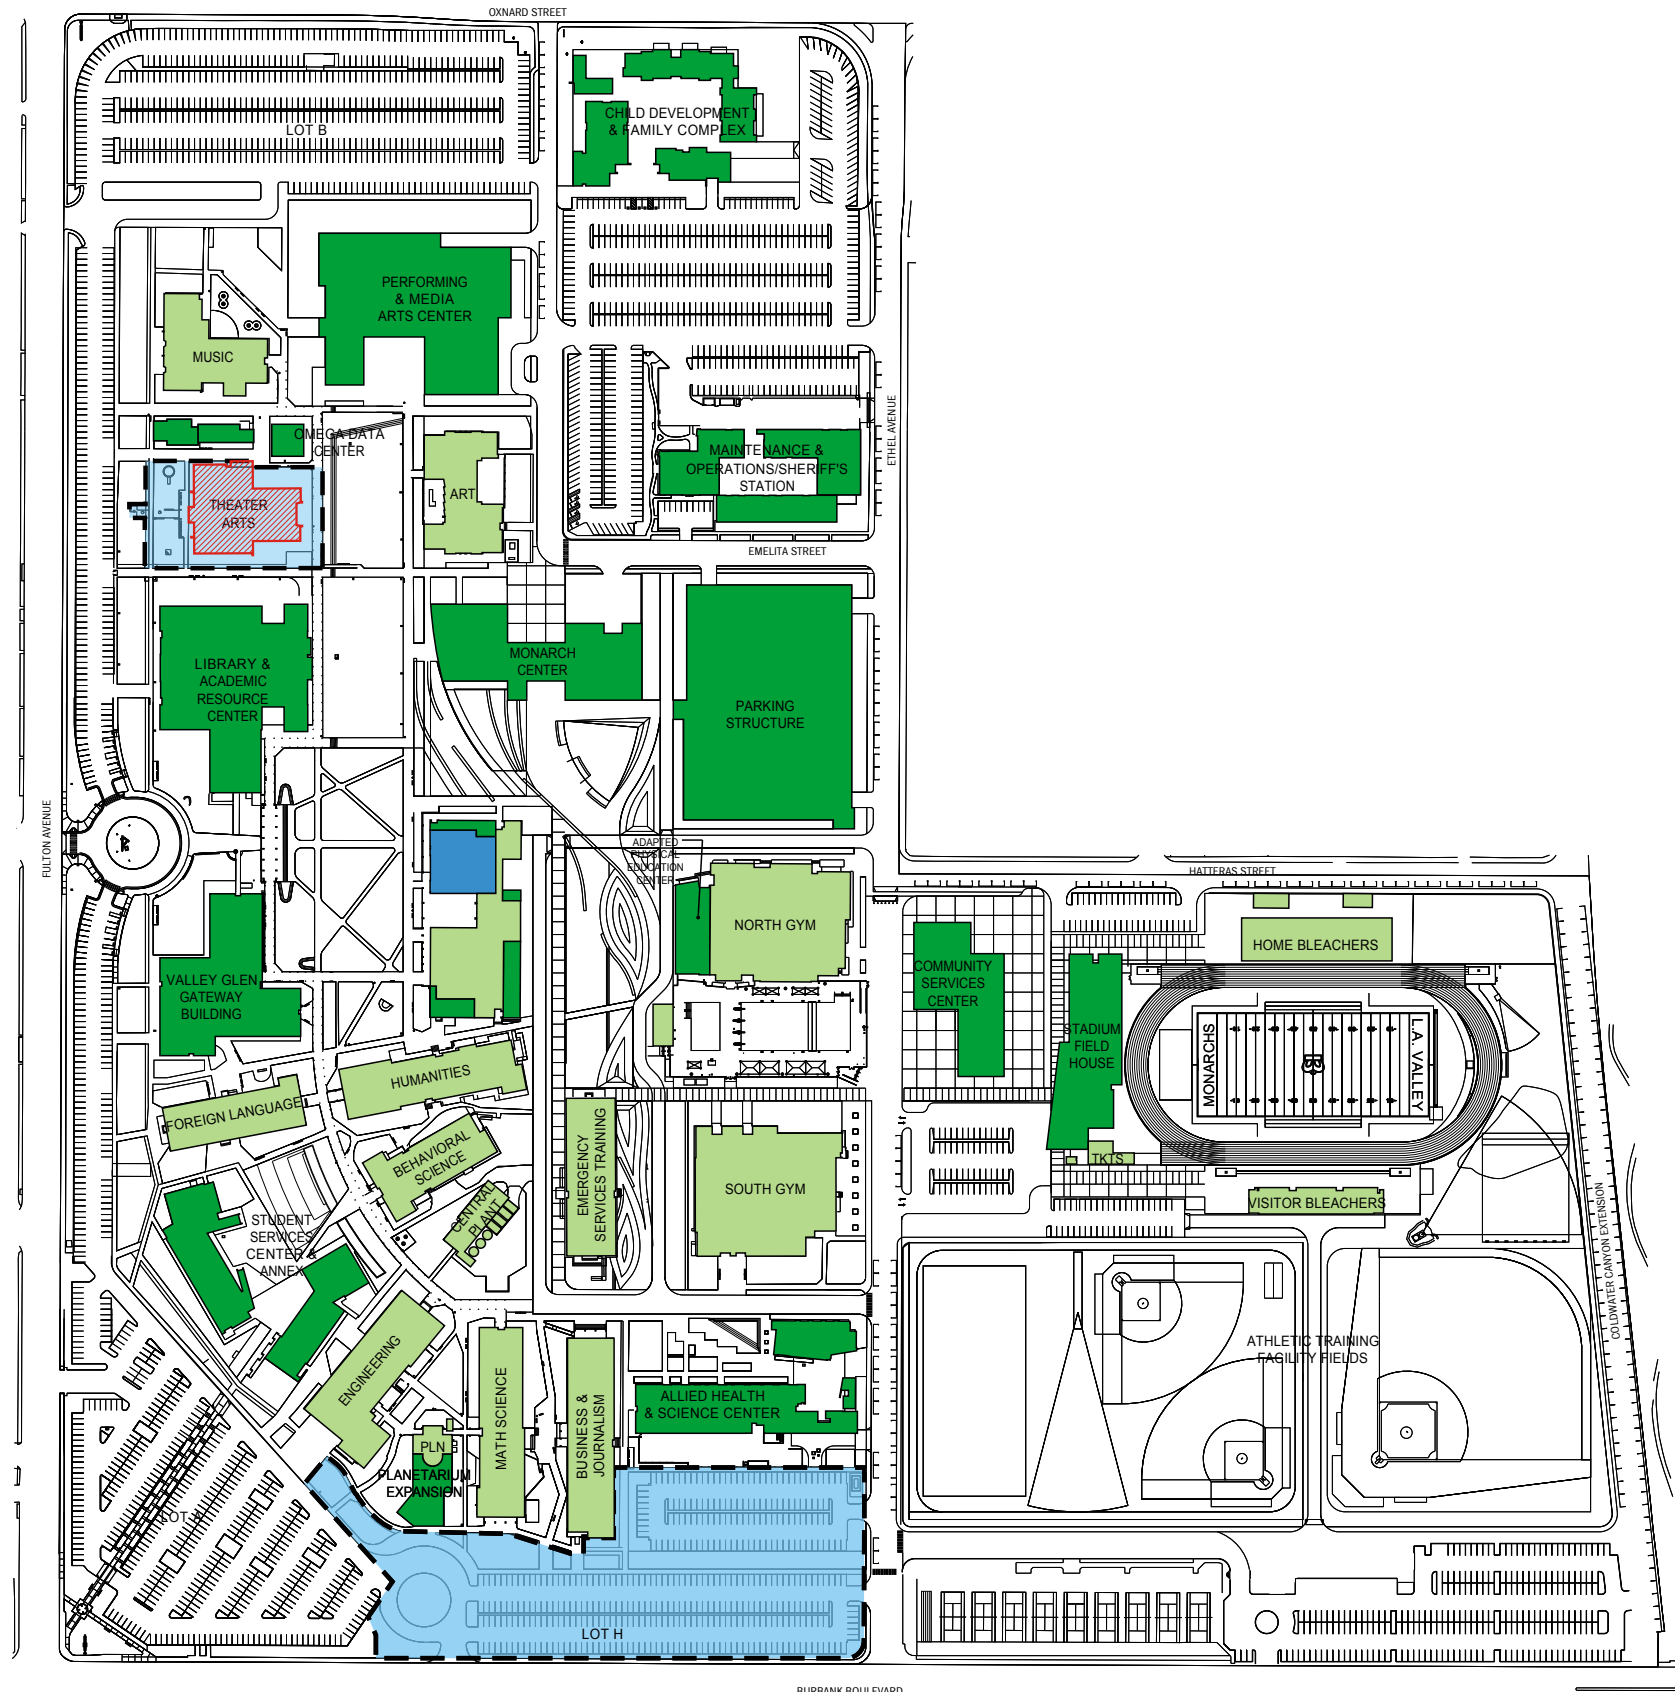

Legend

- Existing Building
- New Building / Major Renovation
- Area Under Construction
- Building To Be Demolished Or Relocated




JUL - AUG - SEP





Q3/2016

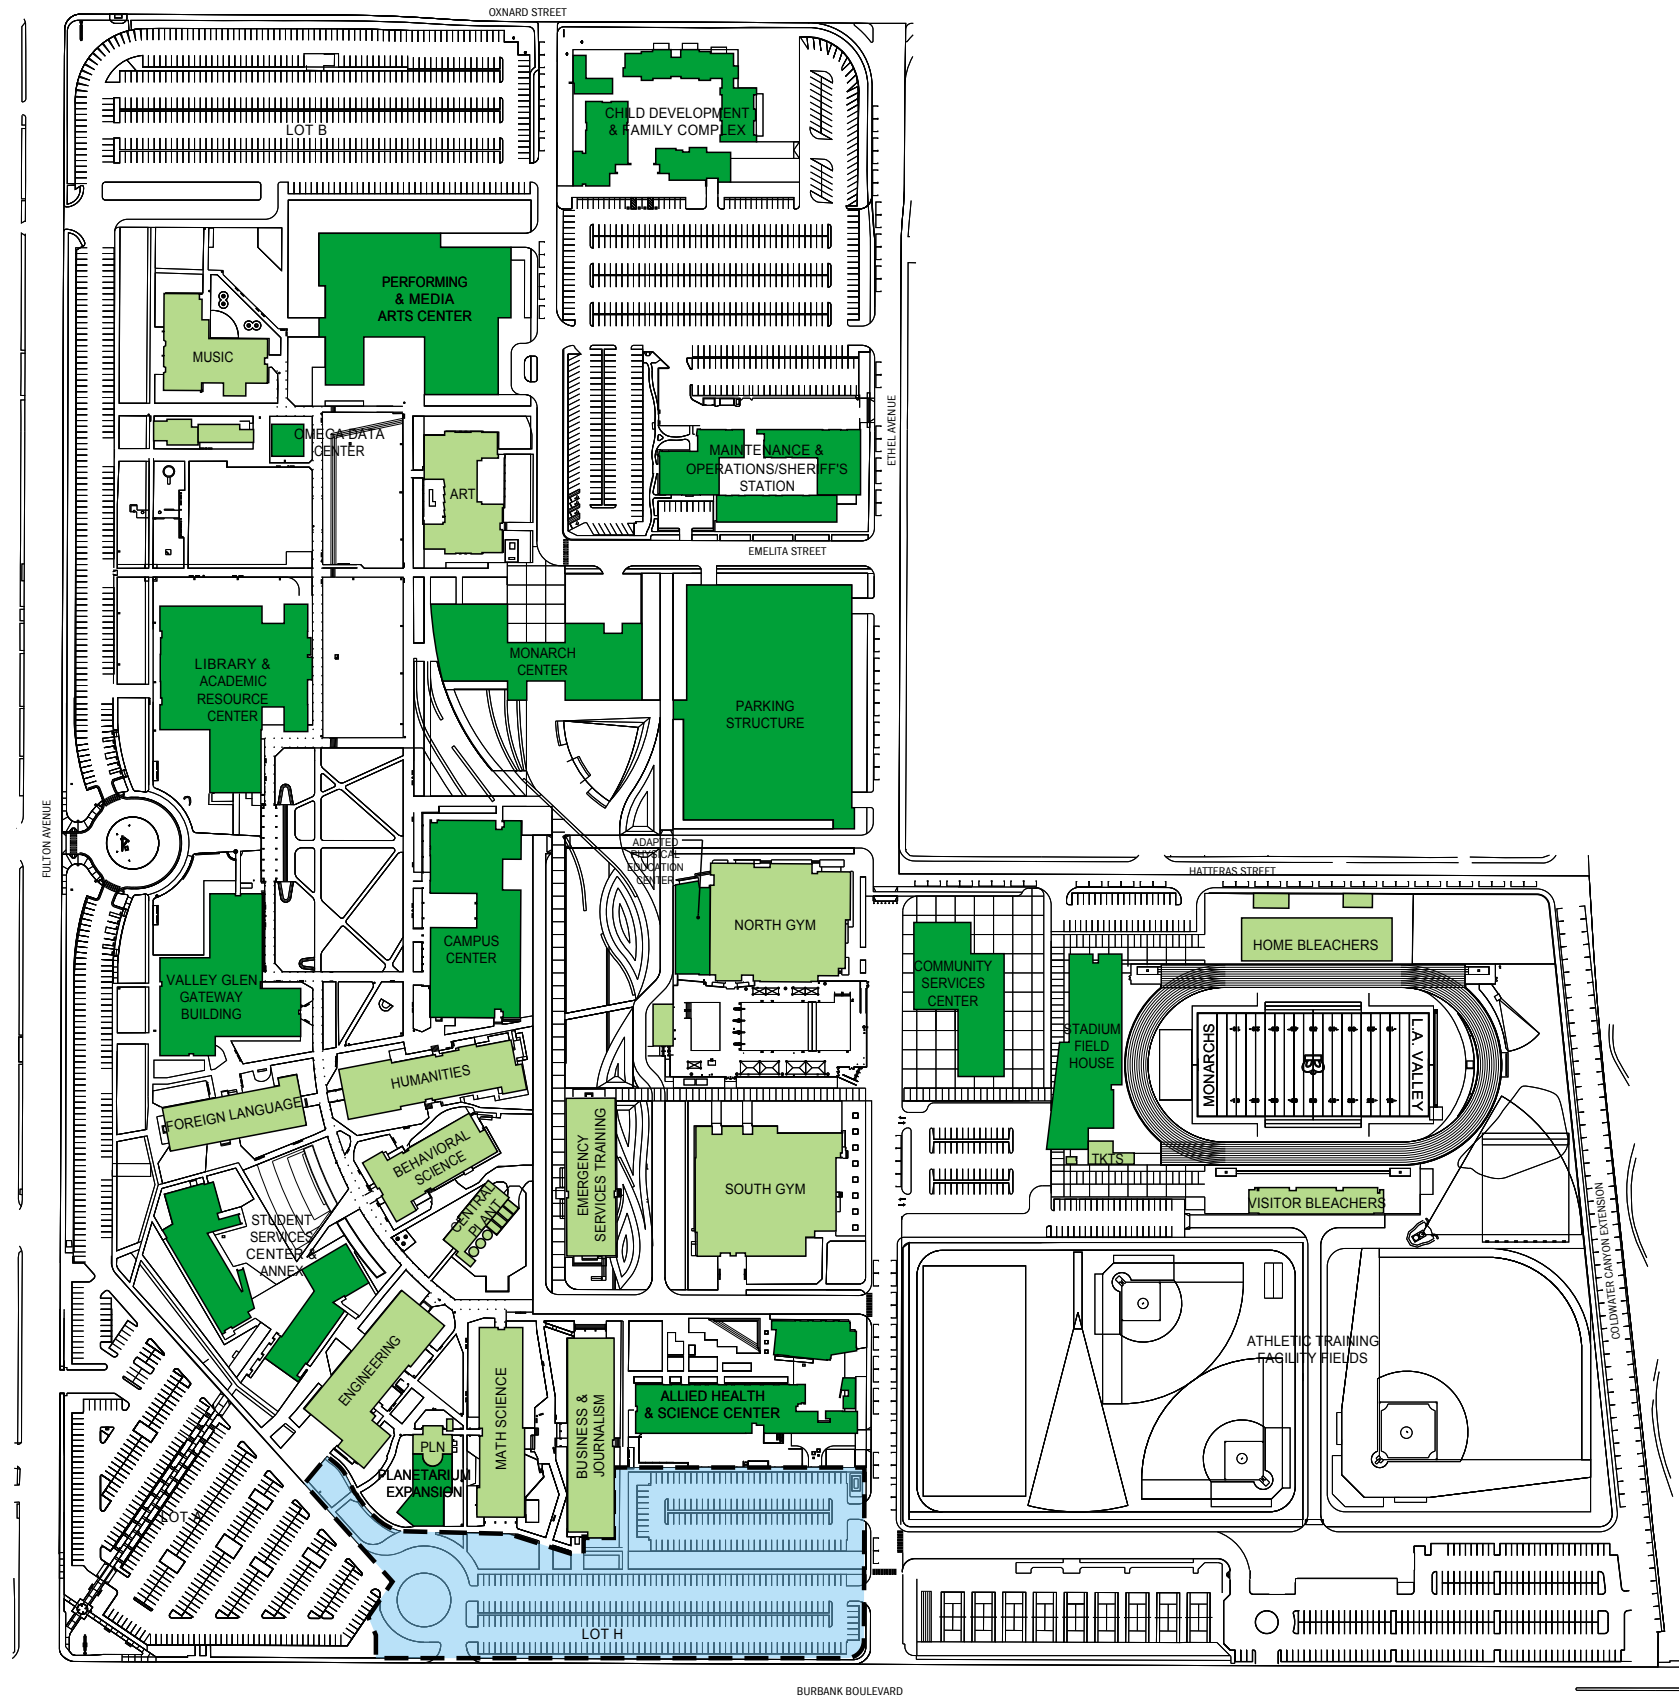
Project Status

- Parking Lots H & J Construction Ongoing
- Campus Center Renovations Ph.2 (Media Arts, Bookstore) Completed



Legend

-  Existing Building
-  New Building / Major Renovation
-  Area Under Construction
-  Building To Be Demolished Or Relocated





OCT - NOV - DEC



Q4/2016

Project Status

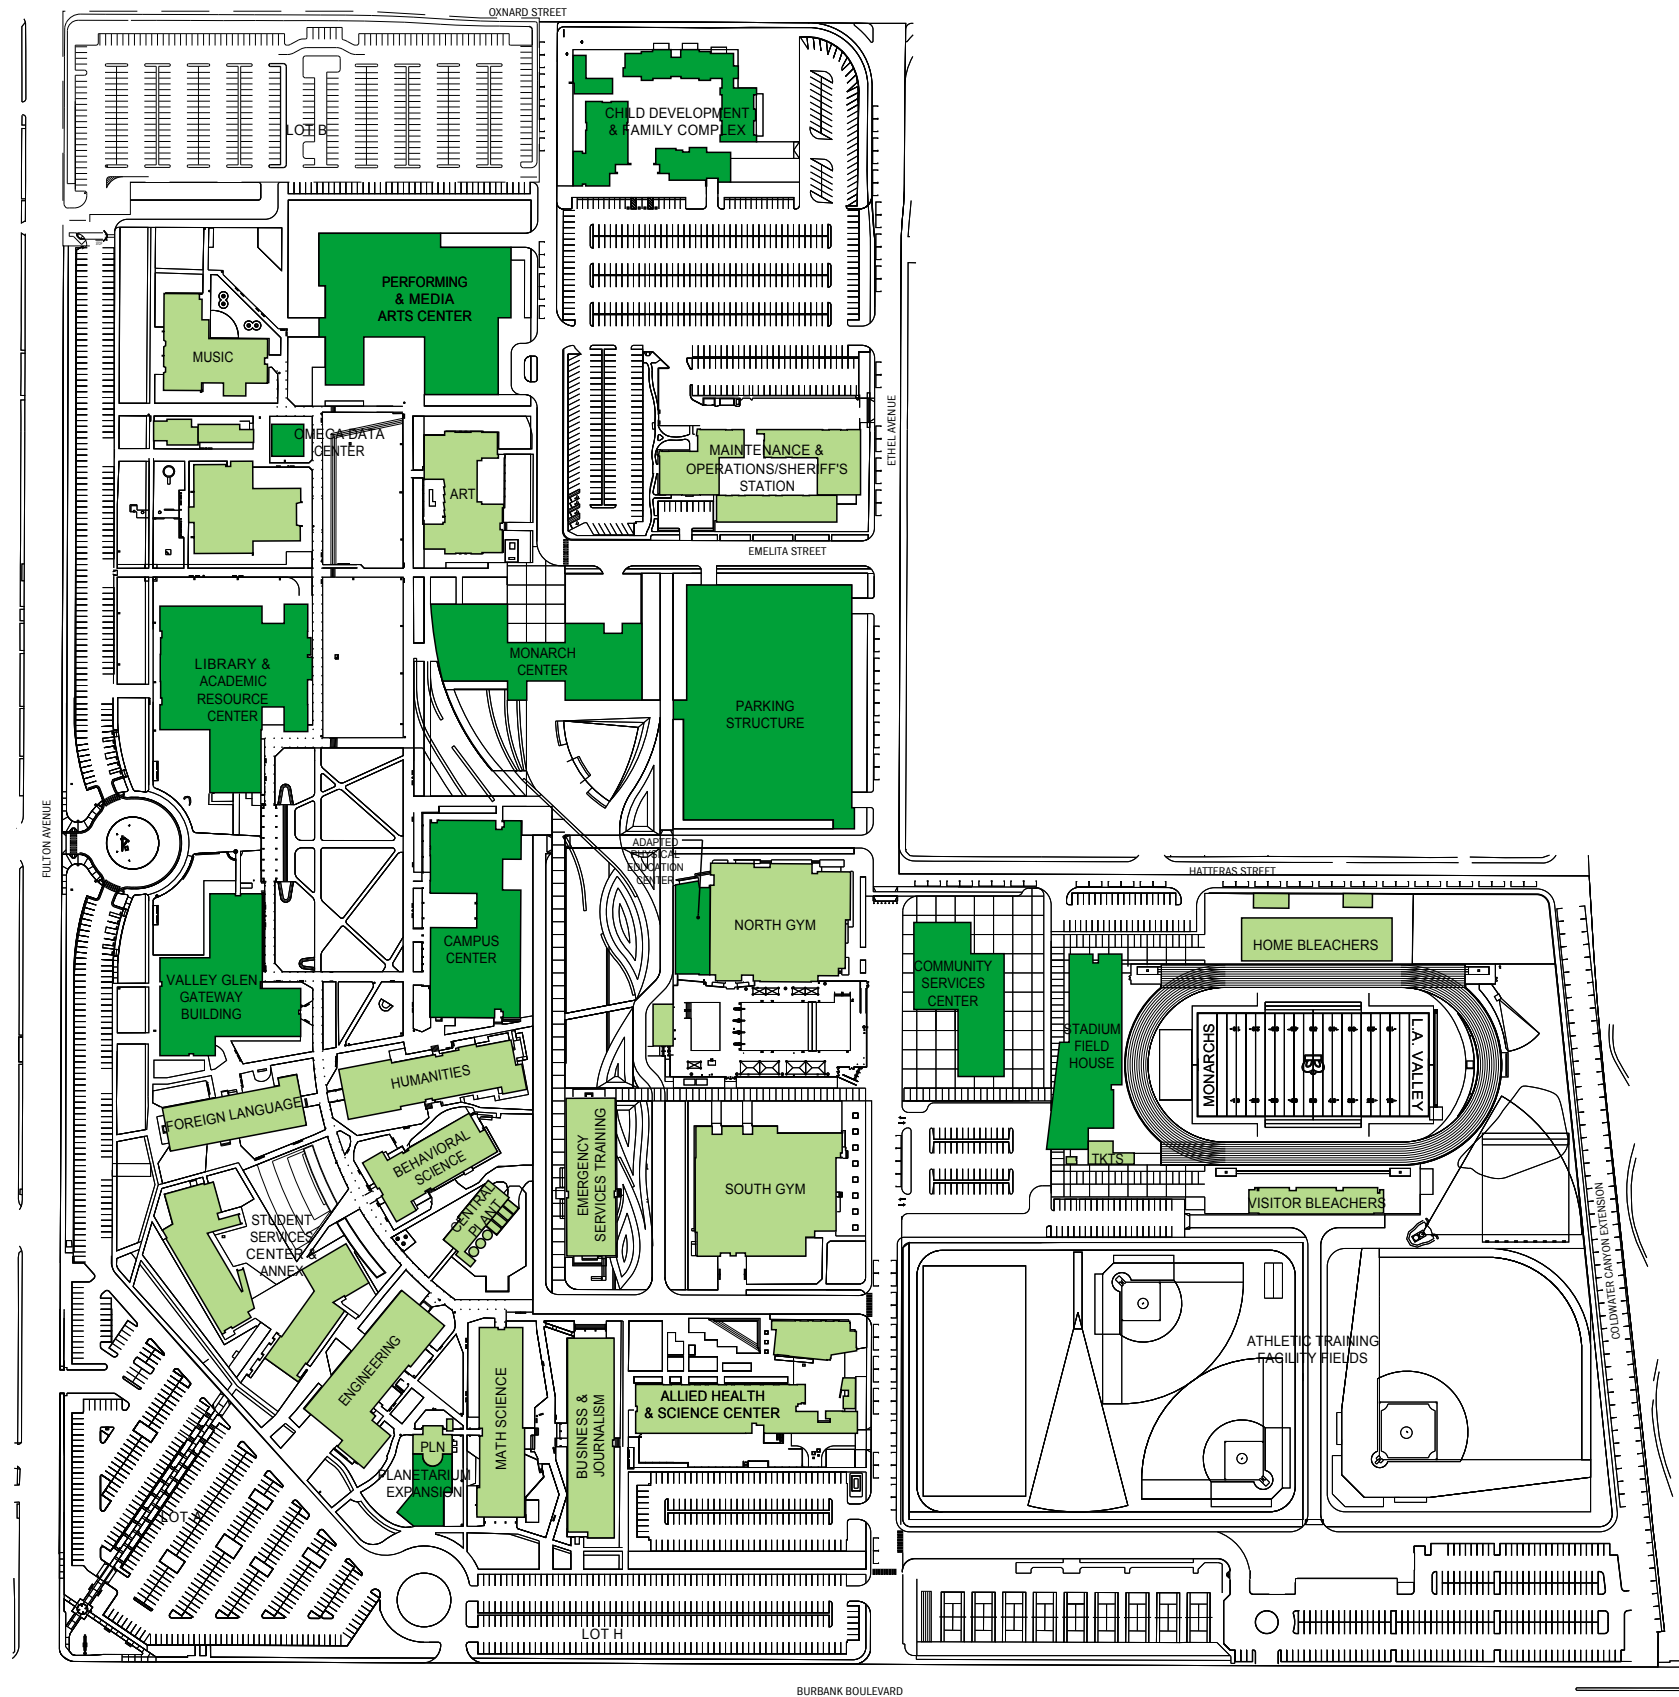- Parking Lots H & J Construction Completed



Legend

-  Existing Building
-  New Building / Major Renovation
-  Area Under Construction
-  Building To Be Demolished Or Relocated
