


An aerial photograph of the Los Angeles Valley College campus and its surrounding environment. The campus is a large, rectangular area with numerous buildings, parking lots, and green spaces. Several baseball and softball fields are visible, along with a large oval track. The campus is surrounded by a dense residential neighborhood with many houses and trees. In the background, a highway and distant mountains are visible.

Los Angeles Valley College

Steinberg Architects
January 10, 2013

LAVC Construction Program Implementation Plan Update

January 10, 2013

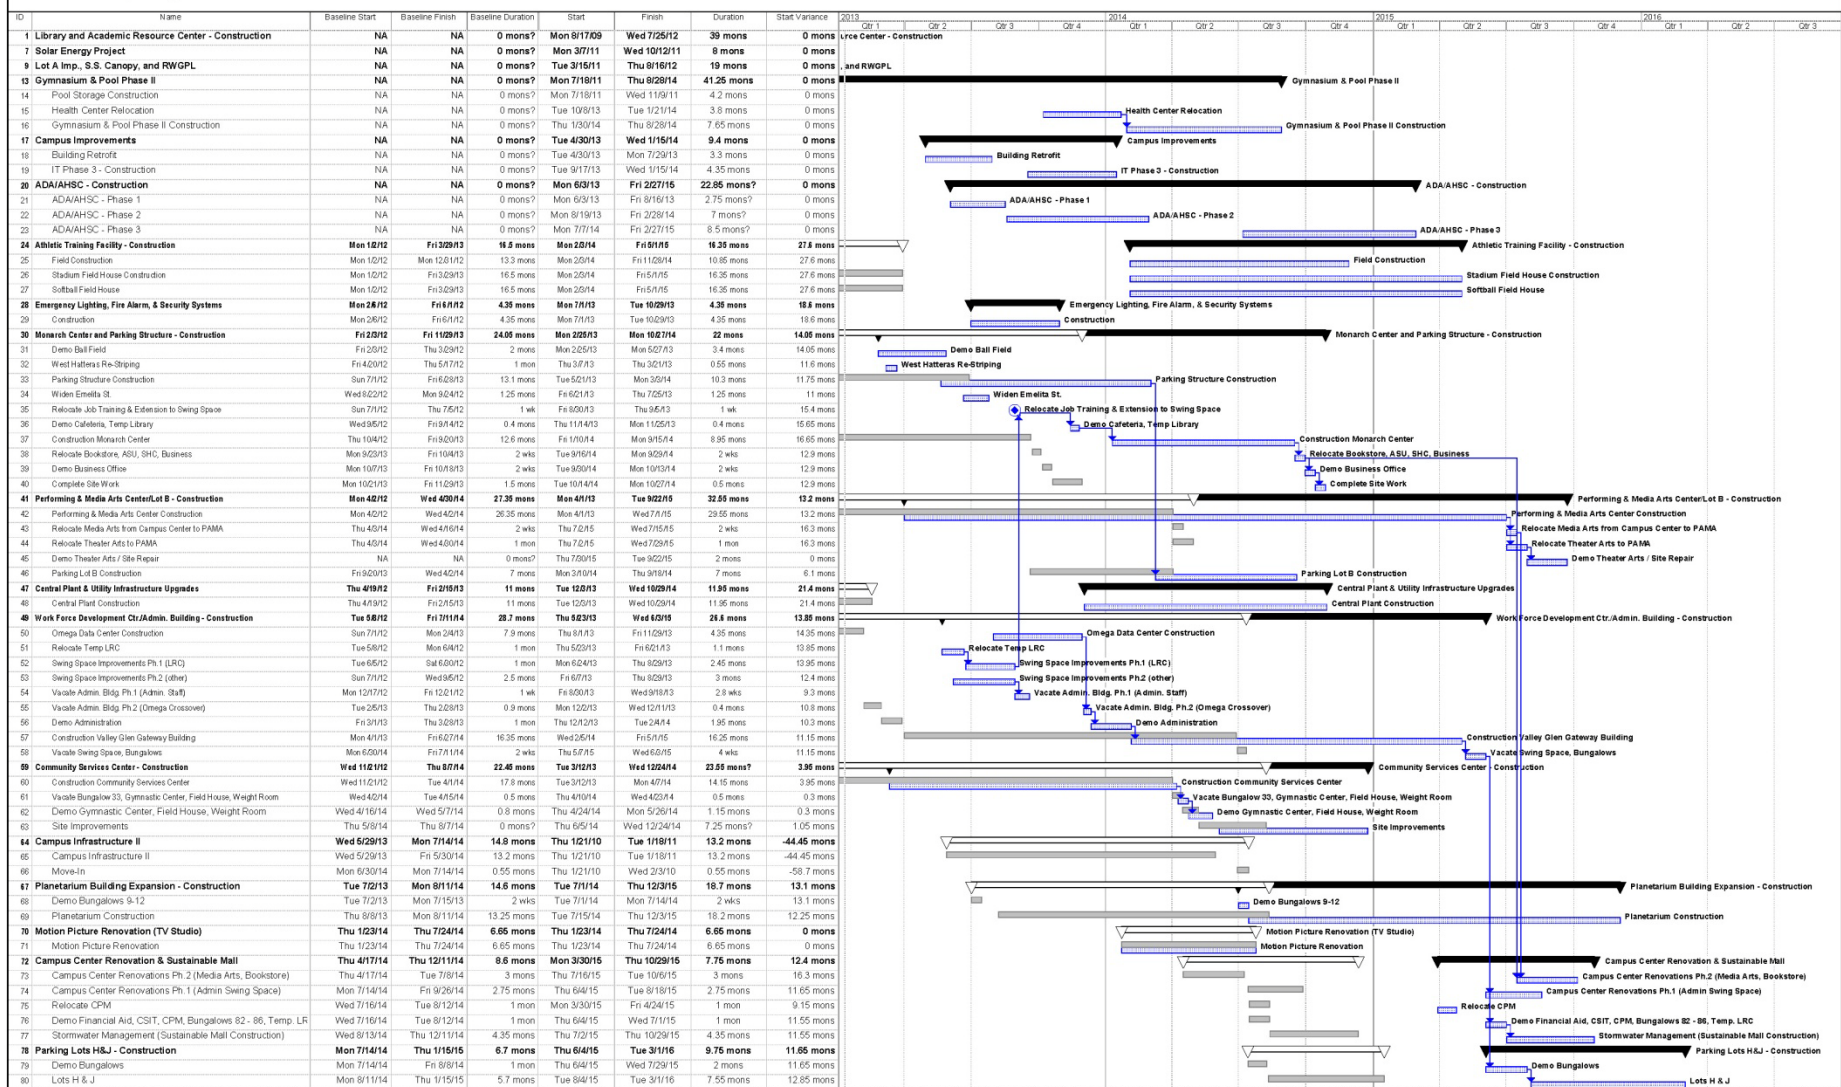


APR - MAY - JUN

Q2/2013

Project Status


- Demo Softball Field
- Parking Structure Construction Begins
- Community Services Center Construction Begins
- Learning Resource Center Relocation & Remodel Begins
- Swing Space Improvements Begins (not shown)
- ADA Upgrades & Allied Health Services Corrective Construction - Phase 1 Begins (not shown)
- Building Retrofit Project Construction Begins (not shown)

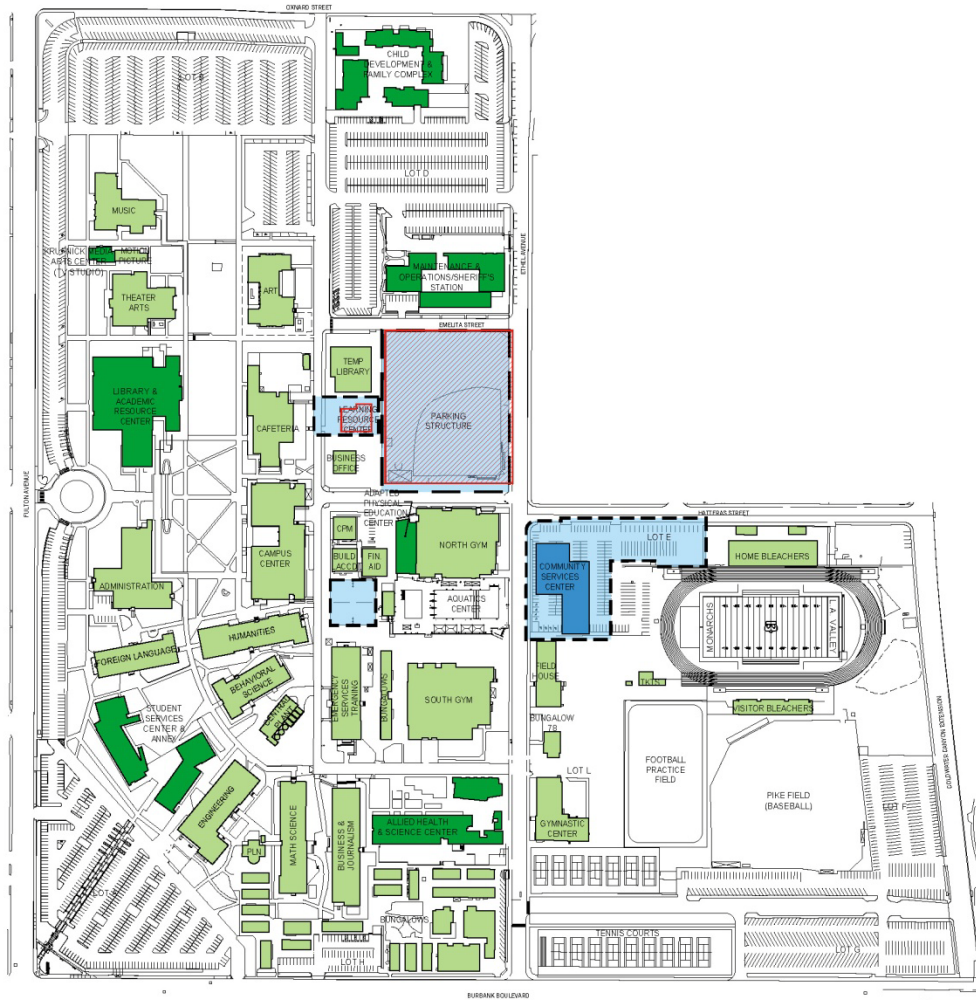

Legend

- Existing Building
- New Building / Major Renovation
- Area Under Construction
- Building To Be Demolished Or Relocated



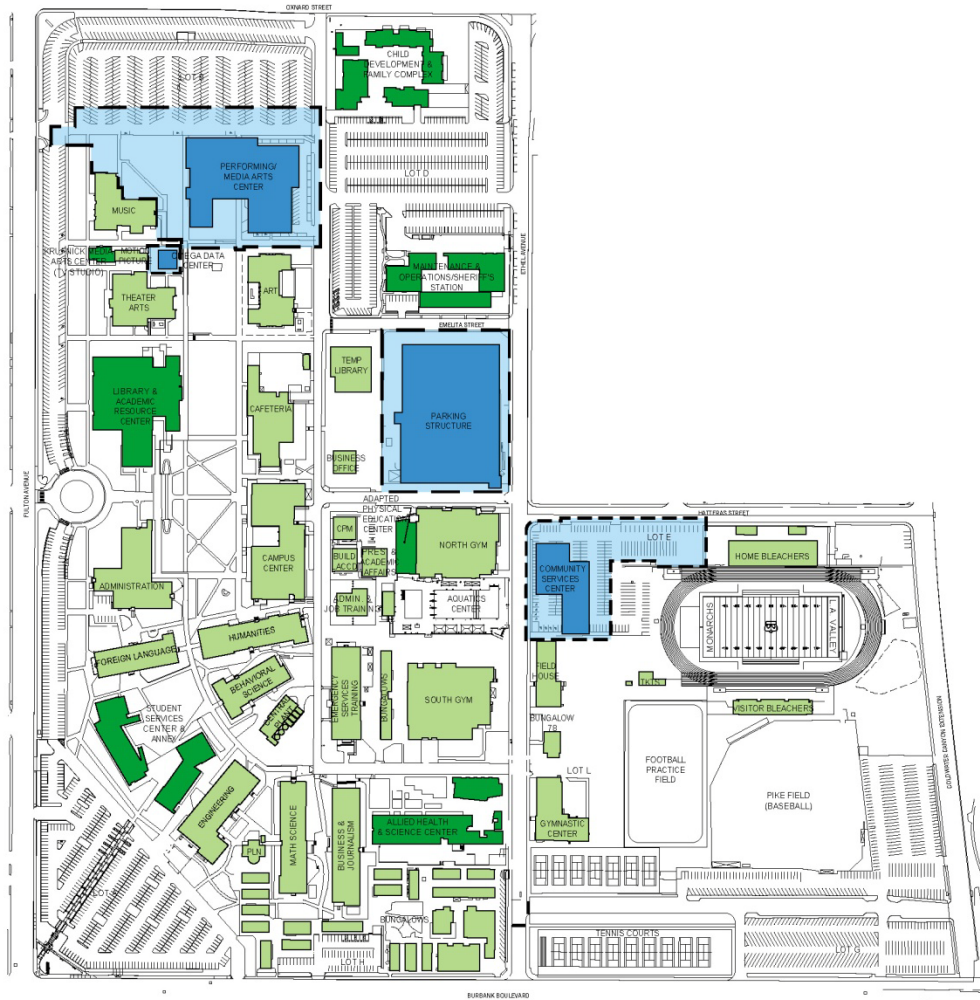

JUL - AUG - SEP

Q3/2013


Project Status

- Performing & Media Arts Center Construction Begins
- Omega Data Center Construction Begins
- ADA Upgrades & Allied Health Services Corrective Construction - Phase 2 Begins (not shown)
- Parking Structure Construction Ongoing
- Community Services Center Construction Ongoing
- Vacate Admin (not shown)
- Learning Resource Center Relocation & Remodel Completed
- Swing Space Improvements Completed (not shown)
- ADA Upgrades & Allied Health Services Corrective Construction - Phase 1 Completed (not shown)
- Building Retrofit Project Construction Completed (not shown)

Legend

- Existing Building
- New Building / Major Renovation
- Area Under Construction
- Building To Be Demolished Or Relocated



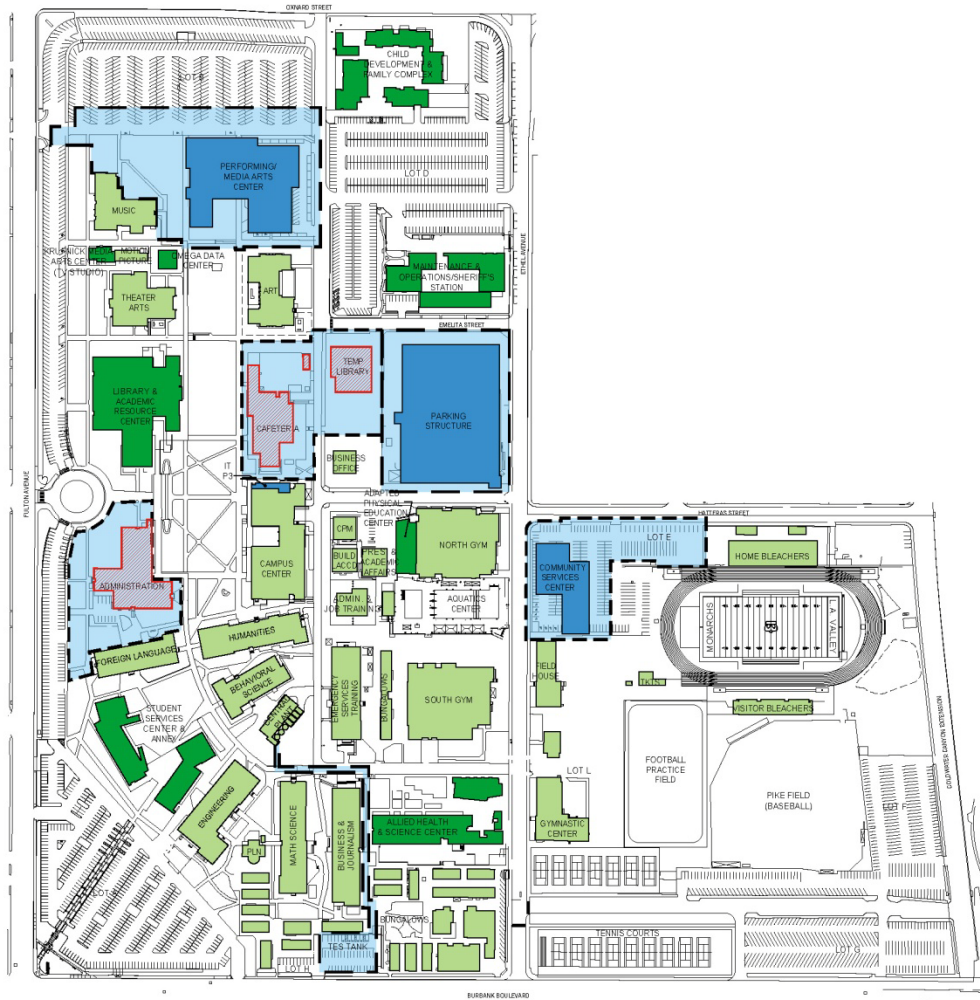

OCT - NOV - DEC

Q4/2013

Project Status

- Central Plant & Utility Infrastructure (TES Tank) Upgrades Construction Begins
- Student Health Center (SHC) Temporary Relocation Construction Begins (not shown)
- IT Phase 3 Construction Begins

- Demo Administration Building
- Demo Cafeteria
- Removal of Temporary Library

- Parking Structure Construction Ongoing

- Community Services Center Construction Ongoing
- Performing & Media Arts Center Construction Ongoing
- ADA Upgrades & Allied Health Services Corrective Construction - Phase 2 Ongoing (not shown)
- Omega Data Center Construction Completed

Legend

- Existing Building
- New Building / Major Renovation
- Area Under Construction
- Building To Be Demolished Or Relocated



Project Status

- Legend

-  Existing Building
-  New Building / Major Renovation
-  Area Under Construction
-  Building To Be Demolished Or Relocated



APR - MAY - JUN


Q2/2014

Project Status

- Demo Gymnastic Center/Weight Room, Field House, Bungalow 78, Lot L
- Performing & Media Arts Center Construction Ongoing
- Central Plant & Utility Infrastructure (TES Tank) Upgrades Constructin Ongoing
- Valley Glen Gateway Construction Ongoing
- Monarch Center Construction Ongoing
- Stadium Field House Construction Ongoing
- Softball Field House Construction Ongoing
- Athletic Training Facility Fields Construction Ongoing
- Parking Lot B Construction Ongoing
- Planetarium Expansion Construction Ongoing
- Motion Picture Renovation Construction Ongoing
- Gymnasium & Pool Phase II Construction Ongoing (not shown)
- Community Services Center Construction Completed

Legend

- Existing Building
- New Building / Major Renovation
- Area Under Construction
- Building To Be Demolished Or Relocated

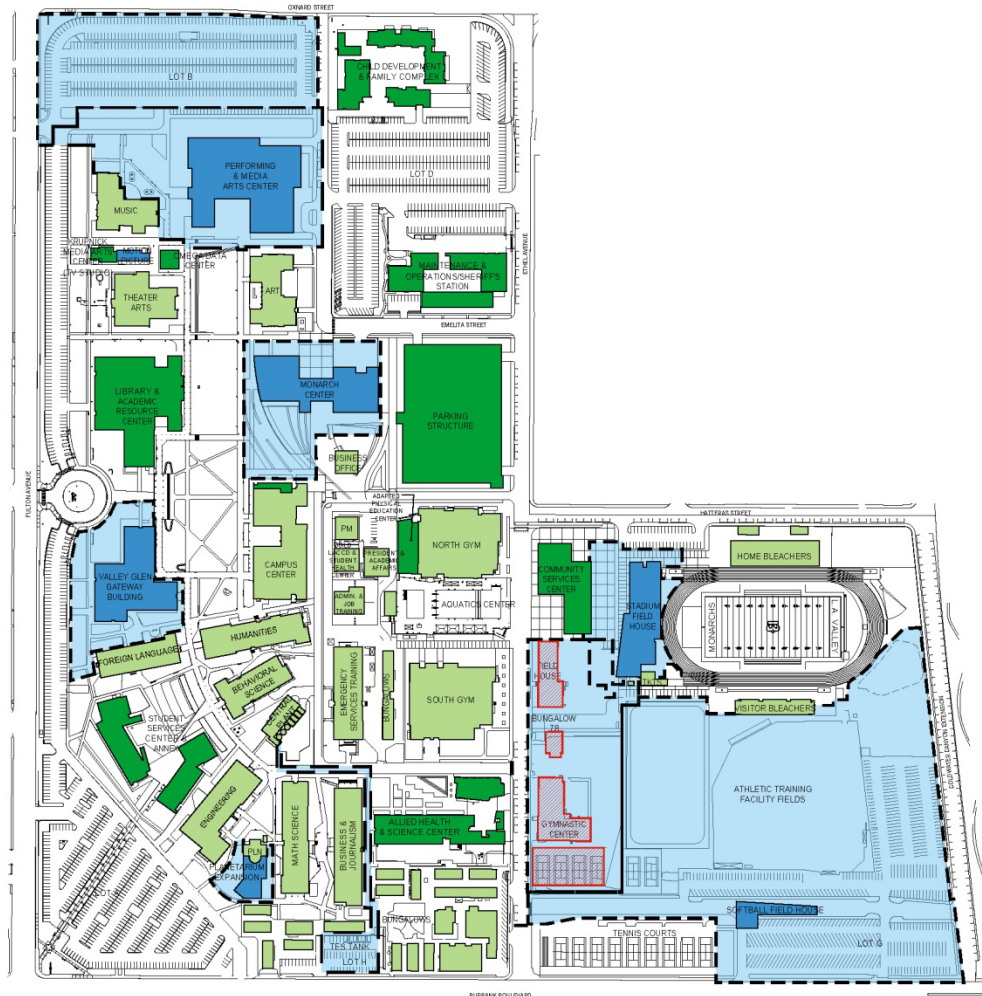

JUL - AUG - SEP


Q3/2014

Project Status

- Community Services Center Site Construction Begins
- ADA Upgrades - Phase 3 Begins (not shown)
- Performing & Media Arts Center Construction Ongoing
- Central Plant & Utility Infrastructure (TES Tank) Upgrades Construction Ongoing
- Valley Glen Gateway Construction Ongoing
- Monarch Center Construction Ongoing
- Stadium Field House Construction Ongoing
- Softball Field House Construction Ongoing
- Athletic Training Facility Fields Construction Ongoing
- Planetarium Expansion Construction Ongoing
- Parking Lot B Construction Completed
- Motion Picture Renovation Construction Completed
- Gymnasium & Pool Phase II Construction Completed (not shown)

Legend

- Existing Building
- New Building / Major Renovation
- Area Under Construction
- Building To Be Demolished Or Relocated

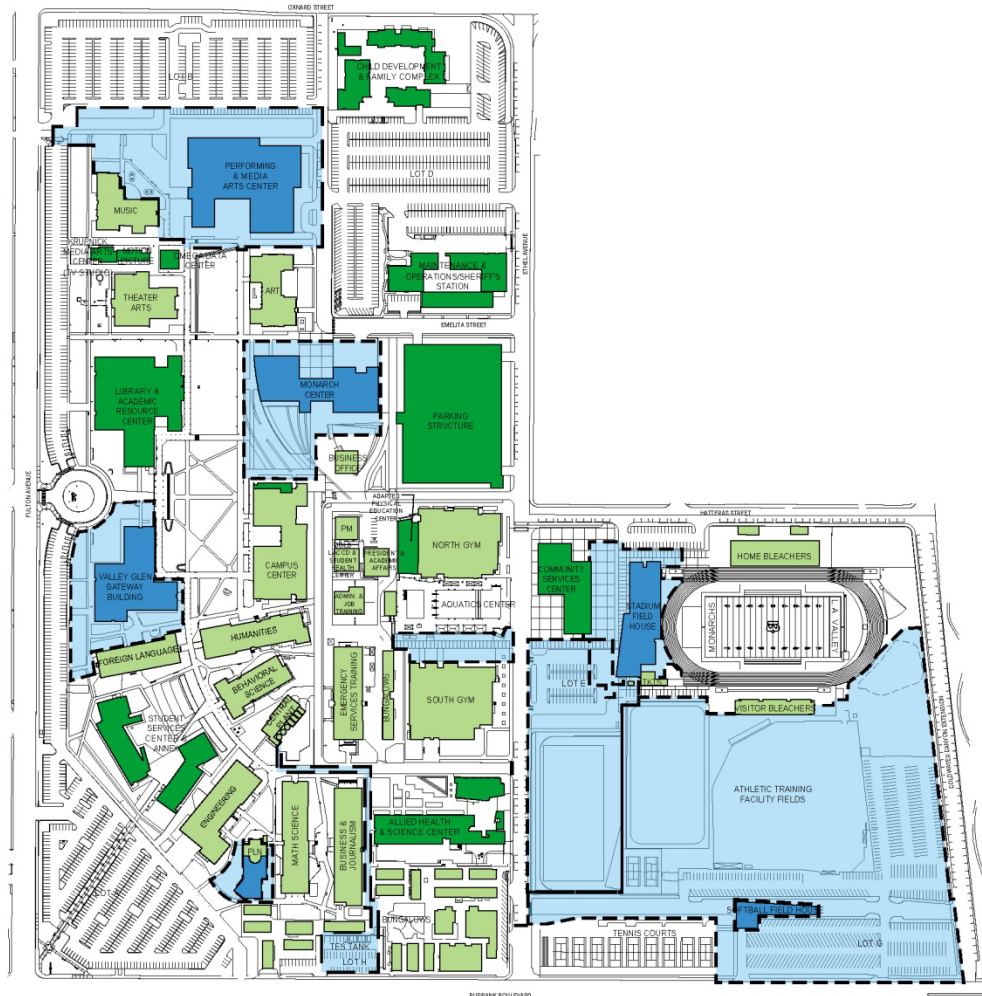


OCT - NOV - DEC

Q4/2014

Project Status

- Performing & Media Arts Center Construction Ongoing
- Valley Glen Gateway Building Construction Ongoing
- Monarch Center Construction Ongoing
- Stadium Field House Construction Ongoing
- Softball Field House Construction Ongoing
- Community Services Center Site Construction Ongoing
- ADA Upgrades - Phase 3 Ongoing (not shown)
- Central Plant & Utility Infrastructure (TES Tank) Upgrades Construction Completed (not shown)
- Athletic Training Facility Fields Construction Completed
- Planetarium Expansion Construction Completed

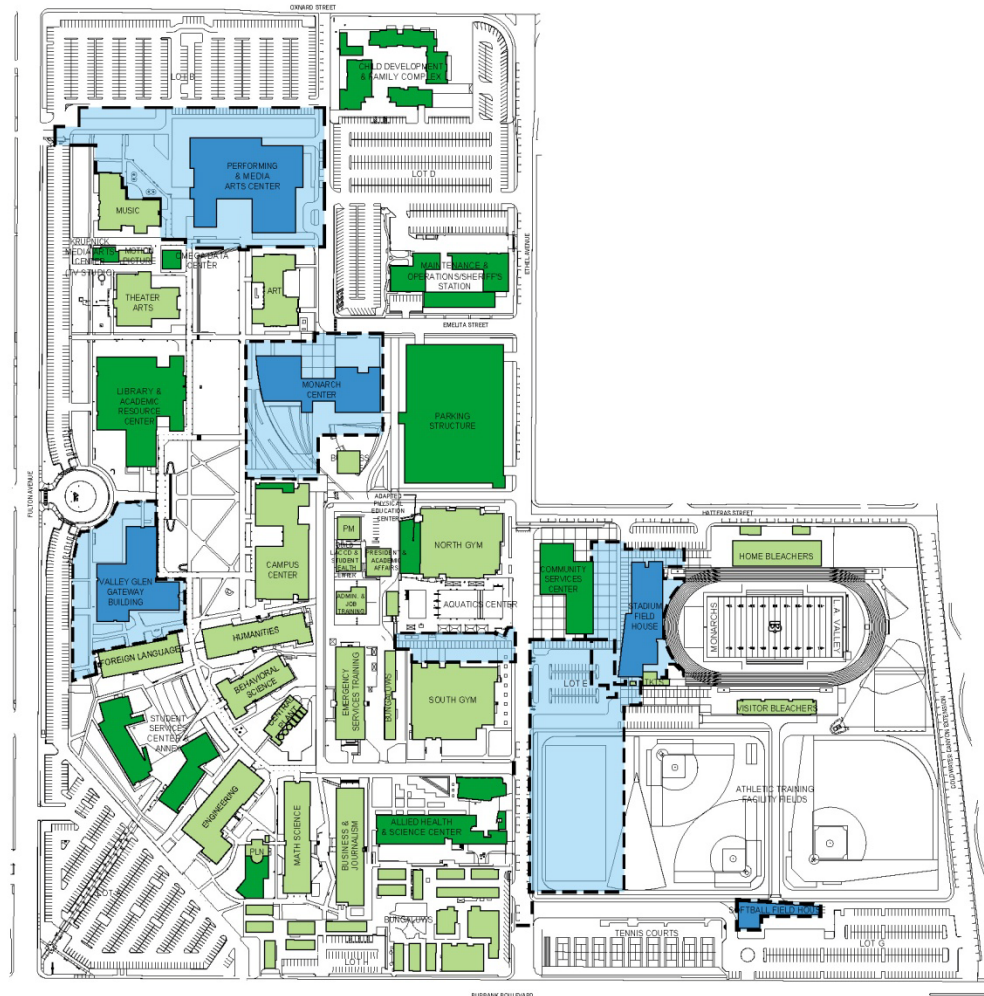

Legend

- Existing Building
- New Building / Major Renovation
- Area Under Construction
- Building To Be Demolished Or Relocated




JAN - FEB - MAR

Q1/2015

Project Status

- Demo Business Office
- Monarch Center Complete Site Improvements Begins
- Performing & Media Arts Center Construction Ongoing
- Valley Glen Gateway Building Construction Ongoing
- Stadium Field House Construction Ongoing
- Softball Field House Construction Ongoing
- Monarch Center Construction Completed
- Community Services Center Site Construction Completed
- ADA Upgrades - Phase 3 Ongoing (not shown)

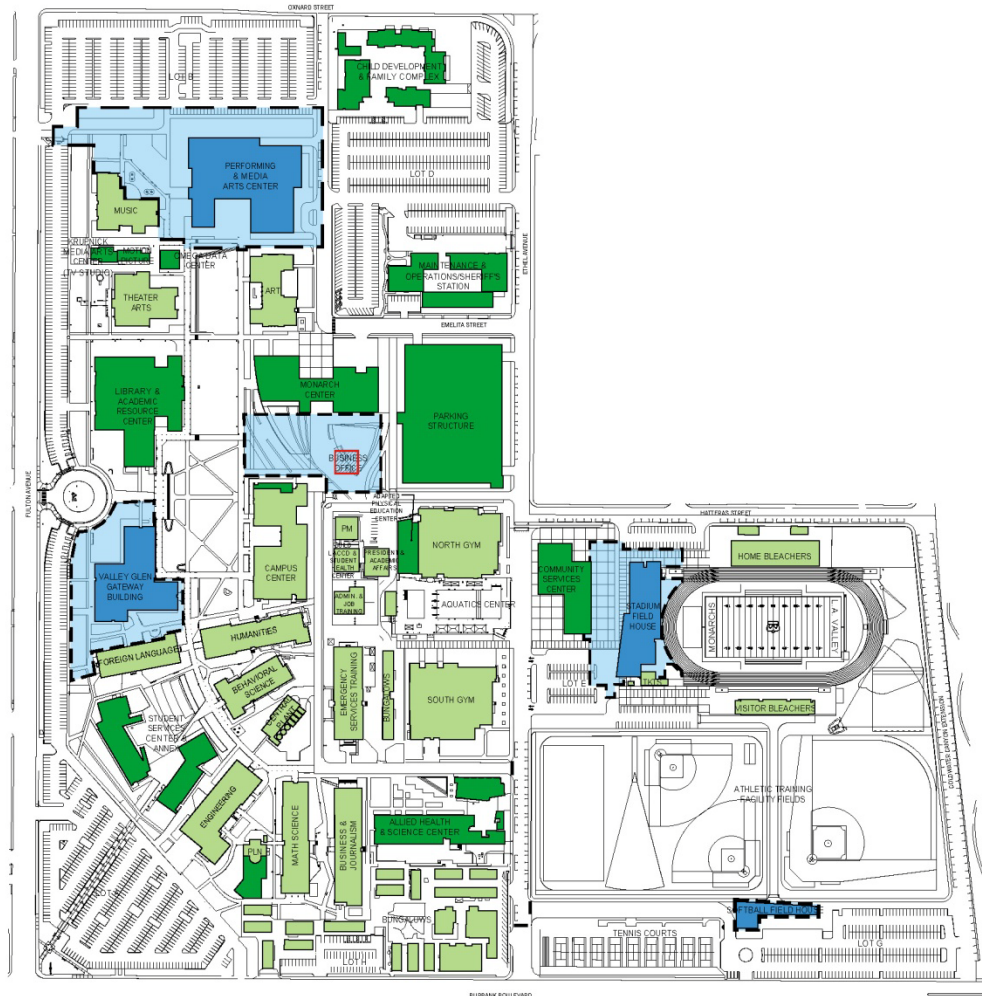

Legend

- Existing Building
- New Building / Major Renovation
- Area Under Construction
- Building To Be Demolished Or Relocated




APR - MAY - JUN

Q2/2015

Project Status

- Campus Center Renovations Ph.1 (Admin Swing Space) Begins
- Relocate CPM (not shown)
- Demo Bungalows Begins
- Demo Financial Aid, CSIT, CPM, Bungalows 82 - 86, Temp. LRC
- Performing & Media Arts Center Construction Ongoing
- Valley Glen Gateway Building Construction Completed
- Stadium Field House Construction Completed
- Softball Field House Construction Completed
- Monarch Center Site Improvements Completed

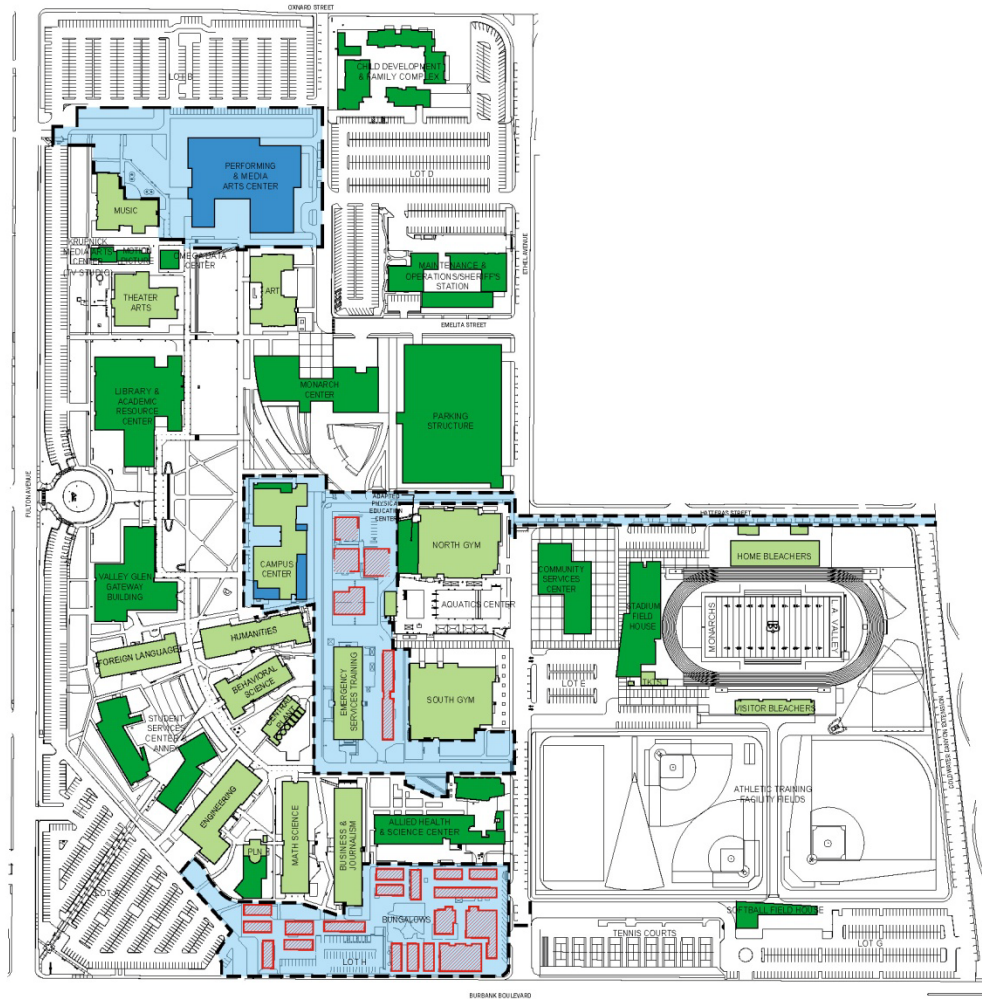

Legend

- Existing Building
- New Building / Major Renovation
- Area Under Construction
- Building To Be Demolished Or Relocated




JUL - AUG - SEP

Q3/2015

Project Status

- Campus Center Renovations Ph.2 (Media Arts, Bookstore) Begins
- Stormwater Management (Sustainable Mall) Construction Begins
- Parking Lots H & J Construction Begins
- Demo Theater Arts/Site Repair
- Performing & Media Arts Center Construction Completed
- Campus Center Renovations Ph.1 (Admin Swing Space) Completed

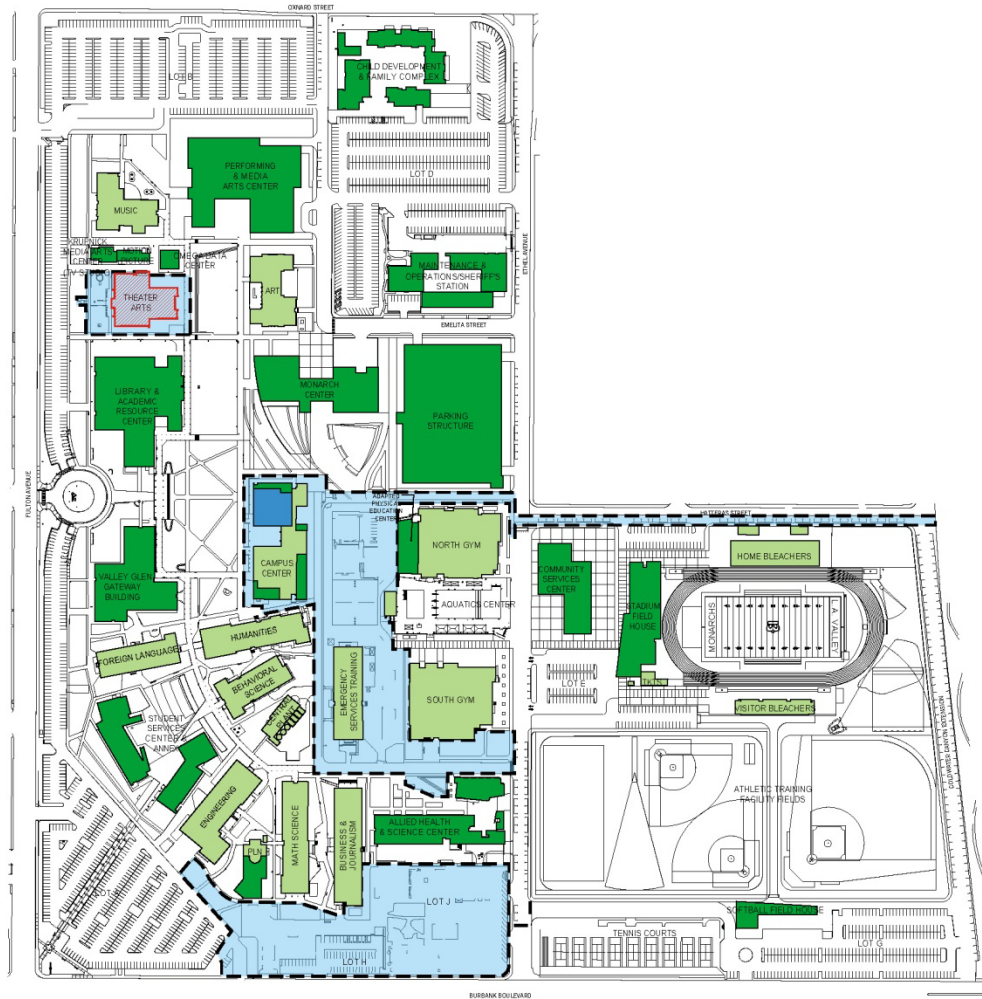

Legend

- Existing Building
- New Building / Major Renovation
- Area Under Construction
- Building To Be Demolished Or Relocated




OCT - NOV - DEC

Q4/2015

Project Status

- Parking Lots H & J Construction Ongoing
- Campus Center Renovations Ph.2 (Media Arts, Bookstore) Completed
- Stormwater Management (Sustainable Mall) Construction Completed

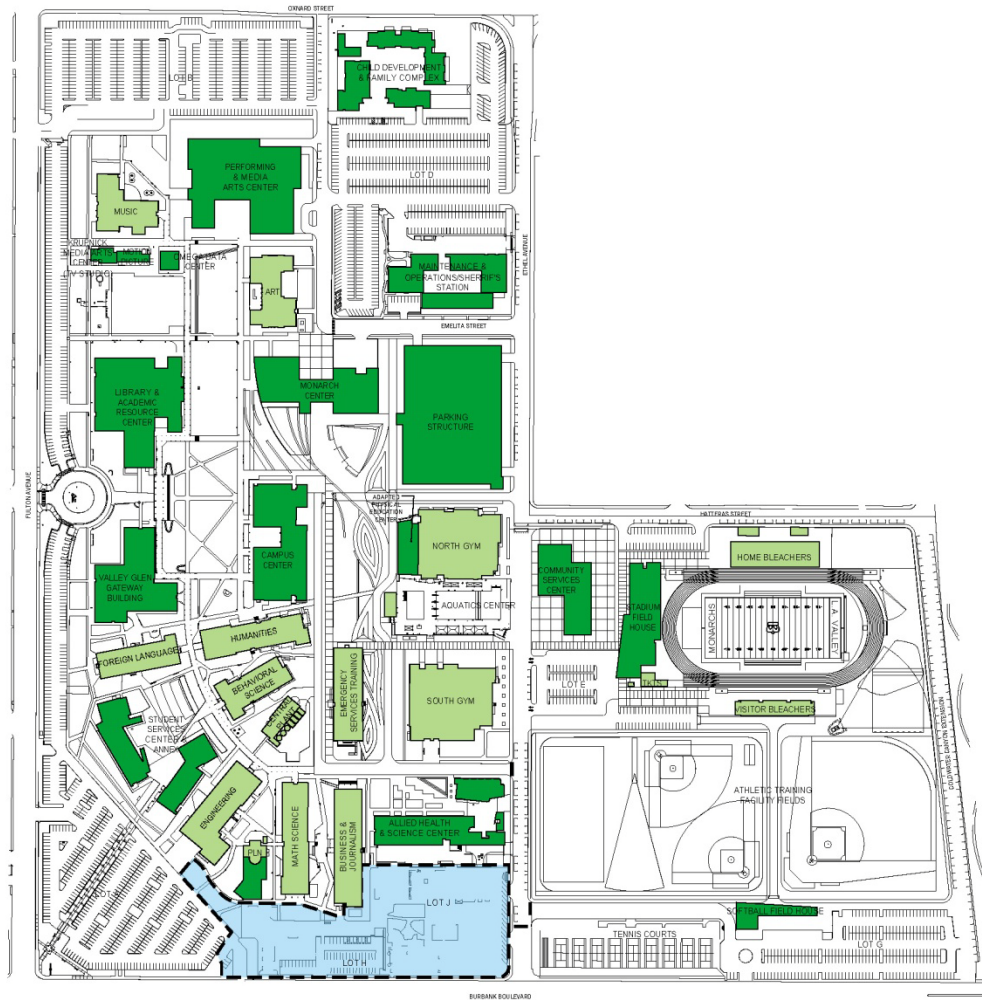

Legend

- Existing Building
- New Building / Major Renovation
- Area Under Construction
- Building To Be Demolished Or Relocated




JAN - FEB - MAR

Q1/2016

Project Status

- Parking Lots H & J Construction Completed

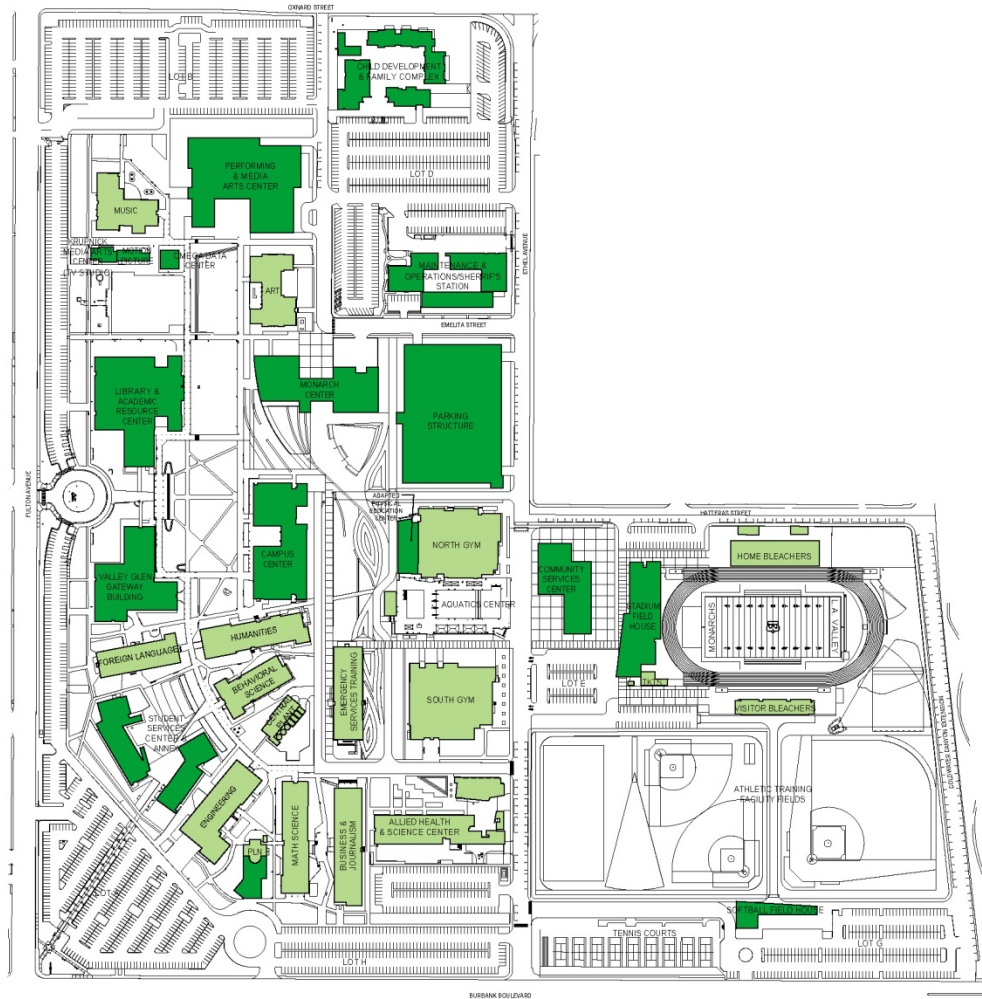

Legend

- Existing Building
- New Building / Major Renovation
- Area Under Construction
- Building To Be Demolished Or Relocated

